


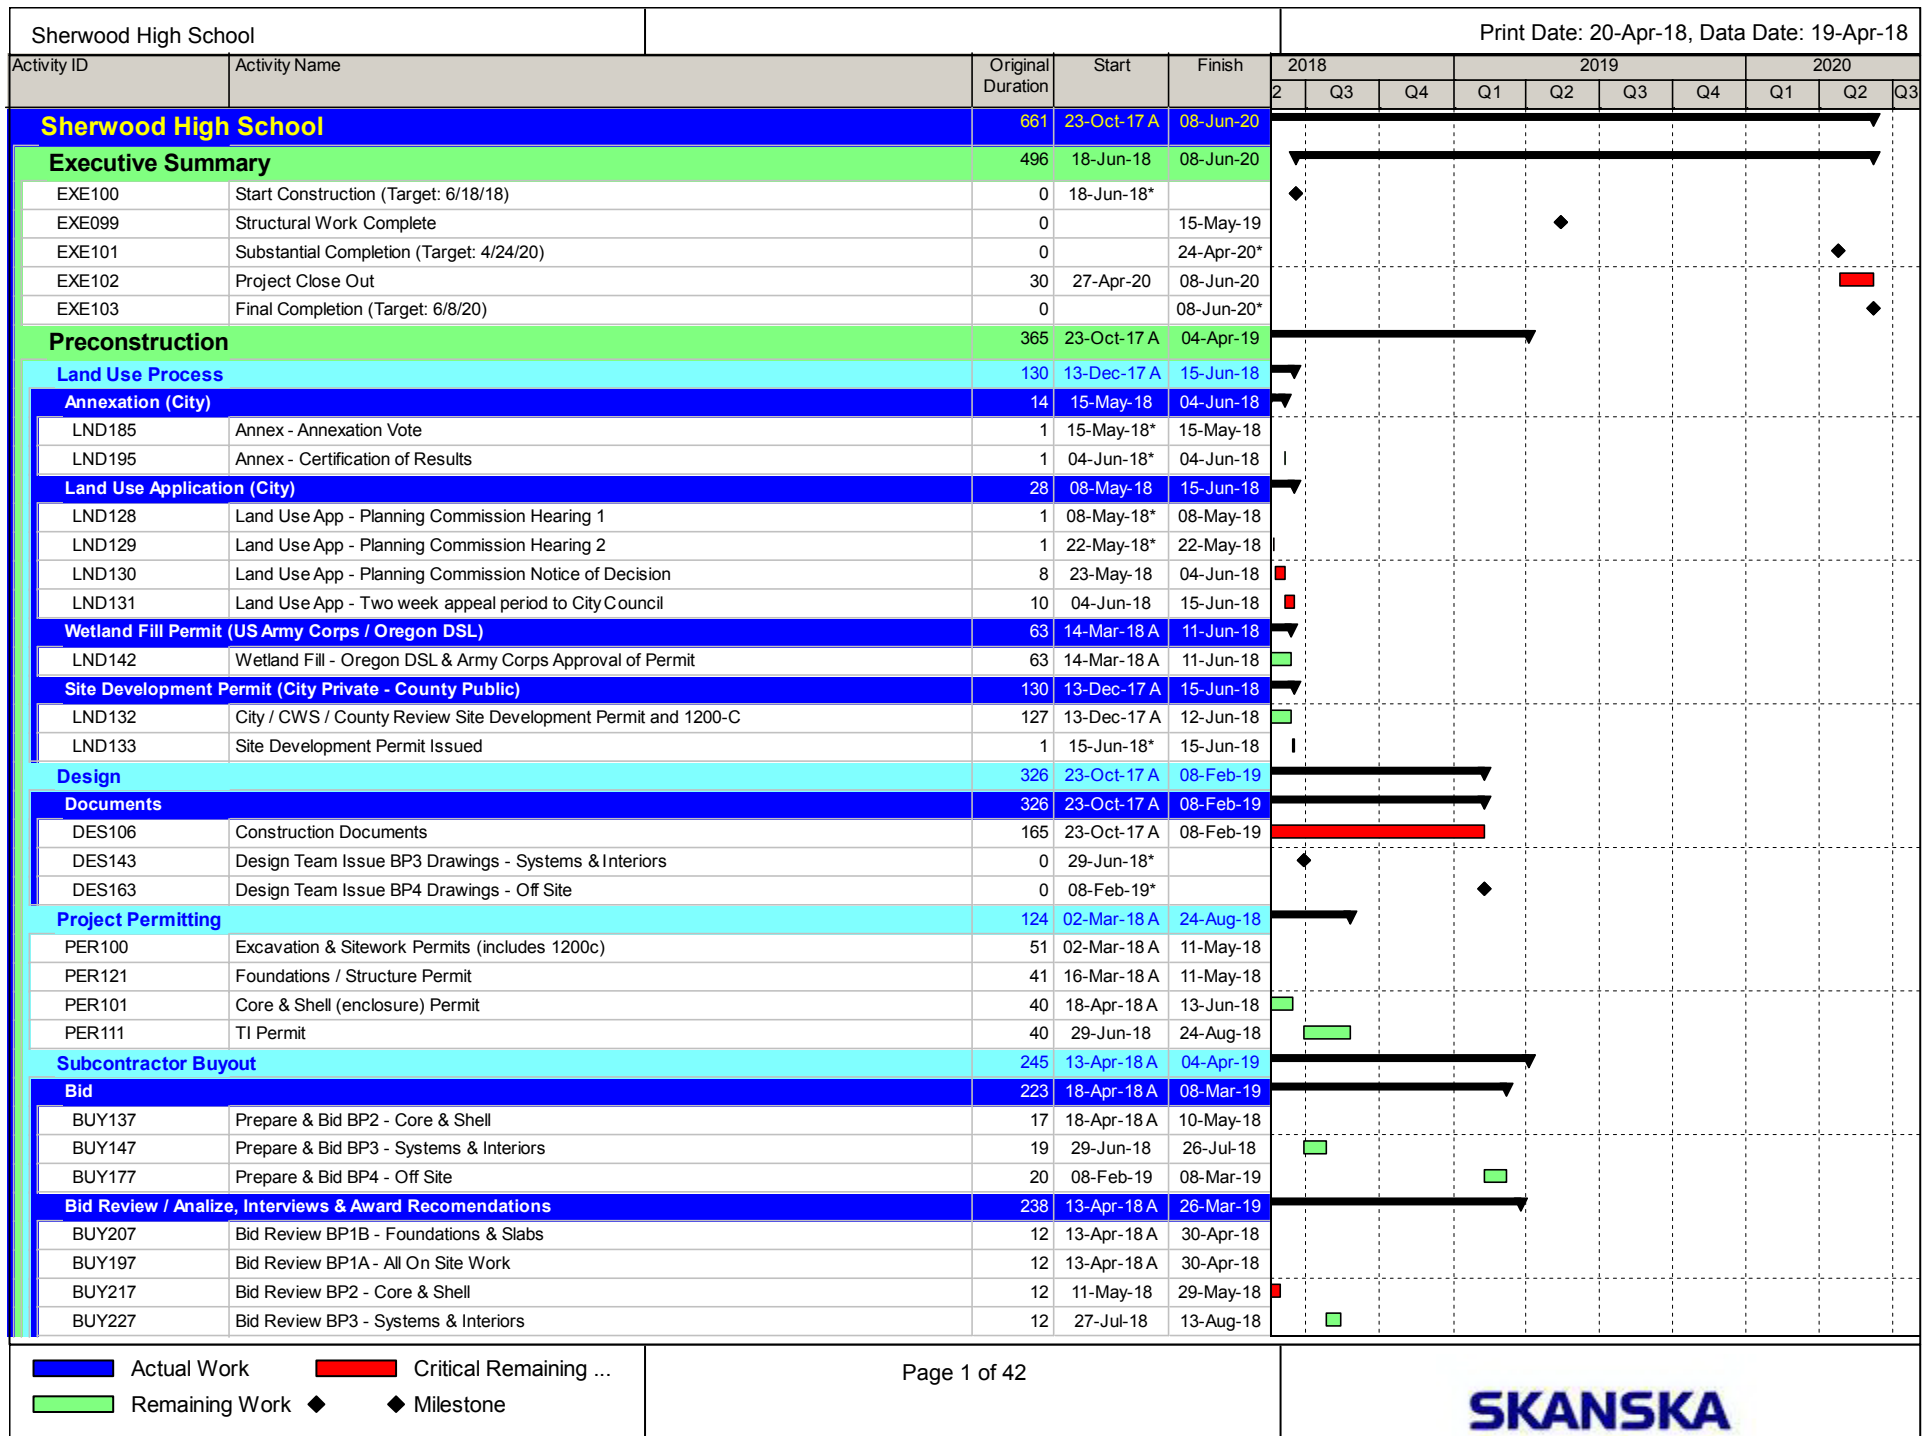

Sherwood High School						Print Date: 20-Apr-18, Data Date: 19-Apr-18								
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
BUY237	Bid Review BP4 - Off Site	12	11-Mar-19	26-Mar-19										
SSD Subcontractor Award Approval		228	01-May-18	28-Mar-19										
BUY239	SSD Award Approval BP1B - Foundations & Slabs	2	01-May-18	02-May-18										
BUY238	SSD Award Approval BP1A - All On Site Work	2	01-May-18	02-May-18										
BUY240	SSD Award Approval BP2 - Core & Shell	2	30-May-18	31-May-18										
BUY241	SSD Award Approval BP3 - Systems & Interiors	2	14-Aug-18	15-Aug-18										
BUY242	SSD Award Approval BP4 - Off Site	2	27-Mar-19	28-Mar-19										
Subcontract Issuance		231	03-May-18	04-Apr-19										
BUY127	Issue Subcontract(s) BP1B - Foundations & Slabs	5	03-May-18	09-May-18										
BUY104	Issue Subcontract(s) BP1A - All On Site Work	5	03-May-18	09-May-18										
BUY106	Issue Subcontract(s) BP2 - Exterior Enclosure	5	01-Jun-18	07-Jun-18										
BUY105	Issue Subcontract(s) BP2 - Structure	6	01-Jun-18	08-Jun-18										
BUY107	Issue Subcontract(s) BP3 - Interiors	5	23-Aug-18	29-Aug-18										
BUY187	Issue Subcontract(s) BP4 - Off Site	5	29-Mar-19	04-Apr-19										
Critical Material & Equipment Procurement		199	10-May-18	26-Feb-19										
PRO103	Submit / Fab / Deliver - Interior Long Leads	70	17-Aug-18	28-Nov-18										
Submittals		159	10-May-18	27-Dec-18										
From Subcontractor		139	10-May-18	28-Nov-18										
BP1		40	10-May-18	06-Jul-18										
PRO104	From Sub - BP1 - Concrete Reinforcing - Foundations	30	10-May-18	21-Jun-18										
PRO105	From Sub - BP1 - Concrete Reinforcing - Site Concrete	15	10-May-18	31-May-18										
PRO106	From Sub - BP1 - Structural Steel Shops - Anchor Bolts	15	10-May-18	31-May-18										
PRO107	From Sub - BP1 - Fire Sprinkler Shops - UG Piping	15	10-May-18	31-May-18										
PRO108	From Sub - BP1 - Fire Sprinkler - UG Materials & Equipment	20	10-May-18	07-Jun-18										
PRO109	From Sub - BP1 - Plumbing Shops - UG Piping	15	10-May-18	31-May-18										
PRO110	From Sub - BP1 - Plumbing - UG Materials & Equipment	15	10-May-18	31-May-18										
PRO111	From Sub - BP1 - HVAC - UG Piping / Duct	15	10-May-18	31-May-18										
PRO112	From Sub - BP1 - HVAC - UG Materials & Equipment	20	10-May-18	07-Jun-18										
PRO113	From Sub - BP1 - Electrical - UG Materials	15	10-May-18	31-May-18										
PRO114	From Sub - BP1 - Electrical - Sports Field Lighting	40	10-May-18	06-Jul-18										
PRO115	From Sub - BP1 - Civil - Lock & Load Retaining Wall Materials	15	10-May-18	31-May-18										
PRO116	From Sub - BP1 - Landscaping - Irrigation Materials & Equipment	30	10-May-18	21-Jun-18										
BP2		119	08-Jun-18	28-Nov-18										
PRO2256	From Sub - BP2 - HM Frame Shops - Core & Shell	20	08-Jun-18	06-Jul-18										
PRO2296	From Sub - BP2 - Brick Veneer	30	08-Jun-18	20-Jul-18										
PRO2336	From Sub - BP2 - Metal Panels	30	08-Jun-18	20-Jul-18										
PRO2376	From Sub - BP2 - Storefront & Curtain Wall	30	08-Jun-18	20-Jul-18										
PRO2416	From Sub - BP2 - Glazing	25	08-Jun-18	13-Jul-18										
PRO516	From Sub - BP2 - Concrete Reinforcing - Elevated Slabs - Sector A	30	11-Jun-18	23-Jul-18										
PRO556	From Sub - BP2 - Concrete Reinforcing - Elevated Slabs - Sector E	30	11-Jun-18	23-Jul-18										
PRO596	From Sub - BP2 - Concrete Reinforcing - Elevated Slabs - Sector B	30	11-Jun-18	23-Jul-18										
PRO636	From Sub - BP2 - Concrete Reinforcing - Elevated Slabs - Sector D	30	11-Jun-18	23-Jul-18										
PRO716	From Sub - BP2 - Concrete Reinforcing - Elevated Slabs - Sector F	30	11-Jun-18	23-Jul-18										

■ Actual Work
 ■ Critical Remaining ...
 ■ Remaining Work
 ◆ Milestone

Sherwood High School						Print Date: 20-Apr-18, Data Date: 19-Apr-18								
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
PRO136	Skanska Review - BP1 - Concrete Reinforcing - Site Concrete	5	01-Jun-18	07-Jun-18	█									
PRO146	Skanska Review - BP1 - Structural Steel Shops - Anchor Bolts	5	01-Jun-18	07-Jun-18	█									
PRO156	Skanska Review - BP1 - Fire Sprinkler Shops - UG Piping	5	01-Jun-18	07-Jun-18	█									
PRO176	Skanska Review - BP1 - Plumbing Shops - UG Piping	5	01-Jun-18	07-Jun-18	█									
PRO186	Skanska Review - BP1 - Plumbing - UG Materials & Equipment	5	01-Jun-18	07-Jun-18	█									
PRO196	Skanska Review - BP1 - HVAC - UG Piping / Duct	5	01-Jun-18	07-Jun-18	█									
PRO216	Skanska Review - BP1 - Electrical - UG Materials	5	01-Jun-18	07-Jun-18	█									
PRO236	Skanska Review - BP1 - Civil - Lock & Load Retaining Wall Materials	5	01-Jun-18	07-Jun-18	█									
PRO166	Skanska Review - BP1 - Fire Sprinkler - UG Materials & Equipment	5	08-Jun-18	14-Jun-18	█									
PRO206	Skanska Review - BP1 - HVAC - UG Materials & Equipment	5	08-Jun-18	14-Jun-18	█									
PRO126	Skanska Review - BP1 - Concrete Reinforcing - Foundations	5	22-Jun-18	28-Jun-18	█									
PRO246	Skanska Review - BP1 - Landscaping - Irrigation Materials & Equipment	5	22-Jun-18	28-Jun-18	█									
PRO226	Skanska Review - BP1 - Electrical - Sports Field Lighting	5	09-Jul-18	13-Jul-18	█									
BP2		104	09-Jul-18	05-Dec-18	←									
PRO2266	Skanska Review - BP2 - HM Frame Shops - Core & Shell	5	09-Jul-18	13-Jul-18	█									
PRO876	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector A	5	10-Jul-18	16-Jul-18	█									
PRO1236	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector B	5	10-Jul-18	16-Jul-18	█									
PRO2546	Skanska Review - BP2 - Gym Equipment	5	10-Jul-18	16-Jul-18	█									
PRO2426	Skanska Review - BP2 - Glazing	5	16-Jul-18	20-Jul-18	█									
PRO1156	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector A	5	23-Jul-18	27-Jul-18	█									
PRO2306	Skanska Review - BP2 - Brick Veneer	5	23-Jul-18	27-Jul-18	█									
PRO2346	Skanska Review - BP2 - Metal Panels	5	23-Jul-18	27-Jul-18	█									
PRO2386	Skanska Review - BP2 - Storefront & Curtain Wall	5	23-Jul-18	27-Jul-18	█									
PRO526	Skanska Review - BP2 - Concrete Reinforcing - Elevated Slabs - Sector A	5	24-Jul-18	30-Jul-18	█									
PRO566	Skanska Review - BP2 - Concrete Reinforcing - Elevated Slabs - Sector E	5	24-Jul-18	30-Jul-18	█									
PRO606	Skanska Review - BP2 - Concrete Reinforcing - Elevated Slabs - Sector B	5	24-Jul-18	30-Jul-18	█									
PRO646	Skanska Review - BP2 - Concrete Reinforcing - Elevated Slabs - Sector D	5	24-Jul-18	30-Jul-18	█									
PRO726	Skanska Review - BP2 - Concrete Reinforcing - Elevated Slabs - Sector F	5	24-Jul-18	30-Jul-18	█									
PRO766	Skanska Review - BP2 - Concrete Reinforcing - Elevated Slabs - Sector G&J	5	24-Jul-18	30-Jul-18	█									
PRO956	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector B	5	24-Jul-18	30-Jul-18	█									
PRO1746	Skanska Review - BP2 - Steel Decking Shops - Sector A	5	24-Jul-18	30-Jul-18	█									
PRO1196	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector E	5	06-Aug-18	10-Aug-18	█									
PRO916	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector E	5	07-Aug-18	13-Aug-18	█									
PRO1786	Skanska Review - BP2 - Steel Decking Shops - Sector E	5	07-Aug-18	13-Aug-18	█									
PRO2026	Skanska Review - BP2 - Metal Stairs Shops - Sector A	5	07-Aug-18	13-Aug-18	█									
PRO1276	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector D	5	20-Aug-18	24-Aug-18	█									
PRO996	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector D	5	21-Aug-18	27-Aug-18	█									
PRO1716	Skanska Review - BP2 - Steel Joist Framing Calcs	5	21-Aug-18	27-Aug-18	█									
PRO1826	Skanska Review - BP2 - Steel Decking Shops - Sector B	5	21-Aug-18	27-Aug-18	█									
PRO2066	Skanska Review - BP2 - Metal Stairs Shops - Sector E	5	21-Aug-18	27-Aug-18	█									
PRO2466	Skanska Review - BP2 - Elevator	5	21-Aug-18	27-Aug-18	█									
PRO1436	Skanska Review - BP2 - Steel Joist Framing Shops - Sector A	5	31-Aug-18	07-Sep-18	█									
PRO1396	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector G&J	5	04-Sep-18	10-Sep-18	█									

█ Actual Work █ Critical Remaining ...
█ Remaining Work ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
PRO1116	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector G&J	5	05-Sep-18	11-Sep-18										
PRO1866	Skanska Review - BP2 - Steel Decking Shops - Sector D	5	05-Sep-18	11-Sep-18										
PRO2106	Skanska Review - BP2 - Metal Stairs Shops - Sector B	5	05-Sep-18	11-Sep-18										
PRO2506	Skanska Review - BP2 - CMU Masonry	5	12-Sep-18	18-Sep-18										
PRO1476	Skanska Review - BP2 - Steel Joist Framing Shops - Sector E	5	17-Sep-18	21-Sep-18										
PRO806	Skanska Review - BP2 - Concrete Tilt Up Shops - Sector A&B	5	18-Sep-18	24-Sep-18										
PRO1356	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector F	5	18-Sep-18	24-Sep-18										
PRO1076	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector F	5	19-Sep-18	25-Sep-18										
PRO1946	Skanska Review - BP2 - Steel Decking Shops - Sector F	5	19-Sep-18	25-Sep-18										
PRO2146	Skanska Review - BP2 - Metal Stairs Shops - Sector D	5	19-Sep-18	25-Sep-18										
PRO1516	Skanska Review - BP2 - Steel Joist Framing Shops - Sector B	5	01-Oct-18	05-Oct-18										
PRO1316	Skanska Review - BP2 - Structural Steel Shops - Framing - Sector H	5	02-Oct-18	09-Oct-18										
PRO1036	Skanska Review - BP2 - Structural Steel Shops - Embeds - Sector H	5	03-Oct-18	10-Oct-18										
PRO1986	Skanska Review - BP2 - Steel Decking Shops - Sector G&J	5	03-Oct-18	10-Oct-18										
PRO2186	Skanska Review - BP2 - Metal Stairs Shops - Sector F	5	03-Oct-18	10-Oct-18										
PRO1556	Skanska Review - BP2 - Steel Joist Framing Shops - Sector D	5	16-Oct-18	22-Oct-18										
PRO1906	Skanska Review - BP2 - Steel Decking Shops - Sector H	5	18-Oct-18	24-Oct-18										
PRO2226	Skanska Review - BP2 - Metal Stairs Shops - Sector G&J	5	18-Oct-18	24-Oct-18										
PRO1636	Skanska Review - BP2 - Steel Joist Framing Shops - Sector F	5	30-Oct-18	05-Nov-18										
PRO846	Skanska Review - BP2 - Concrete Tilt Up Shops - Sector G&J	5	31-Oct-18	06-Nov-18										
PRO1676	Skanska Review - BP2 - Steel Joist Framing Shops - Sector G&J	5	13-Nov-18	19-Nov-18										
PRO1596	Skanska Review - BP2 - Steel Joist Framing Shops - Sector H	5	29-Nov-18	05-Dec-18										
Architect / Engineer Review & Approval		139	08-Jun-18	27-Dec-18										
BP1		40	08-Jun-18	03-Aug-18										
PRO266	A/E Review & Approval - BP1 - Concrete Reinforcing - Site Concrete	15	08-Jun-18	28-Jun-18										
PRO276	A/E Review & Approval - BP1 - Structural Steel Shops - Anchor Bolts	15	08-Jun-18	28-Jun-18										
PRO286	A/E Review & Approval - BP1 - Fire Sprinkler Shops - UG Piping	15	08-Jun-18	28-Jun-18										
PRO306	A/E Review & Approval - BP1 - Plumbing Shops - UG Piping	15	08-Jun-18	28-Jun-18										
PRO316	A/E Review & Approval - BP1 - Plumbing - UG Materials & Equipment	15	08-Jun-18	28-Jun-18										
PRO326	A/E Review & Approval - BP1 - HVAC - UG Piping / Duct	15	08-Jun-18	28-Jun-18										
PRO346	A/E Review & Approval - BP1 - Electrical - UG Materials	15	08-Jun-18	28-Jun-18										
PRO366	A/E Review & Approval - BP1 - Civil - Lock & Load Retaining Wall Materials	15	08-Jun-18	28-Jun-18										
PRO296	A/E Review & Approval - BP1 - Fire Sprinkler - UG Materials & Equipment	15	15-Jun-18	06-Jul-18										
PRO336	A/E Review & Approval - BP1 - HVAC - UG Materials & Equipment	15	15-Jun-18	06-Jul-18										
PRO256	A/E Review & Approval - BP1 - Concrete Reinforcing - Foundations	15	29-Jun-18	20-Jul-18										
PRO376	A/E Review & Approval - BP1 - Landscaping - Irrigation Materials & Equipment	15	29-Jun-18	20-Jul-18										
PRO356	A/E Review & Approval - BP1 - Electrical - Sports Field Lighting	15	16-Jul-18	03-Aug-18										
BP2		114	16-Jul-18	27-Dec-18										
PRO2276	A/E Review & Approval - BP2 - HM Frame Shops - Core & Shell	15	16-Jul-18	03-Aug-18										
PRO886	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector A	15	17-Jul-18	06-Aug-18										
PRO1246	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector B	15	17-Jul-18	06-Aug-18										
PRO2556	A/E Review & Approval - BP2 - Gym Equipment	15	17-Jul-18	06-Aug-18										
PRO2436	A/E Review & Approval - BP2 - Glazing	15	23-Jul-18	10-Aug-18										

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
PRO1166	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector A	15	30-Jul-18	17-Aug-18		■								
PRO2316	A/E Review & Approval - BP2 - Brick Veneer	15	30-Jul-18	17-Aug-18		■								
PRO2356	A/E Review & Approval - BP2 - Metal Panels	15	30-Jul-18	17-Aug-18		■								
PRO2396	A/E Review & Approval - BP2 - Storefront & Curtain Wall	15	30-Jul-18	17-Aug-18		■								
PRO536	A/E Review & Approval - BP2 - Concrete Reinforcing - Elevated Slabs - Sector A	15	31-Jul-18	20-Aug-18		■								
PRO576	A/E Review & Approval - BP2 - Concrete Reinforcing - Elevated Slabs - Sector E	15	31-Jul-18	20-Aug-18		■								
PRO616	A/E Review & Approval - BP2 - Concrete Reinforcing - Elevated Slabs - Sector B	15	31-Jul-18	20-Aug-18		■								
PRO656	A/E Review & Approval - BP2 - Concrete Reinforcing - Elevated Slabs - Sector D	15	31-Jul-18	20-Aug-18		■								
PRO736	A/E Review & Approval - BP2 - Concrete Reinforcing - Elevated Slabs - Sector F	15	31-Jul-18	20-Aug-18		■								
PRO776	A/E Review & Approval - BP2 - Concrete Reinforcing - Elevated Slabs - Sector G&J	15	31-Jul-18	20-Aug-18		■								
PRO966	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector B	15	31-Jul-18	20-Aug-18		■								
PRO1756	A/E Review & Approval - BP2 - Steel Decking Shops - Sector A	15	31-Jul-18	20-Aug-18		■								
PRO1206	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector E	15	13-Aug-18	31-Aug-18		■								
PRO926	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector E	15	14-Aug-18	04-Sep-18		■								
PRO1796	A/E Review & Approval - BP2 - Steel Decking Shops - Sector E	15	14-Aug-18	04-Sep-18		■								
PRO2036	A/E Review & Approval - BP2 - Metal Stairs Shops - Sector A	15	14-Aug-18	04-Sep-18		■								
PRO1286	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector D	15	27-Aug-18	17-Sep-18		■								
PRO1006	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector D	15	28-Aug-18	18-Sep-18		■								
PRO1726	A/E Review & Approval BP2 - Steel Joist Framing Calcs	15	28-Aug-18	18-Sep-18		■								
PRO1836	A/E Review & Approval - BP2 - Steel Decking Shops - Sector B	15	28-Aug-18	18-Sep-18		■								
PRO2076	A/E Review & Approval - BP2 - Metal Stairs Shops - Sector E	15	28-Aug-18	18-Sep-18		■								
PRO2476	A/E Review & Approval - BP2 - Elevator	15	28-Aug-18	18-Sep-18		■								
PRO1446	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector A	15	10-Sep-18	28-Sep-18		■								
PRO1406	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector G&J	15	11-Sep-18	01-Oct-18		■								
PRO1126	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector G&J	15	12-Sep-18	02-Oct-18		■								
PRO1876	A/E Review & Approval - BP2 - Steel Decking Shops - Sector D	15	12-Sep-18	02-Oct-18		■								
PRO2116	A/E Review & Approval - BP2 - Metal Stairs Shops - Sector B	15	12-Sep-18	02-Oct-18		■								
PRO2516	A/E Review & Approval - BP2 - CMU Masonry	15	19-Sep-18	10-Oct-18		■								
PRO1486	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector E	15	24-Sep-18	15-Oct-18		■								
PRO816	A/E Review & Approval - BP2 - Concrete Tilt Up Shops - Sector A&B	15	25-Sep-18	16-Oct-18		■								
PRO1366	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector F	15	25-Sep-18	16-Oct-18		■								
PRO1086	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector F	15	26-Sep-18	17-Oct-18		■								
PRO1956	A/E Review & Approval - BP2 - Steel Decking Shops - Sector F	15	26-Sep-18	17-Oct-18		■								
PRO2156	A/E Review & Approval - BP2 - Metal Stairs Shops - Sector D	15	26-Sep-18	17-Oct-18		■								
PRO1526	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector B	15	09-Oct-18	29-Oct-18		■								
PRO1326	A/E Review & Approval - BP2 - Structural Steel Shops - Framing - Sector H	15	10-Oct-18	30-Oct-18		■								
PRO1046	A/E Review & Approval - BP2 - Structural Steel Shops - Embeds - Sector H	15	11-Oct-18	31-Oct-18		■								
PRO1996	A/E Review & Approval - BP2 - Steel Decking Shops - Sector G&J	15	11-Oct-18	31-Oct-18		■								
PRO2196	A/E Review & Approval - BP2 - Metal Stairs Shops - Sector F	15	11-Oct-18	31-Oct-18		■								
PRO1566	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector D	15	23-Oct-18	12-Nov-18		■								
PRO1916	A/E Review & Approval - BP2 - Steel Decking Shops - Sector H	15	25-Oct-18	14-Nov-18		■								
PRO2236	A/E Review & Approval - BP2 - Metal Stairs Shops - Sector G&J	15	25-Oct-18	14-Nov-18		■								
PRO1646	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector F	15	06-Nov-18	28-Nov-18		■								

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
PRO856	A/E Review & Approval - BP2 - Concrete Tilt Up Shops - Sector G&J	15	07-Nov-18	29-Nov-18										
PRO1686	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector G&J	15	20-Nov-18	12-Dec-18										
PRO1606	A/E Review & Approval - BP2 - Steel Joist Framing Shops - Sector H	15	06-Dec-18	27-Dec-18										
Exterior Enclosure Mock Up		51	20-Aug-18	31-Oct-18										
MKUP100	F/R/P Slab	4	20-Aug-18	23-Aug-18										
MKUP101	Frame Walls (includes parapet)	4	24-Aug-18	29-Aug-18										
MKUP102	Sheathing (includes parapet)	2	30-Aug-18	31-Aug-18										
MKUP103	Weather Resistive Barrier	5	04-Sep-18	10-Sep-18										
MKUP104	RO Flashing	3	11-Sep-18	13-Sep-18										
MKUP105	Parapet Waterproofing	3	11-Sep-18	13-Sep-18										
MKUP106	Punch Window	3	14-Sep-18	18-Sep-18										
MKUP107	Brick Masonry	6	19-Sep-18	26-Sep-18										
MKUP108	Metal Panels (includes parapet)	4	27-Sep-18	02-Oct-18										
MKUP109	Caulking / Sealing	2	03-Oct-18	04-Oct-18										
MKUP110	Water Test Window Assemblies	3	05-Oct-18	10-Oct-18										
MKUP111	Mock Up Review & Approval	15	11-Oct-18	31-Oct-18										
Fabrication & Delivery		164	29-Jun-18	26-Feb-19										
BP1		85	29-Jun-18	30-Oct-18										
PRO396	Fab & Deliver - BP1 - Concrete Reinforcing - Site Concrete	10	29-Jun-18	13-Jul-18										
PRO406	Fab & Deliver - BP1 - Structural Steel - Anchor Bolts	15	29-Jun-18	20-Jul-18										
PRO416	Fab & Deliver - BP1 - Fire Sprinkler - UG Piping	20	29-Jun-18	27-Jul-18										
PRO436	Fab & Deliver - BP1 - Plumbing - UG Piping	20	29-Jun-18	27-Jul-18										
PRO446	Fab & Deliver - BP1 - Plumbing - UG Materials & Equipment	25	29-Jun-18	03-Aug-18										
PRO456	Fab & Deliver - BP1 - HVAC - UG Piping / Duct	20	29-Jun-18	27-Jul-18										
PRO476	Fab & Deliver - BP1 - Electrical - UG Materials	15	29-Jun-18	20-Jul-18										
PRO496	Fab & Deliver - BP1 - Civil - Lock & Load Retaining Wall Materials	25	29-Jun-18	03-Aug-18										
PRO426	Fab & Deliver - BP1 - Fire Sprinkler - UG Materials & Equipment	40	09-Jul-18	31-Aug-18										
PRO466	Fab & Deliver - BP1 - HVAC - UG Materials & Equipment	40	09-Jul-18	31-Aug-18										
PRO386	Fab & Deliver - BP1 - Concrete Reinforcing - Foundations	10	23-Jul-18	03-Aug-18										
PRO506	Fab & Deliver - BP1 - Landscaping - Irrigation Materials & Equipment	50	23-Jul-18	01-Oct-18										
PRO486	Fab & Deliver - BP1 - Electrical - Sports Field Lighting	60	06-Aug-18	30-Oct-18										
BP2		139	06-Aug-18	26-Feb-19										
PRO2286	Fab & Deliver - BP2 - HM Frames - Core & Shell	40	06-Aug-18	01-Oct-18										
PRO896	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector A	15	07-Aug-18	27-Aug-18										
PRO1256	Fab & Deliver - BP2 - Structural Steel - Framing - Sector B	50	07-Aug-18	17-Oct-18										
PRO2566	Fab & Deliver - BP2 - Gym Equipment	60	07-Aug-18	31-Oct-18										
PRO2446	Fab & Deliver - BP2 - Glazing	60	13-Aug-18	06-Nov-18										
PRO1176	Fab & Deliver - BP2 - Structural Steel - Framing - Sector A	50	20-Aug-18	30-Oct-18										
PRO2326	Fab & Deliver - BP2 - Brick Veneer	40	20-Aug-18	16-Oct-18										
PRO2366	Fab & Deliver - BP2 - Metal Panels	60	20-Aug-18	13-Nov-18										
PRO2406	Fab & Deliver - BP2 - Storefront & Curtain Wall	60	20-Aug-18	13-Nov-18										
PRO546	Fab & Deliver - BP2 - Concrete Reinforcing - Elevated Slabs - Sector A	10	21-Aug-18	04-Sep-18										
PRO586	Fab & Deliver - BP2 - Concrete Reinforcing - Elevated Slabs - Sector E	10	21-Aug-18	04-Sep-18										

Actual Work

Critical Remaining ...

Remaining Work

◆

◆ Milestone


Page 7 of 42

SKANSKA

■ Actual Work
 ■ Critical Remaining ...
 ■ Remaining Work
 ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
PRO626	Fab & Deliver - BP2 - Concrete Reinforcing - Elevated Slabs - Sector B	10	21-Aug-18	04-Sep-18										
PRO666	Fab & Deliver - BP2 - Concrete Reinforcing - Elevated Slabs - Sector D	10	21-Aug-18	04-Sep-18										
PRO746	Fab & Deliver - BP2 - Concrete Reinforcing - Elevated Slabs - Sector F	10	21-Aug-18	04-Sep-18										
PRO786	Fab & Deliver - BP2 - Concrete Reinforcing - Elevated Slabs - Sector G&J	10	21-Aug-18	04-Sep-18										
PRO976	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector B	15	21-Aug-18	11-Sep-18										
PRO1766	Fab & Deliver - BP2 - Steel Decking - Sector A	40	21-Aug-18	17-Oct-18										
PRO1216	Fab & Deliver - BP2 - Structural Steel - Framing - Sector E	40	04-Sep-18	30-Oct-18										
PRO936	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector E	15	05-Sep-18	25-Sep-18										
PRO1806	Fab & Deliver - BP2 - Steel Decking - Sector E	40	05-Sep-18	31-Oct-18										
PRO2046	Fab & Deliver - BP2 - Metal Stairs - Sector A	40	05-Sep-18	31-Oct-18										
PRO1296	Fab & Deliver - BP2 - Structural Steel - Framing - Sector D	40	18-Sep-18	13-Nov-18										
PRO1016	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector D	15	19-Sep-18	10-Oct-18										
PRO1846	Fab & Deliver - BP2 - Steel Decking - Sector B	40	19-Sep-18	14-Nov-18										
PRO2086	Fab & Deliver - BP2 - Metal Stairs - Sector E	40	19-Sep-18	14-Nov-18										
PRO2486	Fab & Deliver - BP2 - Elevator	60	19-Sep-18	14-Dec-18										
PRO1456	Fab & Deliver - BP2 - Steel Joist Framing - Sector A	40	01-Oct-18	28-Nov-18										
PRO1416	Fab & Deliver - BP2 - Structural Steel - Framing - Sector G&J	40	02-Oct-18	29-Nov-18										
PRO1136	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector G&J	15	03-Oct-18	24-Oct-18										
PRO1886	Fab & Deliver - BP2 - Steel Decking - Sector D	40	03-Oct-18	30-Nov-18										
PRO2126	Fab & Deliver - BP2 - Metal Stairs - Sector B	40	03-Oct-18	30-Nov-18										
PRO2526	Fab & Deliver - BP2 - CMU Masonry	30	11-Oct-18	21-Nov-18										
PRO1496	Fab & Deliver - BP2 - Steel Joist Framing - Sector E	40	16-Oct-18	12-Dec-18										
PRO1376	Fab & Deliver - BP2 - Structural Steel - Framing - Sector F	40	17-Oct-18	13-Dec-18										
PRO1096	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector F	15	18-Oct-18	07-Nov-18										
PRO1966	Fab & Deliver - BP2 - Steel Decking - Sector F	40	18-Oct-18	14-Dec-18										
PRO2166	Fab & Deliver - BP2 - Metal Stairs - Sector D	40	18-Oct-18	14-Dec-18										
PRO1536	Fab & Deliver - BP2 - Steel Joist Framing - Sector B	40	30-Oct-18	27-Dec-18										
PRO1336	Fab & Deliver - BP2 - Structural Steel - Framing - Sector H	40	31-Oct-18	28-Dec-18										
PRO1056	Fab & Deliver - BP2 - Structural Steel - Embeds - Sector H	15	01-Nov-18	21-Nov-18										
PRO2006	Fab & Deliver - BP2 - Steel Decking - Sector G&J	40	01-Nov-18	31-Dec-18										
PRO2206	Fab & Deliver - BP2 - Metal Stairs - Sector F	40	01-Nov-18	31-Dec-18										
PRO1576	Fab & Deliver - BP2 - Steel Joist Framing - Sector D	40	13-Nov-18	11-Jan-19										
PRO1926	Fab & Deliver - BP2 - Steel Decking - Sector H	40	15-Nov-18	15-Jan-19										
PRO2246	Fab & Deliver - BP2 - Metal Stairs - Sector G&J	40	15-Nov-18	15-Jan-19										
PRO1656	Fab & Deliver - BP2 - Steel Joist Framing - Sector F	40	29-Nov-18	28-Jan-19										
PRO1696	Fab & Deliver - BP2 - Steel Joist Framing - Sector G&J	40	13-Dec-18	11-Feb-19										
PRO1616	Fab & Deliver - BP2 - Steel Joist Framing - Sector H	40	28-Dec-18	26-Feb-19										
Construction		481	18-Jun-18	15-May-20										
Early Site Work		230	18-Jun-18	16-May-19										
ESW104	Establish Site Survey	5	18-Jun-18	22-Jun-18										
ESW105	Erosion & Sediment Control	15	20-Jun-18	11-Jul-18										
ESW106	Temp Fencing	20	25-Jun-18	23-Jul-18										

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ ◆ Milestone

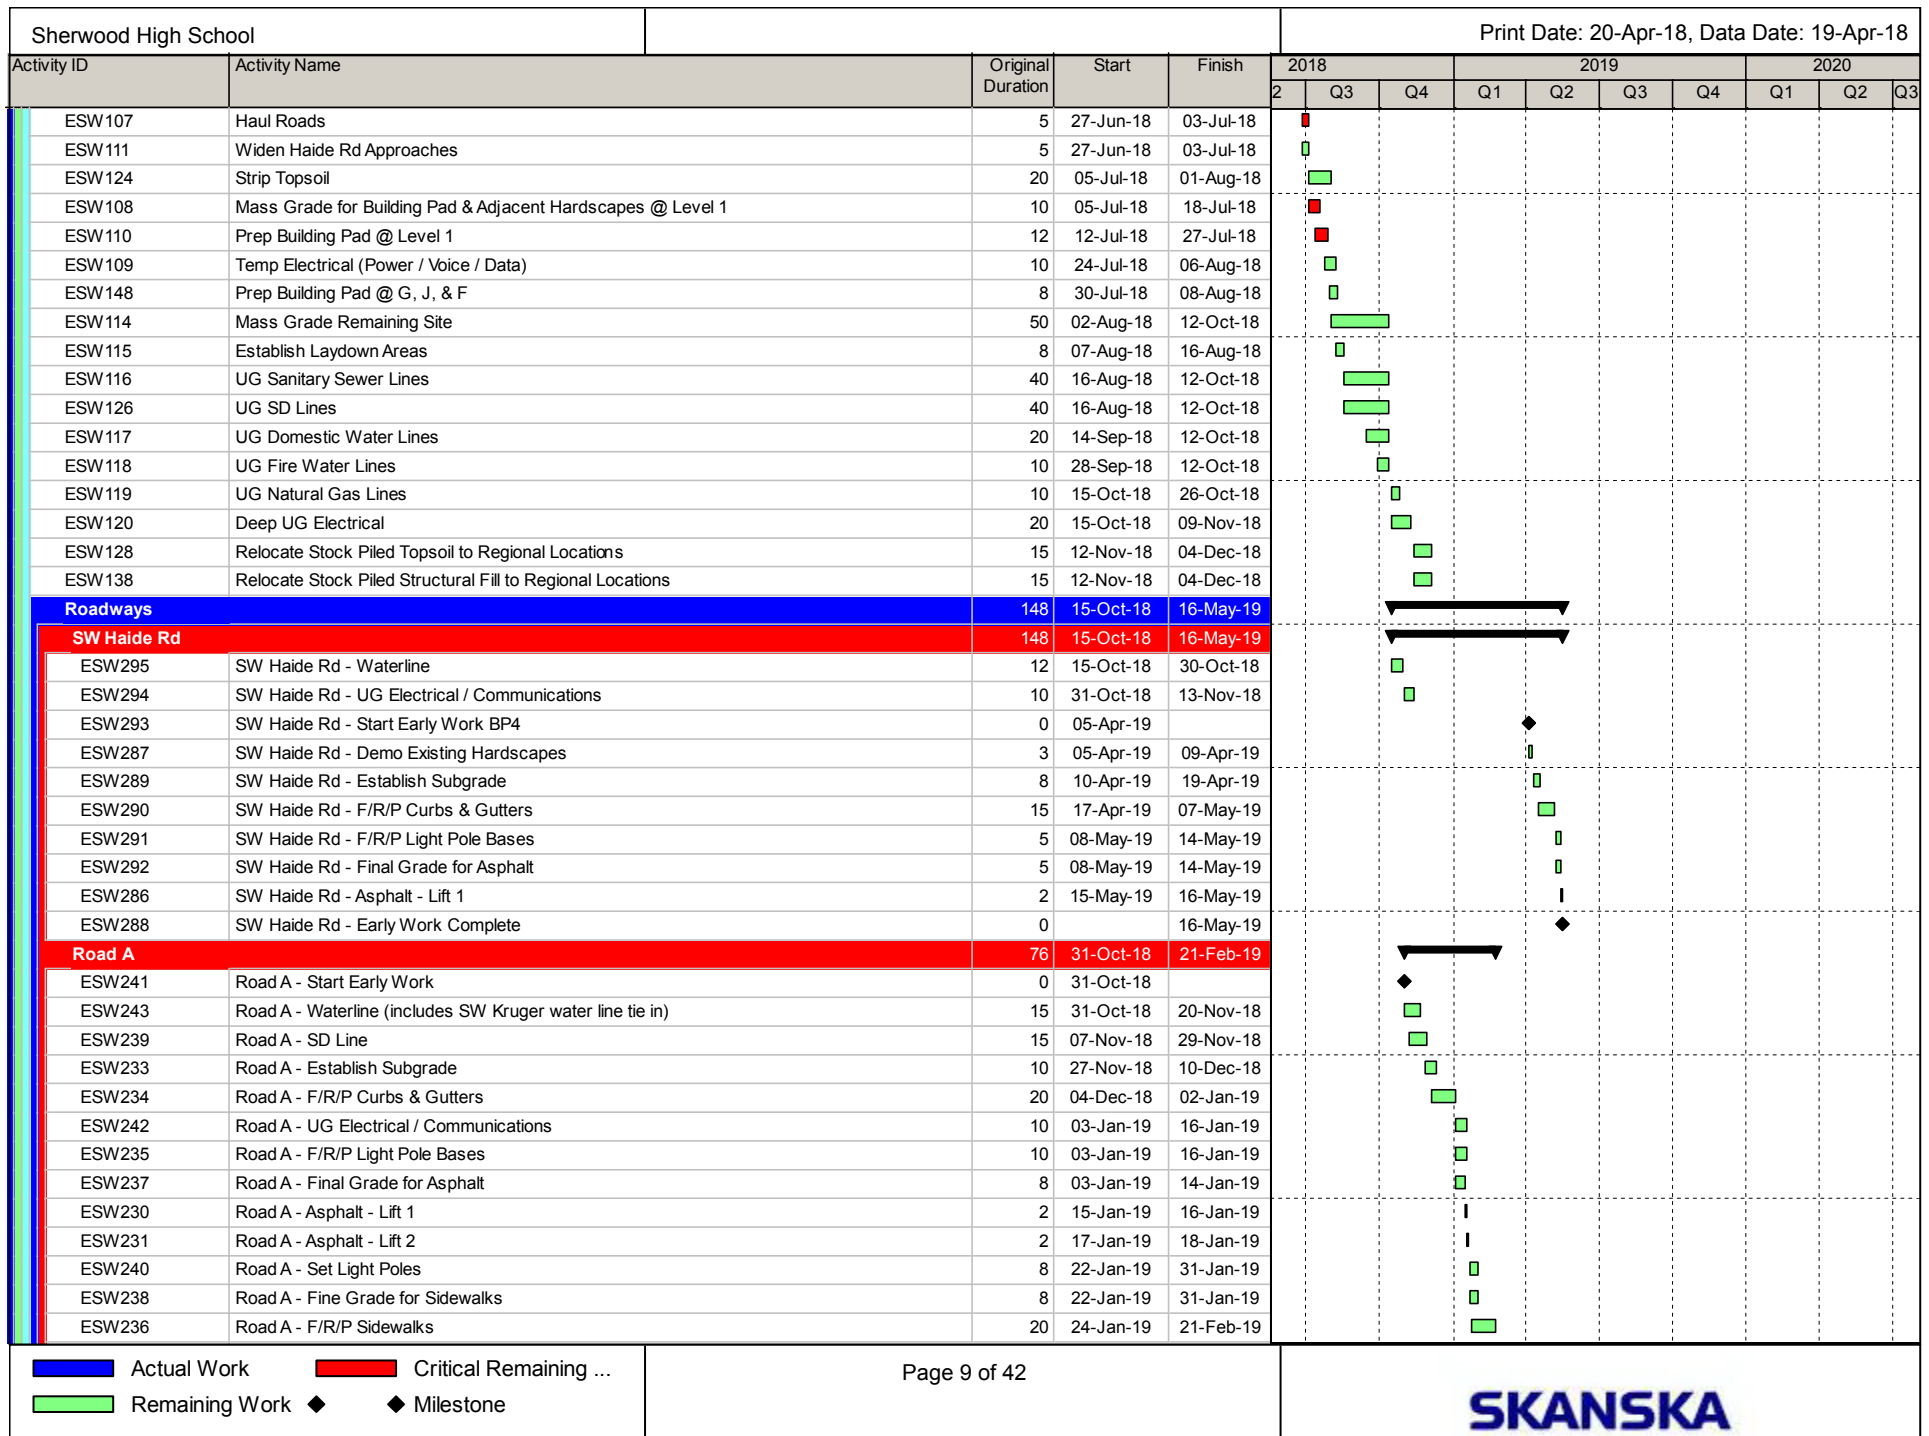

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
ESW232	Road A - Early Work Complete	0		21-Feb-19				◆						
SW Kruger Rd		10	05-Apr-19	18-Apr-19				▼						
ESW296	SW Krueger Rd - UG Electrical / Communications	10	05-Apr-19	18-Apr-19				■						
NE Region		120	12-Jul-18	03-Jan-19										
NE Parking Lot		37	12-Jul-18	31-Aug-18										
ESW205	NE - Parking - Start Early Work	0	12-Jul-18					◆						
ESW204	NE - Parking - Prep Subgrade	20	12-Jul-18	08-Aug-18				■						
ESW203	NE - Parking - Mobilize Skanska Office Trailer	5	09-Aug-18	15-Aug-18				■						
ESW206	NE - Parking - Storm Drainage	6	09-Aug-18	16-Aug-18				■						
ESW201	NE - Parking - Electrical / Telecom	6	17-Aug-18	24-Aug-18				■						
ESW202	NE - Parking - Mobilize Craft Office Trailers	5	27-Aug-18	31-Aug-18				■						
ESW200	NE - Parking - Early Work Complete	0		31-Aug-18				◆						
Storm Water Retention		35	19-Jul-18	06-Sep-18										
ESW223	NE - Retention - Start Early Work	0	19-Jul-18					◆						
ESW224	NE - Retention - UG Stormwater Piping	8	19-Jul-18	30-Jul-18				■						
ESW221	NE - Retention - Excavate Pond Subgrade	9	31-Jul-18	10-Aug-18				■						
ESW218	NE - Retention - Angular Rock Subgrade	6	13-Aug-18	20-Aug-18				■						
ESW222	NE - Retention - Semipermeable Fabric	6	21-Aug-18	28-Aug-18				■						
ESW219	NE - Retention - Drain Rock	6	29-Aug-18	06-Sep-18				■						
ESW220	NE - Retention - Early Work Complete	0		06-Sep-18				◆						
Roadway		55	15-Oct-18	03-Jan-19										
ESW216	NE - Rdwy - Start Early Work	0	15-Oct-18					◆						
ESW215	NE - Rdwy - Prep Subgrade	8	15-Oct-18	24-Oct-18				■						
ESW211	NE - Rdwy - F/R/P Light Pole Bases	6	25-Oct-18	01-Nov-18				■						
ESW217	NE - Rdwy - UG Electrical	10	02-Nov-18	15-Nov-18				■						
ESW214	NE - Rdwy - Fine Grade for Curbs & Sidewalks	6	16-Nov-18	27-Nov-18				■						
ESW210	NE - Rdwy - F/R/P Curbs	10	28-Nov-18	11-Dec-18				■						
ESW212	NE - Rdwy - F/R/P Sidewalks	10	12-Dec-18	26-Dec-18				■						
ESW213	NE - Rdwy - Fine Grade for Asphalt	3	27-Dec-18	31-Dec-18				■						
ESW207	NE - Rdwy - Adjust Manhole Covers	2	28-Dec-18	31-Dec-18				■						
ESW208	NE - Rdwy - Asphalt Lift 1	2	02-Jan-19	03-Jan-19				■						
ESW209	NE - Rdwy - Early Work Complete	0		03-Jan-19				◆						
NW Region		21	17-Aug-18	17-Sep-18										
ESW229	NW - Walls - Start Retaining Walls	0	17-Aug-18					◆						
ESW226	NW - Walls - Excavate for Concrete Retaining Walls	6	17-Aug-18	24-Aug-18				■						
ESW227	NW - Walls - F/R/P Concrete Retaining Footings & Walls	16	22-Aug-18	13-Sep-18				■						
ESW225	NW - Walls - Backfill Concrete Retaining Walls	5	11-Sep-18	17-Sep-18				■						
ESW228	NW - Walls - Retaining Walls Complete	0		17-Sep-18				◆						
SW Region		42	15-Oct-18	13-Dec-18										
W Parking Lot		42	15-Oct-18	13-Dec-18										
ESW284	SW - Parking - Start Early Work	0	15-Oct-18					◆						
ESW283	SW - Parking - Prep Subgrade	5	15-Oct-18	19-Oct-18				■						
ESW285	SW - Parking - Storm Drainage	5	22-Oct-18	26-Oct-18				■						

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
ESW272	Stadium - Retaining Walls & Stairs Complete	0		10-Jan-19				◆						
School Building		452	30-Jul-18	15-May-20										
Sector A		334	30-Jul-18	25-Nov-19										
Foundation (Level 1)		86	30-Jul-18	30-Nov-18										
SECT-A-100	Fndn - Lvl 1 - Excavate for Retaining Wall Footings (grids 29 & 30)	3	30-Jul-18	01-Aug-18										
SECT-A-101	Fndn - Lvl 1 - Excavate for Elevator Pit	2	02-Aug-18	03-Aug-18										
SECT-A-102	Fndn - Lvl 1 - F/R/P Retaining Wall Footings (grids 29 & 30)	5	06-Aug-18	10-Aug-18										
SECT-A-103	Fndn - Lvl 1 - Excavate for Remaining Footings	2	06-Aug-18	07-Aug-18										
SECT-A-105	Fndn - Lvl 1 - F/R/P Elevator Pit Foundation & Walls	8	06-Aug-18	15-Aug-18										
SECT-A-104	Fndn - Lvl 1 - F/R/P Remaining Footings	8	08-Aug-18	17-Aug-18										
SECT-A-152	Fndn - Lvl 1 - F/R/P Retaining Wall (grids 29 & 30)	10	13-Aug-18	24-Aug-18										
SECT-A-116	Fndn - Lvl 1 - F/R/P Footings (adjacent to Elevator Pit)	3	16-Aug-18	20-Aug-18										
SECT-A-126	Fndn - Lvl 1 - Backfill Footings	3	20-Aug-18	22-Aug-18										
SECT-A-107	Fndn - Lvl 1 - UG Plumbing	10	23-Aug-18	06-Sep-18										
SECT-A-106	Fndn - Lvl 1 - UG Electrical	10	23-Aug-18	06-Sep-18										
SECT-A-108	Fndn - Lvl 1 - Fine Grade for SOG	5	07-Sep-18	13-Sep-18										
SECT-A-109	Fndn - Lvl 1 - F/R/P SOG (includes vapor barrier)	8	14-Sep-18	25-Sep-18										
SECT-A-110	Fndn - Lvl 1 - F/R/P Tilt Panels	20	17-Oct-18	13-Nov-18										
SECT-A-111	Fndn - Lvl 1 - Tilt Panel Cure	5	14-Nov-18	20-Nov-18										
SECT-A-112	Fndn - Lvl 1 - Erect Tilt Panels	3	28-Nov-18	30-Nov-18										
Structure		24	03-Dec-18	07-Jan-19										
SECT-A-150	Struct - Erect Steel	7	03-Dec-18	11-Dec-18										
Level 2		17	12-Dec-18	07-Jan-19										
North		11	12-Dec-18	27-Dec-18										
SECT-A-155	Struct - Lvl 2 - N - Metal Decking	3	12-Dec-18	14-Dec-18										
SECT-A-159	Struct - Lvl 2 - N - SOMD Mechanical RI	3	20-Dec-18	24-Dec-18										
SECT-A-160	Struct - Lvl 2 - N - SOMD Electrical RI	3	20-Dec-18	24-Dec-18										
SECT-A-161	Struct - Lvl 2 - N - SOMD Plumbing RI	3	20-Dec-18	24-Dec-18										
SECT-A-166	Struct - Lvl 2 - N - F/R/P SOMD	2	26-Dec-18	27-Dec-18										
Running Track		6	28-Dec-18	07-Jan-19										
SECT-A-156	Struct - Lvl 2 - Track - Steel & Metal Decking	4	28-Dec-18	03-Jan-19										
SECT-A-165	Struct - Lvl 2 - Track - F/R/P SOMD	2	04-Jan-19	07-Jan-19										
Level 3		13	17-Dec-18	04-Jan-19										
SECT-A-157	Struct - Lvl 3 - Metal Decking	3	17-Dec-18	19-Dec-18										
SECT-A-162	Struct - Lvl 3 - SOMD Mechanical RI	3	28-Dec-18	02-Jan-19										
SECT-A-163	Struct - Lvl 3 - SOMD Electrical RI	3	28-Dec-18	02-Jan-19										
SECT-A-164	Struct - Lvl 3 - SOMD Plumbing RI	3	28-Dec-18	02-Jan-19										
SECT-A-167	Struct - Lvl 3 - F/R/P SOMD	2	03-Jan-19	04-Jan-19										
Roof		5	20-Dec-18	27-Dec-18										
SECT-A-158	Struct - Roof - Metal Decking	5	20-Dec-18	27-Dec-18										
Exterior Enclosure		48	27-Dec-18	08-Mar-19										
West		21	28-Dec-18	29-Jan-19										
SECT-A-327	Ext - West - WRB	7	28-Dec-18	08-Jan-19										
Actual Work Critical Remaining ... Remaining Work ◆ Milestone														

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SECT-A-317	Ext - West - Brick Masonry (inc. insulation & lintels)	9	09-Jan-19	22-Jan-19										
SECT-A-307	Ext - West - Clean & Seal	2	23-Jan-19	24-Jan-19										
SECT-A-337	Ext - West - School Emblem	3	25-Jan-19	29-Jan-19										
SECT-A-377	Ext - West - Complete	0		29-Jan-19										
South		41	09-Jan-19	08-Mar-19										
SECT-A-347	Ext - South - WRB (includes flashings)	7	09-Jan-19	17-Jan-19										
SECT-A-397	Ext - South - Exterior Glazing Systems	10	18-Jan-19	01-Feb-19										
SECT-A-357	Ext - South - Brick Masonry (inc. insulation & lintels)	9	04-Feb-19	14-Feb-19										
SECT-A-367	Ext - South - Clean & Seal	2	15-Feb-19	19-Feb-19										
SECT-A-407	Ext - South - Metal Panels	10	15-Feb-19	01-Mar-19										
SECT-A-417	Ext - South - Canopy Assembly	3	04-Mar-19	06-Mar-19										
SECT-A-427	Ext - South - Canopy Roofing	2	07-Mar-19	08-Mar-19										
SECT-A-437	Ext - South - Complete	0		08-Mar-19										
North (@ courtyard)		40	28-Dec-18	26-Feb-19										
Lower Wall		40	28-Dec-18	26-Feb-19										
SECT-A-451	Ext - North - Lower Wall - Framing & Sheathing	15	28-Dec-18	18-Jan-19										
SECT-A-455	Ext - North - Lower Wall - WRB (includes flashings)	9	22-Jan-19	01-Feb-19										
SECT-A-457	Ext - North - Lower Wall - Exterior Glazing Systems	7	04-Feb-19	12-Feb-19										
SECT-A-458	Ext - North - Lower Wall - Brick Masonry (inc. insulation & lintels)	7	13-Feb-19	22-Feb-19										
SECT-A-459	Ext - North - Lower Wall - Clean & Seal	2	25-Feb-19	26-Feb-19										
SECT-A-469	Ext - North - Lower Wall - Complete	0		26-Feb-19										
Upper Wall		23	22-Jan-19	22-Feb-19										
SECT-A-450	Ext - North - Upper Wall - Framing & Sheathing	5	22-Jan-19	28-Jan-19										
SECT-A-452	Ext - North - Upper Wall - WRB (includes flashings)	3	04-Feb-19	06-Feb-19										
SECT-A-453	Ext - North - Upper Wall - Exterior Glazing Systems	4	07-Feb-19	12-Feb-19										
SECT-A-454	Ext - North - Upper Wall - Brick Masonry (inc. insulation, lintels, & precast)	5	13-Feb-19	20-Feb-19										
SECT-A-456	Ext - North - Upper Wall - Clean & Seal	2	21-Feb-19	22-Feb-19										
SECT-A-466	Ext - North - Upper Wall - Complete	0		22-Feb-19										
Roof		42	27-Dec-18	28-Feb-19										
SECT-A-297	Ext - Roof - Start	0		27-Dec-18										
SECT-A-187	Ext - Roof - Parapet Framing & Sheathing	10	28-Dec-18	11-Jan-19										
SECT-A-197	Ext - Roof - Roof Drains	5	28-Dec-18	04-Jan-19										
SECT-A-207	Ext - Roof - Mechanical Curbs / Penetrations	5	28-Dec-18	04-Jan-19										
SECT-A-217	Ext - Roof - Roofing	15	14-Jan-19	04-Feb-19										
SECT-A-237	Ext - Roof - Flashing	8	05-Feb-19	14-Feb-19										
SECT-A-247	Ext - Roof - Set Mech Units	2	05-Feb-19	06-Feb-19										
SECT-A-257	Ext - Roof - Mech Unit Electrical Connections	15	07-Feb-19	28-Feb-19										
SECT-A-267	Ext - Roof - Mech Unit Mechanical Connections	15	07-Feb-19	28-Feb-19										
SECT-A-277	Ext - Roof - Screen Wall - Framing	10	07-Feb-19	21-Feb-19										
SECT-A-227	Ext - Roof - Building Dry In	0		12-Feb-19										
SECT-A-287	Ext - Roof - Screen Wall - Metal Panels	5	22-Feb-19	28-Feb-19										
Interior Buildout		160	05-Feb-19	20-Sep-19										
Completion		70	16-Aug-19	25-Nov-19										

Actual Work

Remaining Work

◆


◆ Milestone


Critical Remaining ...


Page 13 of 42


SKANSKA

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

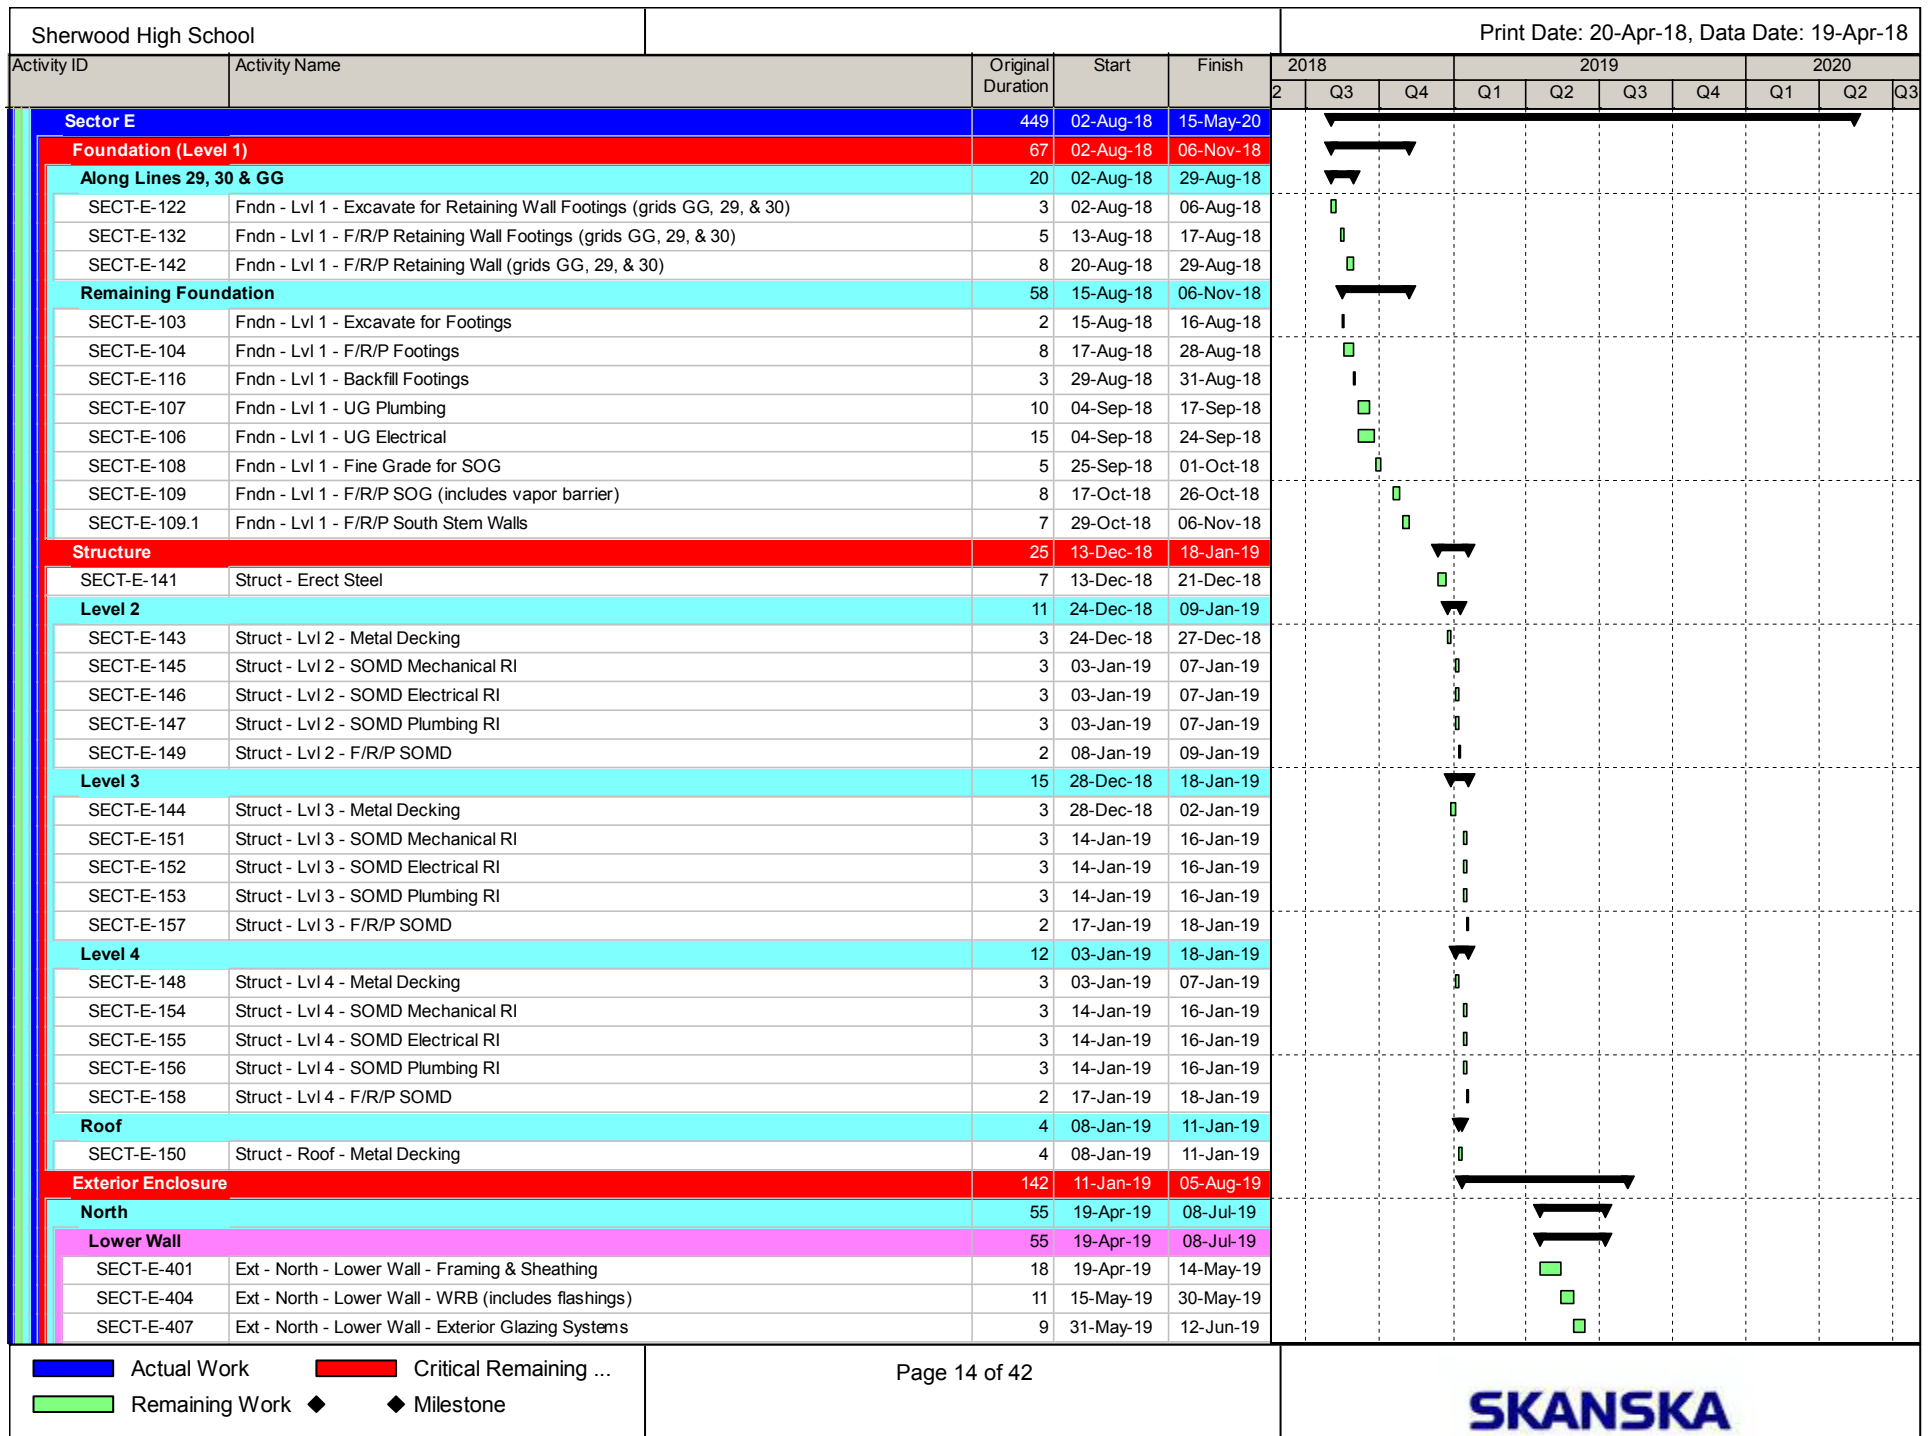

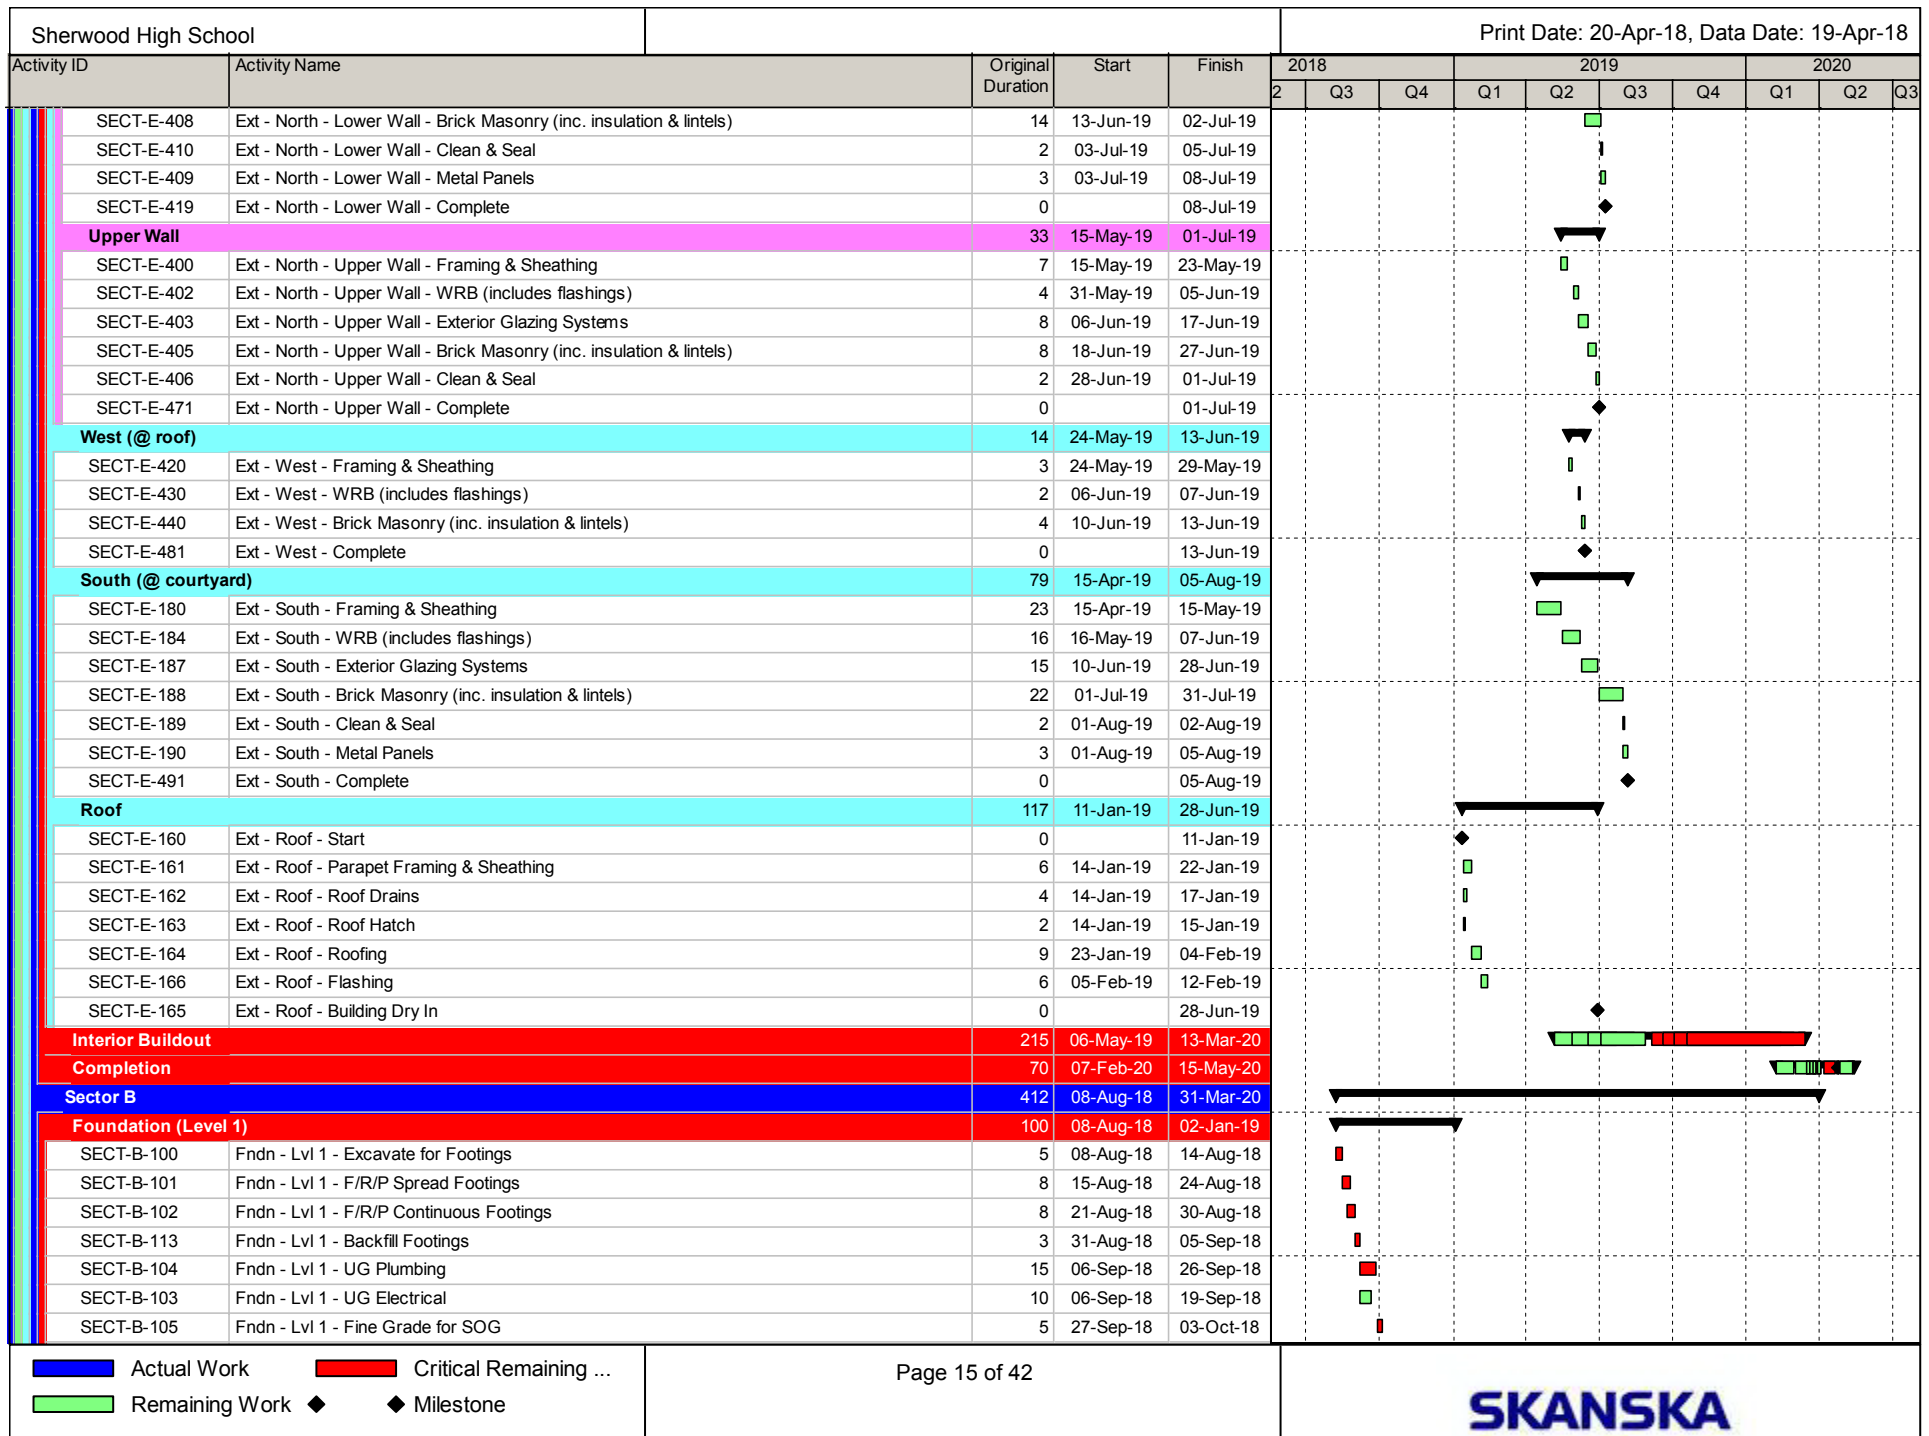


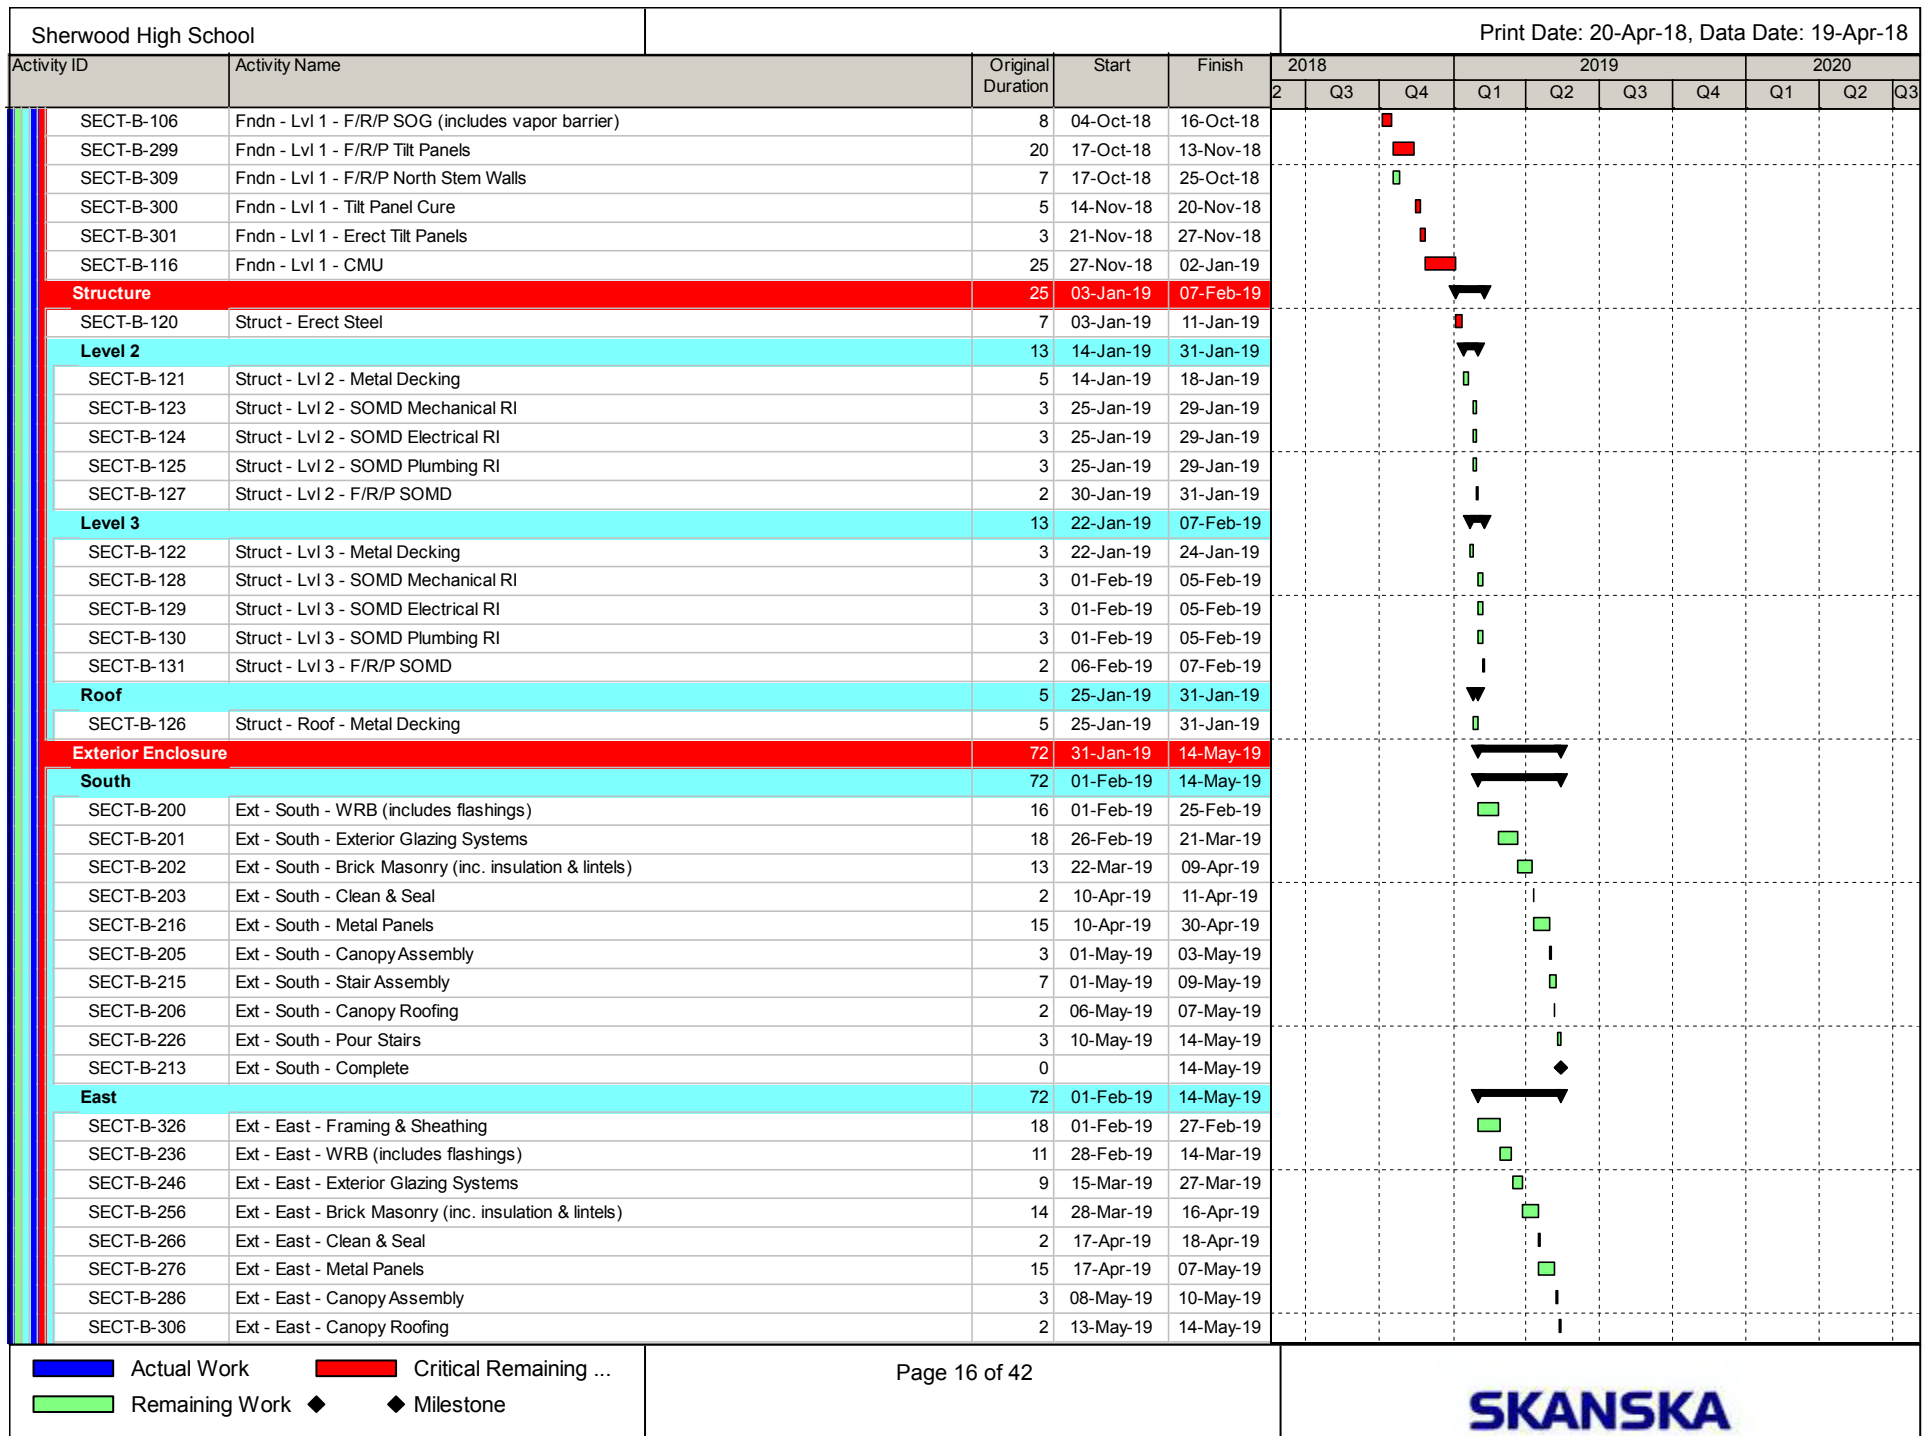


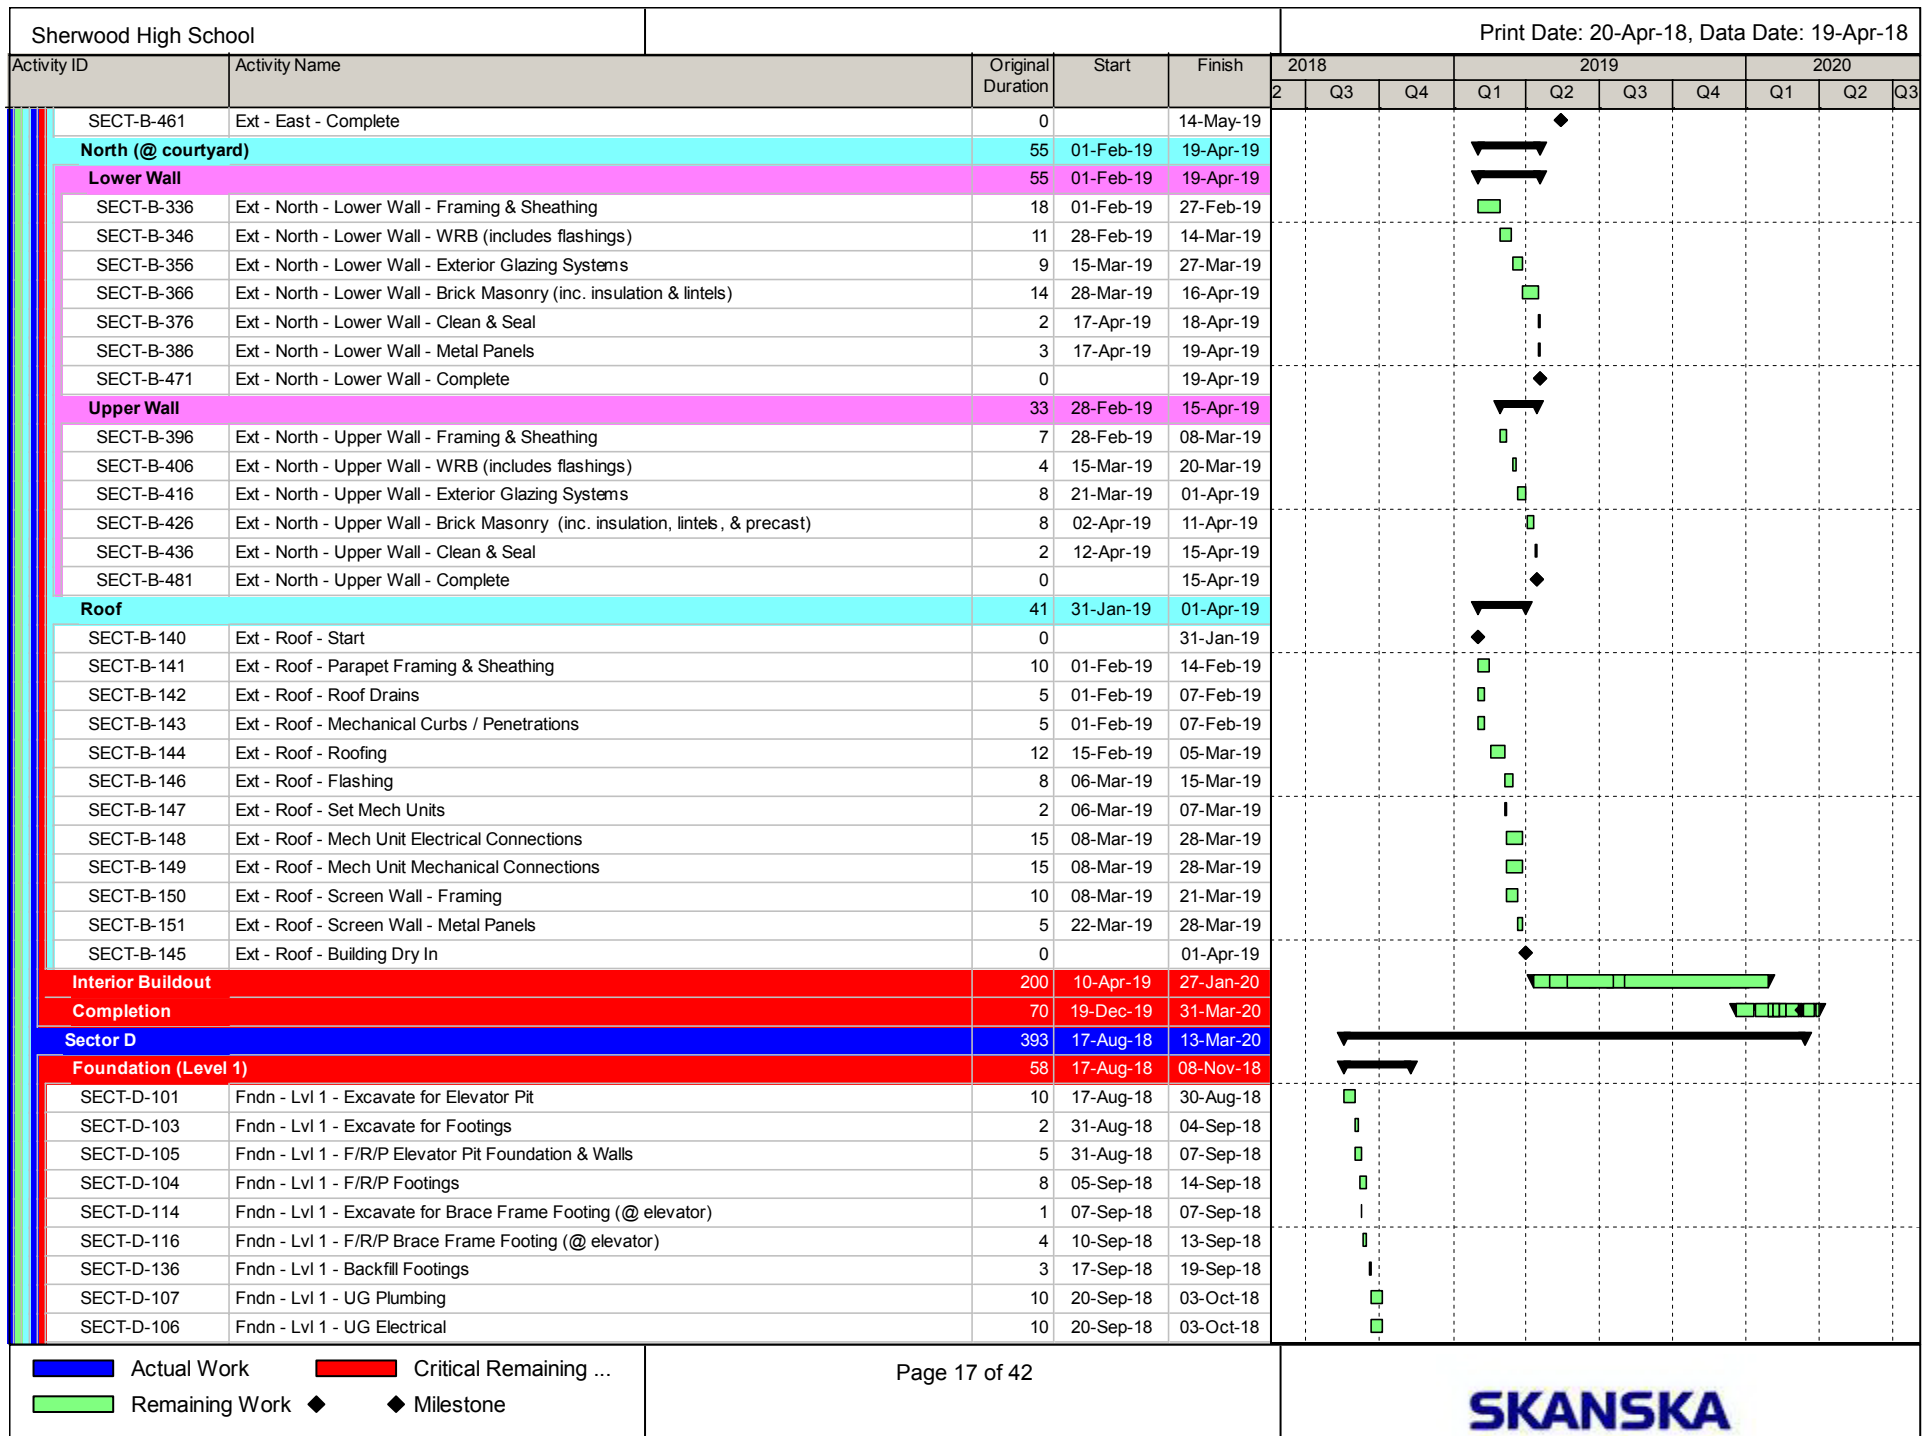

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SECT-D-108	Fndn - Lvl 1 - Fine Grade for SOG	4	04-Oct-18	10-Oct-18										
SECT-D-109	Fndn - Lvl 1 - F/R/P SOG (includes vapor barrier)	6	29-Oct-18	05-Nov-18										
SECT-D-109.1	Fndn - Lvl 1 - F/R/P South Stem Walls	3	06-Nov-18	08-Nov-18										
Structure		25	14-Jan-19	19-Feb-19										
SECT-D-117	Struct - Erect Steel	7	14-Jan-19	23-Jan-19										
Level 2		11	24-Jan-19	07-Feb-19										
SECT-D-118	Struct - Lvl 2 - Metal Decking	3	24-Jan-19	28-Jan-19										
SECT-D-120	Struct - Lvl 2 - SOMD Mechanical RI	3	01-Feb-19	05-Feb-19										
SECT-D-121	Struct - Lvl 2 - SOMD Electrical RI	3	01-Feb-19	05-Feb-19										
SECT-D-122	Struct - Lvl 2 - SOMD Plumbing RI	3	01-Feb-19	05-Feb-19										
SECT-D-124	Struct - Lvl 2 - F/R/P SOMD	2	06-Feb-19	07-Feb-19										
Level 3		15	29-Jan-19	19-Feb-19										
SECT-D-119	Struct - Lvl 3 - Metal Decking	3	29-Jan-19	31-Jan-19										
SECT-D-125	Struct - Lvl 3 - SOMD Mechanical RI	3	12-Feb-19	14-Feb-19										
SECT-D-126	Struct - Lvl 3 - SOMD Electrical RI	3	12-Feb-19	14-Feb-19										
SECT-D-127	Struct - Lvl 3 - SOMD Plumbing RI	3	12-Feb-19	14-Feb-19										
SECT-D-128	Struct - Lvl 3 - F/R/P SOMD	2	15-Feb-19	19-Feb-19										
Level 4		12	01-Feb-19	19-Feb-19										
SECT-D-138	Struct - Lvl 4 - Metal Decking	3	01-Feb-19	05-Feb-19										
SECT-D-148	Struct - Lvl 4 - SOMD Mechanical RI	3	12-Feb-19	14-Feb-19										
SECT-D-158	Struct - Lvl 4 - SOMD Electrical RI	3	12-Feb-19	14-Feb-19										
SECT-D-168	Struct - Lvl 4 - SOMD Plumbing RI	3	12-Feb-19	14-Feb-19										
SECT-D-178	Struct - Lvl 4 - F/R/P SOMD	2	15-Feb-19	19-Feb-19										
Roof		4	06-Feb-19	11-Feb-19										
SECT-D-123	Struct - Roof - Metal Decking	4	06-Feb-19	11-Feb-19										
Exterior Enclosure		99	11-Feb-19	02-Jul-19										
East		79	12-Feb-19	04-Jun-19										
SECT-D-212	Ext - East - Framing & Sheathing	25	12-Feb-19	19-Mar-19										
SECT-D-213	Ext - East - WRB (includes flashings)	4	20-Mar-19	25-Mar-19										
SECT-D-214	Ext - East - Exterior Glazing Systems	30	26-Mar-19	06-May-19										
SECT-D-215	Ext - East - Brick Masonry (inc. insulation & lintels)	8	07-May-19	16-May-19										
SECT-D-217	Ext - East - Clean & Seal	2	17-May-19	20-May-19										
SECT-D-216	Ext - East - Metal Panels	12	17-May-19	04-Jun-19										
SECT-D-236	Ext - East - Complete	0		04-Jun-19										
North		70	20-Mar-19	26-Jun-19										
Lower Wall		25	20-Mar-19	23-Apr-19										
SECT-D-221	Ext - North - Lower Wall - Framing & Sheathing	8	20-Mar-19	29-Mar-19										
SECT-D-224	Ext - North - Lower Wall - WRB (includes flashings)	3	01-Apr-19	03-Apr-19										
SECT-D-227	Ext - North - Lower Wall - Exterior Glazing Systems	7	04-Apr-19	12-Apr-19										
SECT-D-228	Ext - North - Lower Wall - Brick Masonry (inc. insulation & lintels)	5	15-Apr-19	19-Apr-19										
SECT-D-230	Ext - North - Lower Wall - Clean & Seal	2	22-Apr-19	23-Apr-19										
SECT-D-229	Ext - North - Lower Wall - Metal Panels	2	22-Apr-19	23-Apr-19										
SECT-D-281	Ext - North - Lower Wall - Complete	0		23-Apr-19										

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

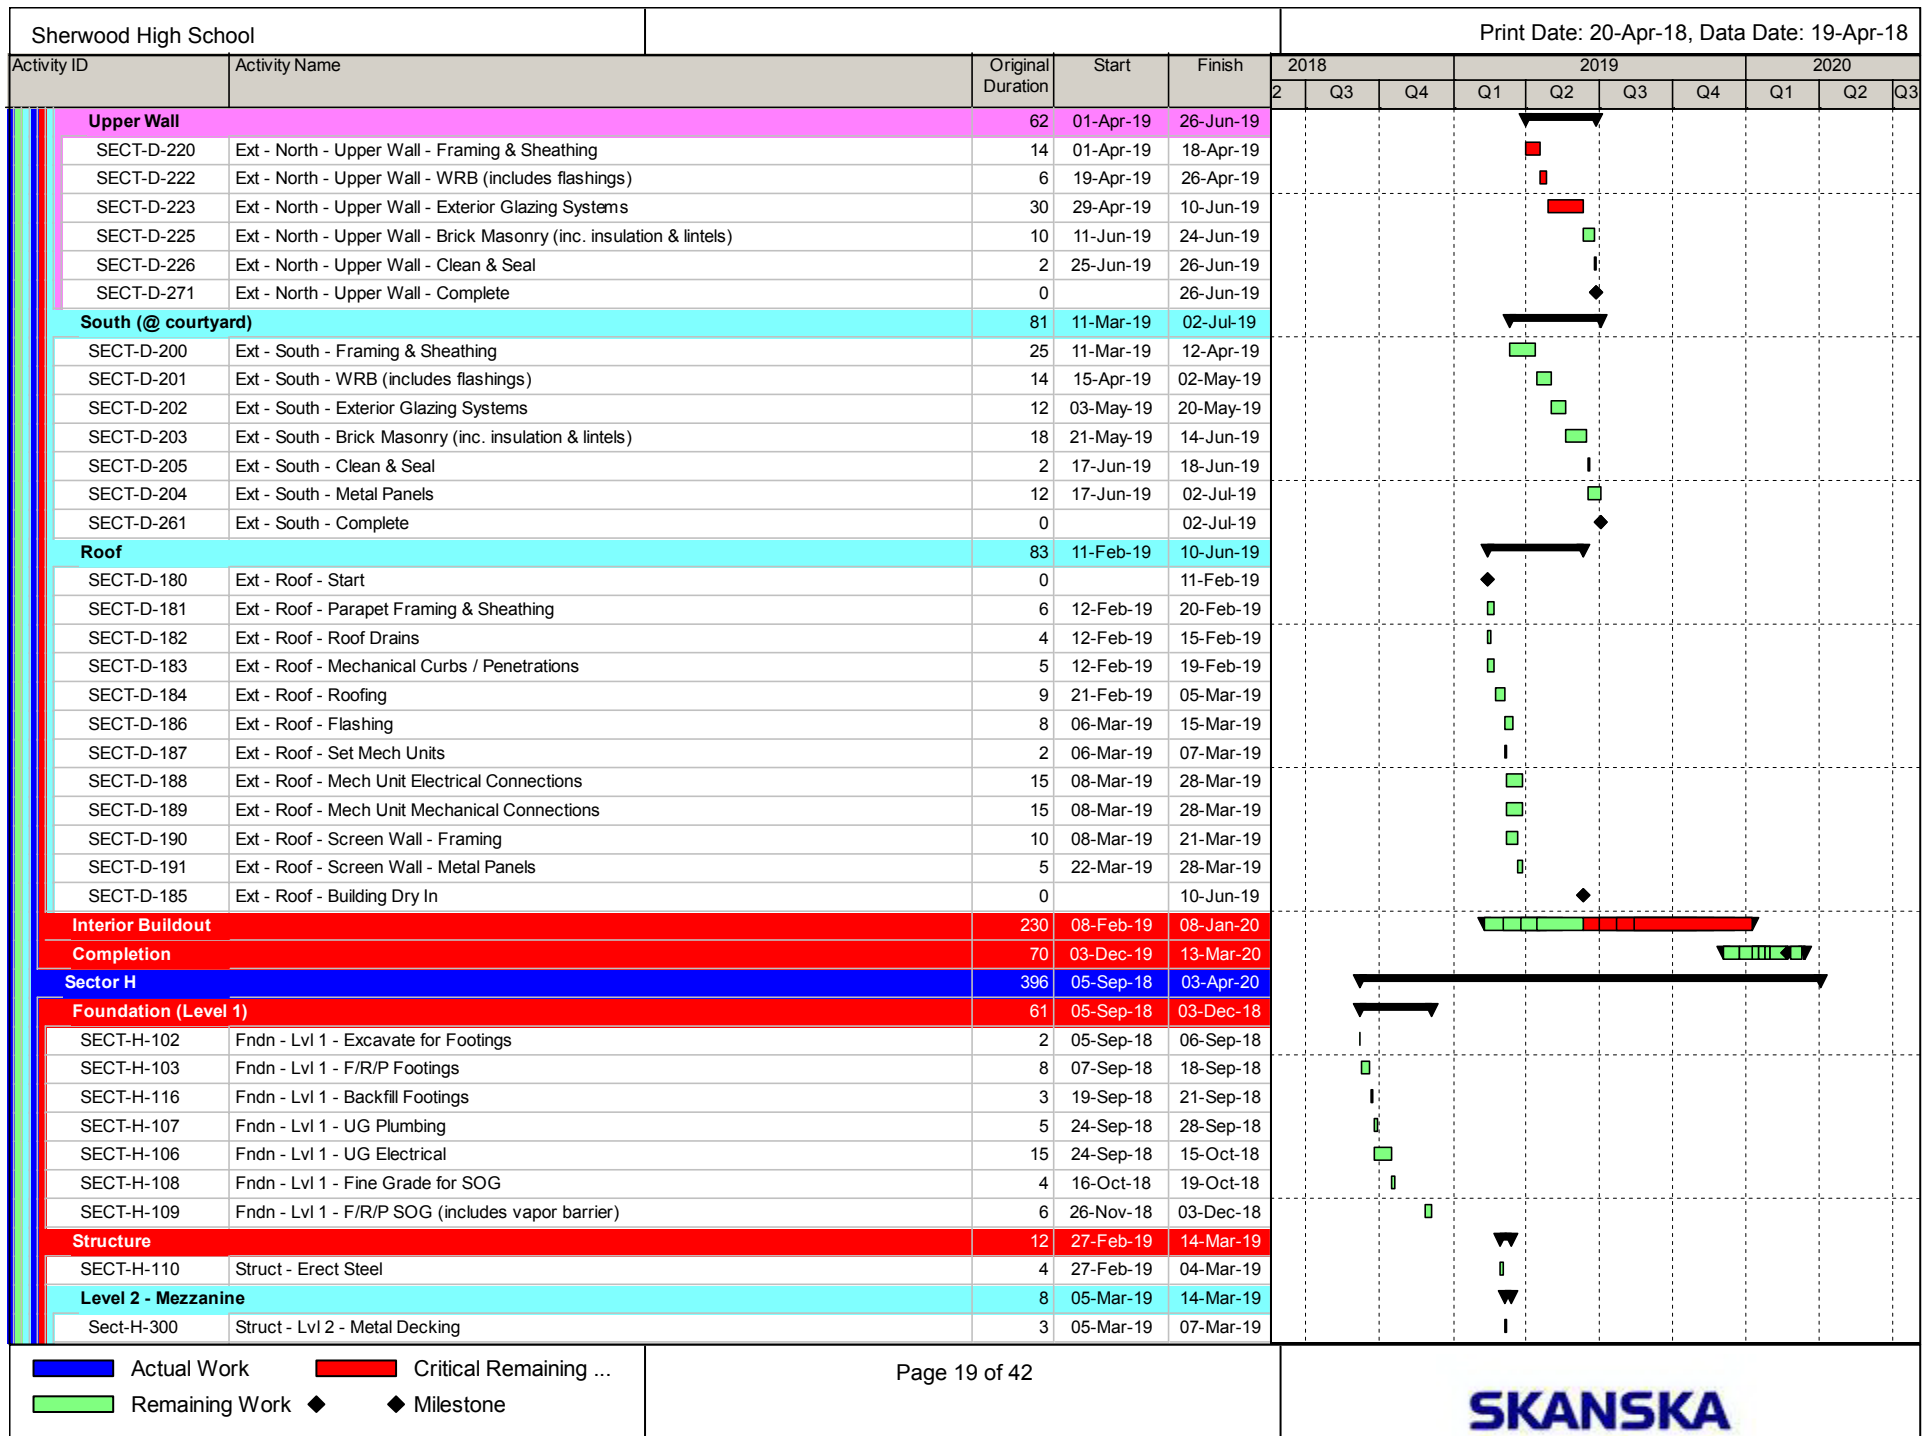

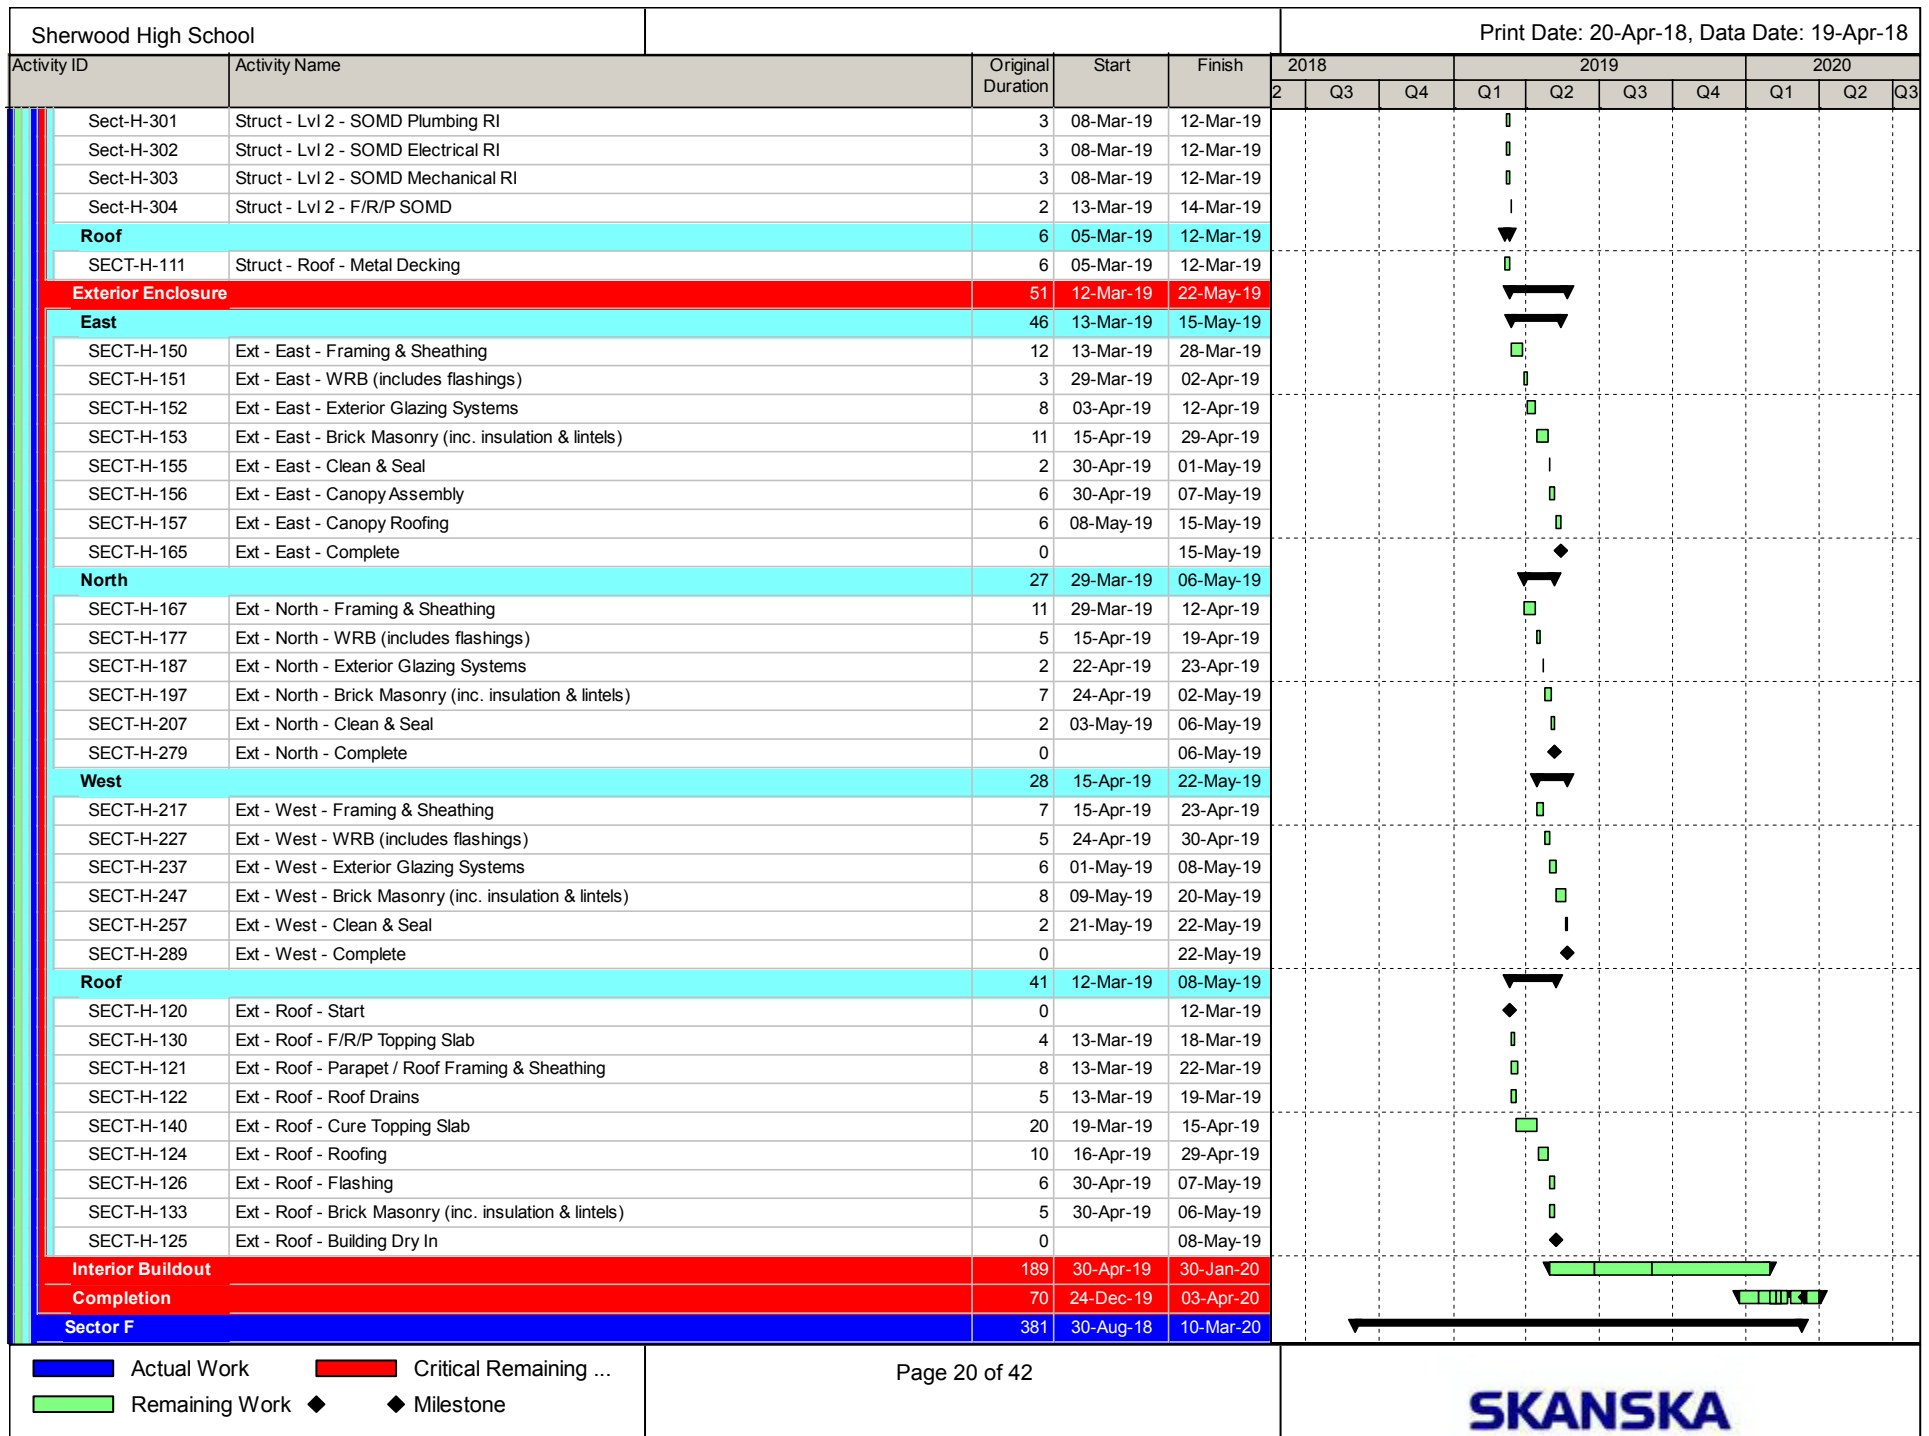


Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019			2020			
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
Foundation		101	30-Aug-18	28-Jan-19										
Level 2		83	30-Aug-18	31-Dec-18										
SECT-F-141	Fndn - Lvl 2 - Retaining Wall Concrete Cure (grids 29, & 30)	5	30-Aug-18	06-Sep-18										
SECT-F-111	Fndn - Lvl 2 - Waterproof Retaining Wall (grids 29, & 30)	10	30-Aug-18	13-Sep-18										
SECT-F-121	Fndn - Lvl 2 - Retaining Wall Drainage (grids 29, & 30)	8	14-Sep-18	25-Sep-18										
SECT-F-131	Fndn - Lvl 2 - Backfill & Compaction	5	26-Sep-18	02-Oct-18										
SECT-F-100	Fndn - Lvl 2 - Excavate for Footings	3	03-Oct-18	05-Oct-18										
SECT-F-102	Fndn - Lvl 2 - F/R/P Footings	8	09-Oct-18	18-Oct-18										
SECT-F-123	Fndn - Lvl 2 - Backfill Footings	3	19-Oct-18	23-Oct-18										
SECT-F-113	Fndn - Lvl 2 - F/R/P Retaining Wall (grids 8.1, 8.2, 18, 20, 26, K, S)	10	19-Oct-18	01-Nov-18										
SECT-F-104	Fndn - Lvl 2 - UG Plumbing	10	24-Oct-18	06-Nov-18										
SECT-F-103	Fndn - Lvl 2 - UG Electrical	15	24-Oct-18	13-Nov-18										
SECT-F-105	Fndn - Lvl 2 - Fine Grade for SOG	5	14-Nov-18	20-Nov-18										
SECT-F-106	Fndn - Lvl 2 - F/R/P SOG (includes vapor barrier)	8	21-Nov-18	04-Dec-18										
SECT-F-116	Fndn - Lvl 2 - F/R/P Seating / Stair Assembly	18	05-Dec-18	31-Dec-18										
Level 3		57	02-Nov-18	28-Jan-19										
SECT-F-171	Fndn - Lvl 3 - Retaining Wall Concrete Cure (grids 8.1, 8.2, 18, 20, 26, K, S)	5	02-Nov-18	08-Nov-18										
SECT-F-161	Fndn - Lvl 3 - Waterproof Retaining Wall (grids 8.1, 8.2, 18, 20, 26, K, S)	10	02-Nov-18	15-Nov-18										
SECT-F-181	Fndn - Lvl 3 - Retaining Wall Drainage (grids 8.1, 8.2, 18, 20, 26, K, S)	8	16-Nov-18	29-Nov-18										
SECT-F-191	Fndn - Lvl 3 - Backfill & Compaction	5	30-Nov-18	06-Dec-18										
SECT-F-211	Fndn - Lvl 3 - Excavate for Footings	3	07-Dec-18	11-Dec-18										
SECT-F-221	Fndn - Lvl 3 - F/R/P Footings	5	12-Dec-18	18-Dec-18										
SECT-F-291	Fndn - Lvl 3 - Backfill Footings	3	19-Dec-18	21-Dec-18										
SECT-F-251	Fndn - Lvl 3 - F/R/P Freezer Rat Slab	5	19-Dec-18	26-Dec-18										
SECT-F-241	Fndn - Lvl 3 - UG Plumbing	10	24-Dec-18	08-Jan-19										
SECT-F-231	Fndn - Lvl 3 - UG Electrical	10	24-Dec-18	08-Jan-19										
SECT-F-261	Fndn - Lvl 3 - Fine Grade for SOG	5	09-Jan-19	15-Jan-19										
SECT-F-271	Fndn - Lvl 3 - F/R/P SOG (includes vapor barrier)	8	16-Jan-19	28-Jan-19										
Structure		22	29-Jan-19	28-Feb-19										
SECT-F-284	Struct - Erect Steel	7	29-Jan-19	06-Feb-19										
Level 3		15	07-Feb-19	28-Feb-19										
SECT-F-285	Struct - Lvl 3 - Metal Decking	3	07-Feb-19	11-Feb-19										
SECT-F-280	Struct - Lvl 3 - SOMD Mechanical RI	3	22-Feb-19	26-Feb-19										
SECT-F-281	Struct - Lvl 3 - SOMD Electrical RI	3	22-Feb-19	26-Feb-19										
SECT-F-282	Struct - Lvl 3 - SOMD Plumbing RI	3	22-Feb-19	26-Feb-19										
SECT-F-283	Struct - Lvl 3 - F/R/P SOMD	2	27-Feb-19	28-Feb-19										
Roof		7	12-Feb-19	21-Feb-19										
SECT-F-286	Struct - Roof - Metal Decking	7	12-Feb-19	21-Feb-19										
Exterior Enclosure		102	21-Feb-19	17-Jul-19										
North		57	22-Feb-19	13-May-19										
Lower Wall		57	22-Feb-19	13-May-19										
SECT-F-340	Ext - North - Lower Wall - Framing & Sheathing	13	22-Feb-19	12-Mar-19										
SECT-F-344	Ext - North - Lower Wall - WRB (includes flashings)	4	13-Mar-19	18-Mar-19										


Actual Work Critical Remaining ... Remaining Work Milestone Milestone

Page 21 of 42

SKANSKA


■ Actual Work
 ■ Critical Remaining ...
 ■ Remaining Work
 ◆ Milestone

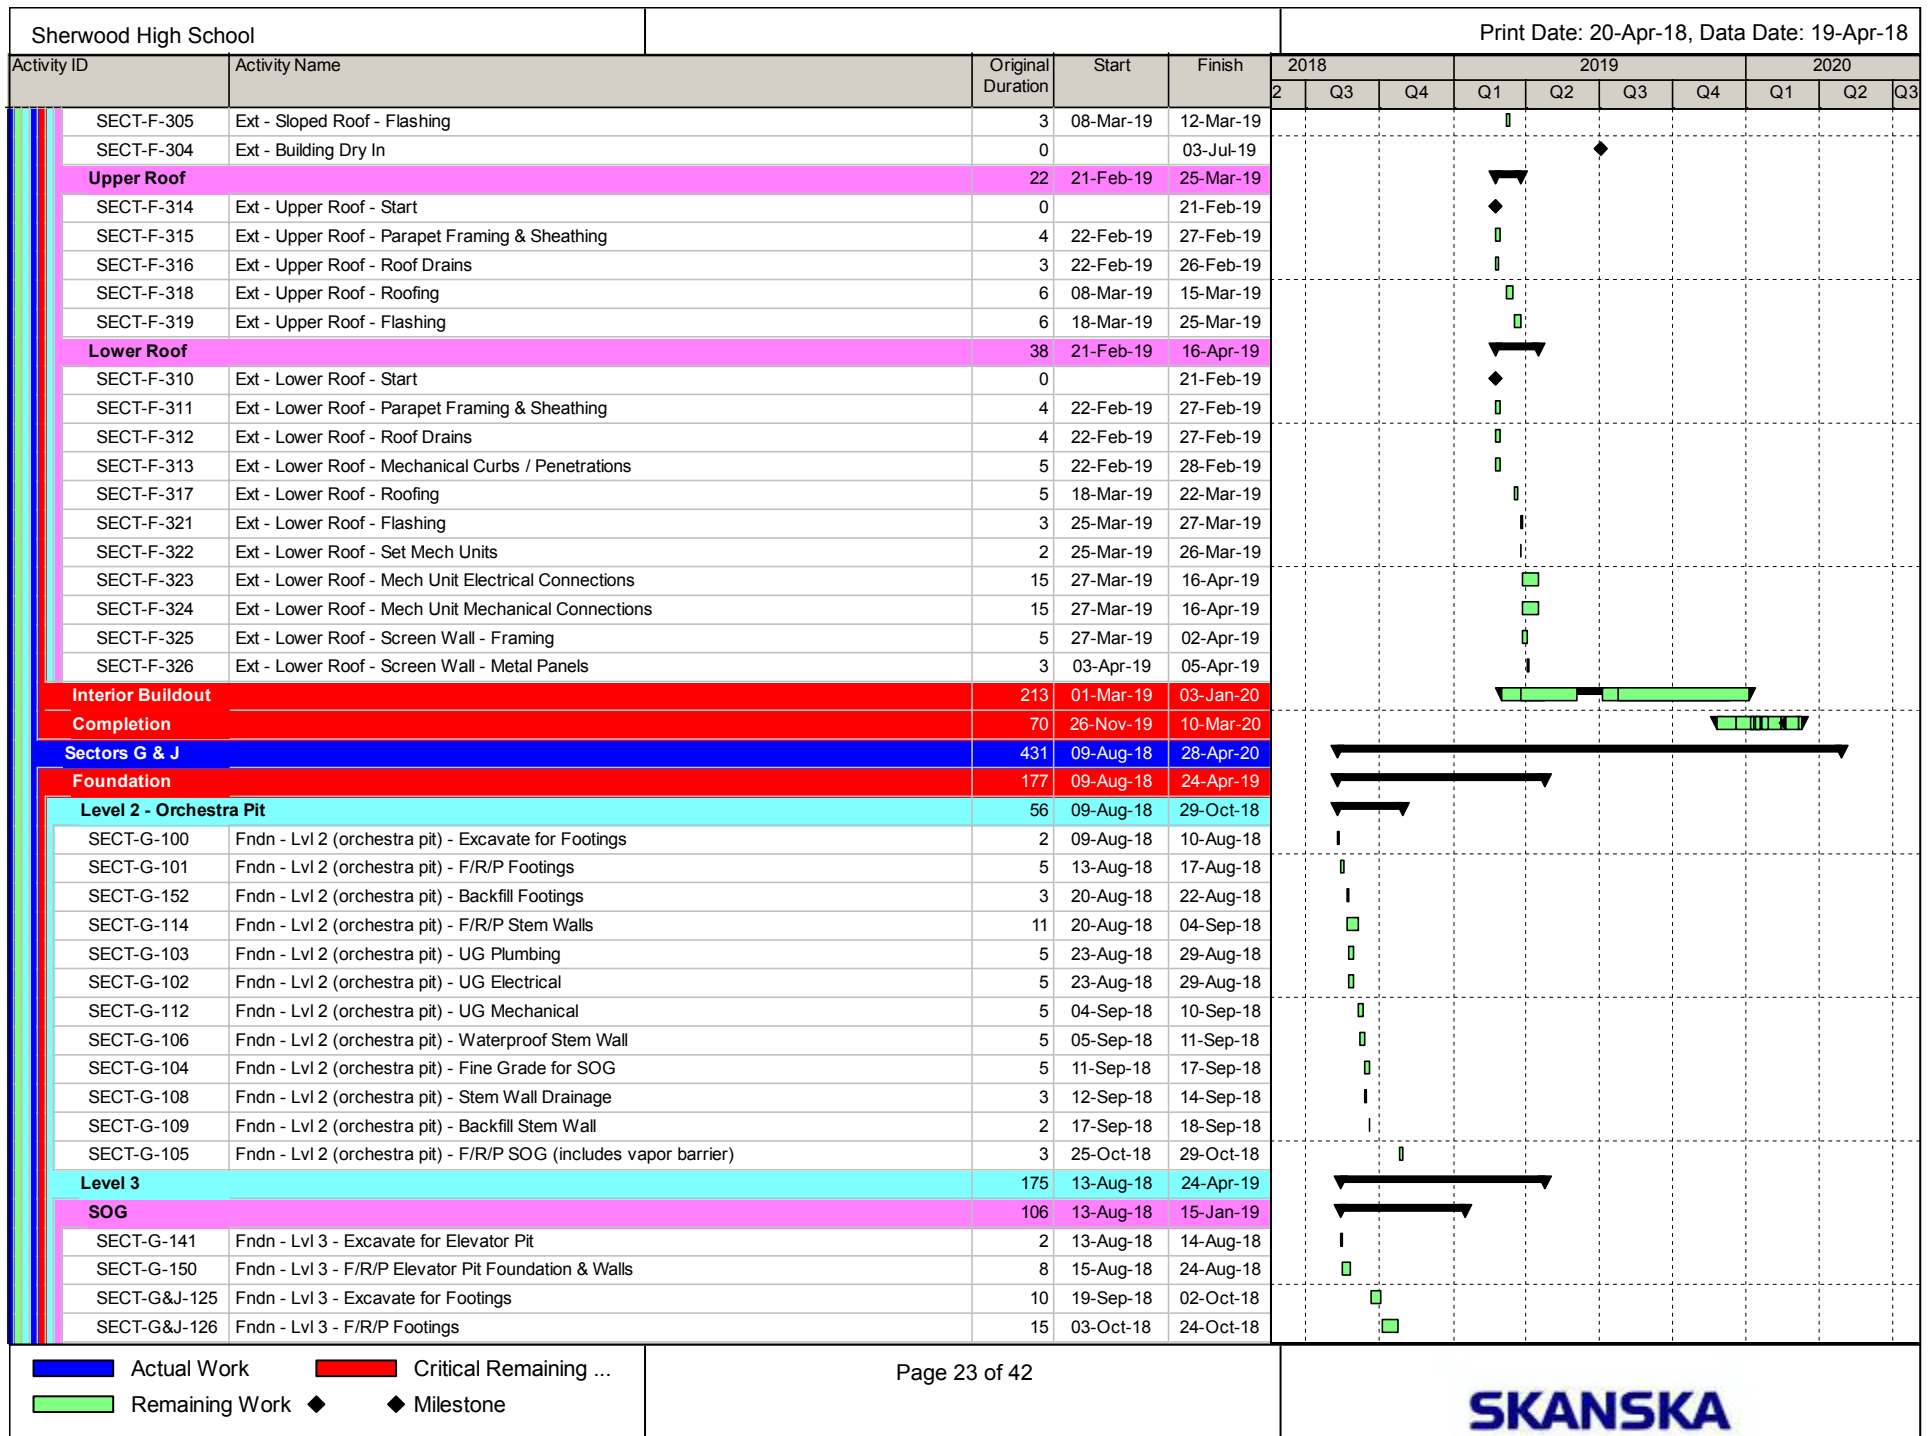


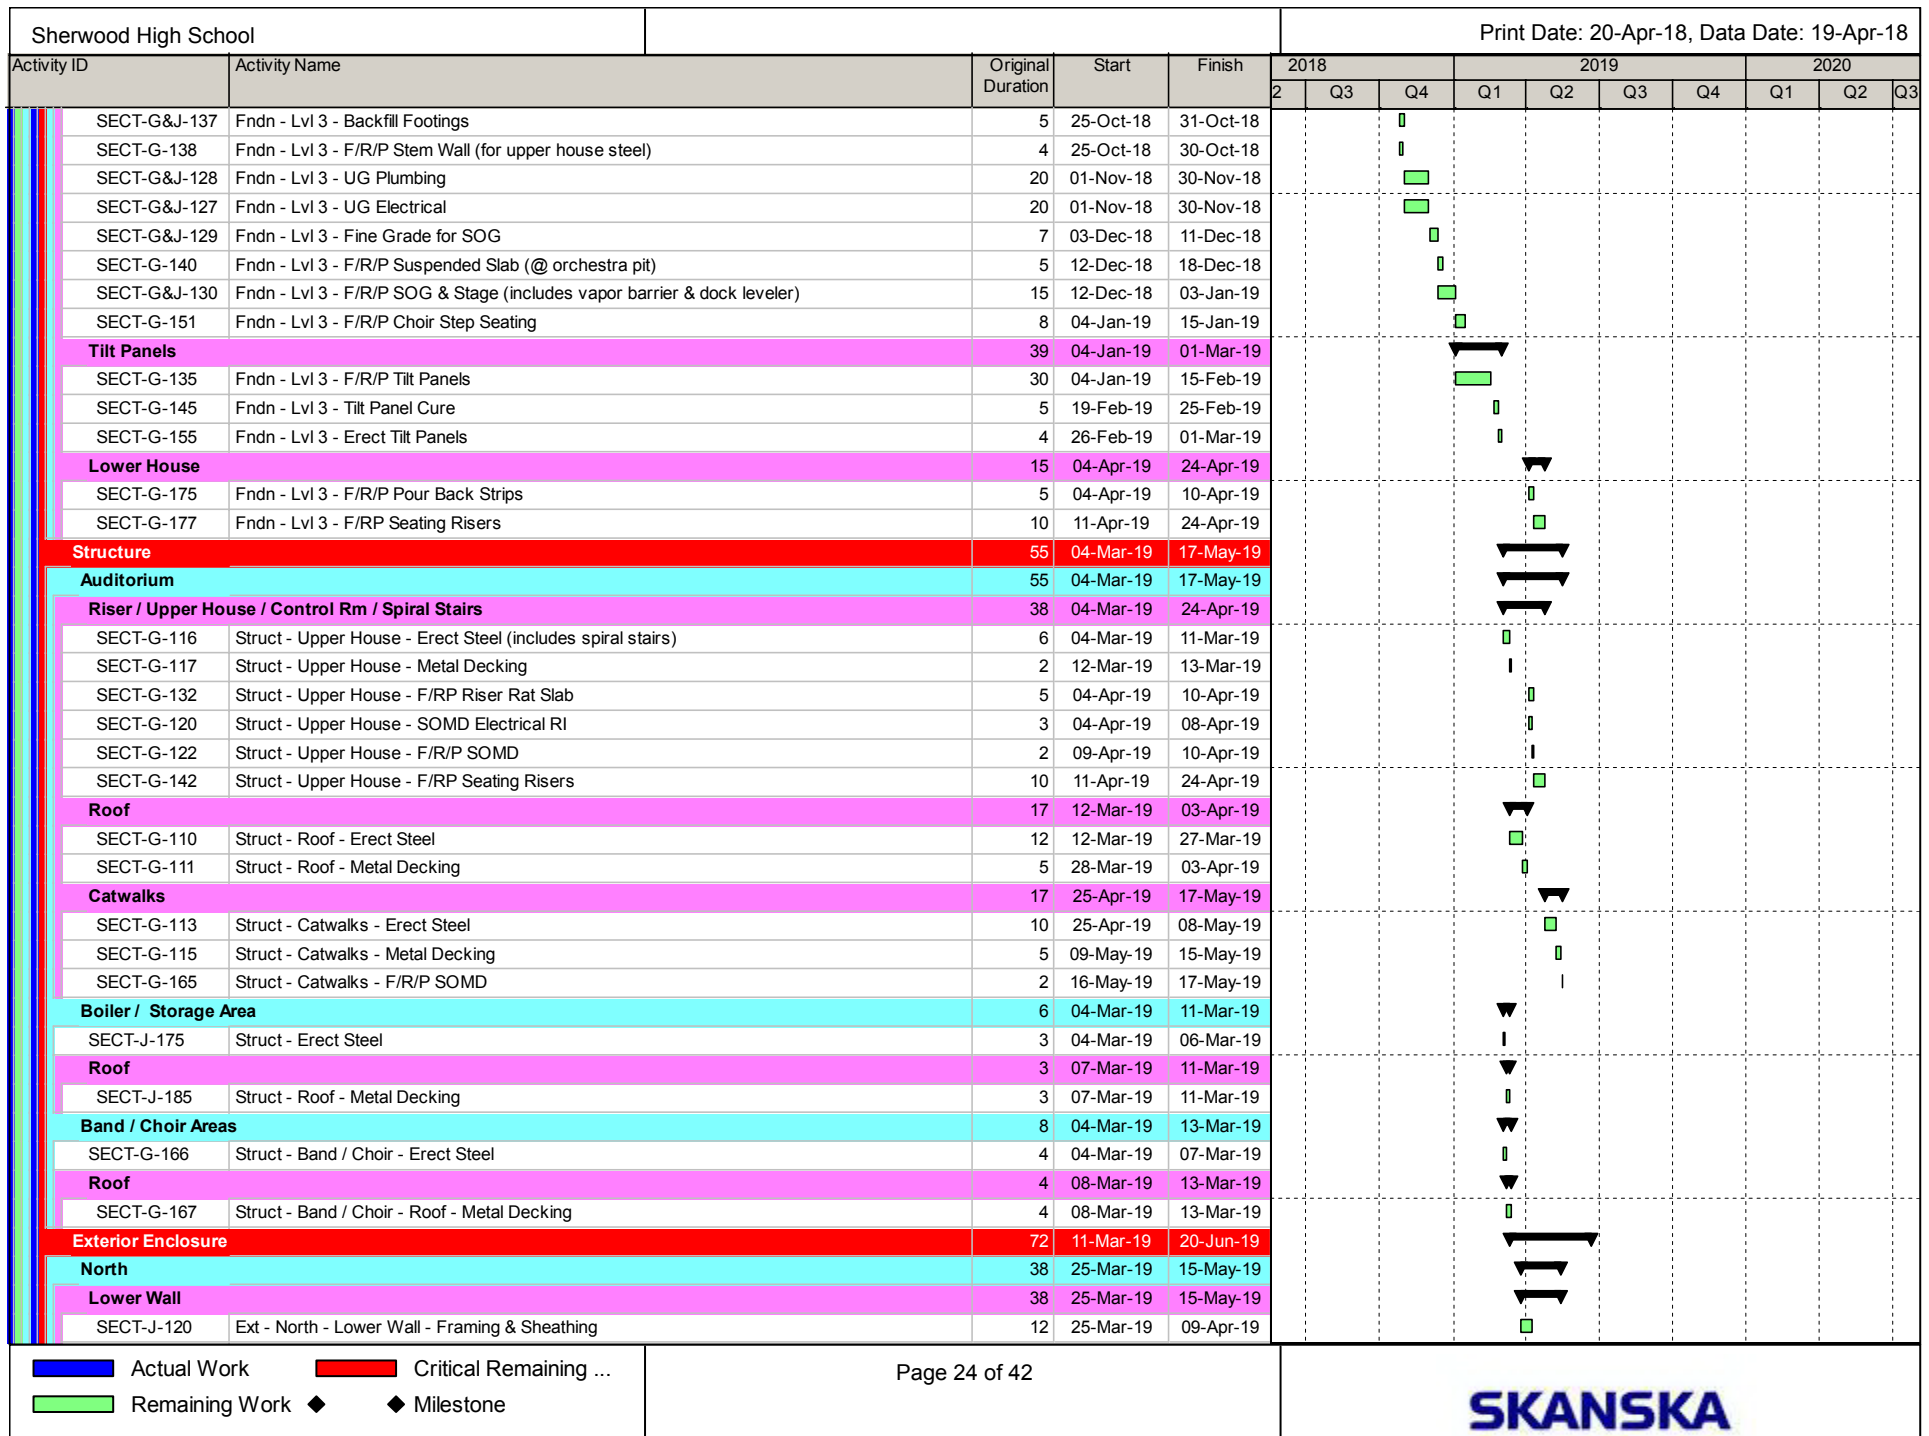

Sherwood High School						Print Date: 20-Apr-18, Data Date: 19-Apr-18								
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SECT-J-124	Ext - North - Lower Wall - WRB (includes flashings)	5	10-Apr-19	16-Apr-19										
SECT-J-125	Ext - North - Lower Wall - Exterior Glazing Systems	2	17-Apr-19	18-Apr-19										
SECT-J-129	Ext - North - Lower Wall - Brick Masonry (inc. insulation & lintels)	16	19-Apr-19	10-May-19										
SECT-J-130	Ext - North - Lower Wall - Clean & Seal	3	13-May-19	15-May-19										
SECT-J-150	Ext - North - Lower Wall - Complete	0		15-May-19										
Upper Wall		24	10-Apr-19	13-May-19										
SECT-J-121	Ext - North - Upper Wall - Framing & Sheathing	8	10-Apr-19	19-Apr-19										
SECT-J-122	Ext - North - Upper Wall - WRB (includes flashings)	6	22-Apr-19	29-Apr-19										
SECT-J-128	Ext - North - Upper Wall - Metal Panels	10	30-Apr-19	13-May-19										
SECT-J-221	Ext - North - Lower Wall - Complete	0		13-May-19										
West		40	25-Apr-19	20-Jun-19										
Lower Wall		40	25-Apr-19	20-Jun-19										
SECT-G&J-140	Ext - West - Lower Wall - Framing & Sheathing	11	25-Apr-19	09-May-19										
SECT-G&J-144	Ext - West - Lower Wall - WRB (includes flashings)	4	10-May-19	15-May-19										
SECT-G&J-145	Ext - West - Lower Wall - Exterior Glazing Systems	4	16-May-19	21-May-19										
SECT-J-140	Ext - North - Lower Wall - Roll Top Doors	6	16-May-19	23-May-19										
SECT-G&J-149	Ext - West - Lower Wall - Brick Masonry (inc. insulation & lintels)	15	22-May-19	12-Jun-19										
SECT-G&J-150	Ext - West - Lower Wall - Clean & Seal	3	13-Jun-19	17-Jun-19										
SECT-G&J-152	Ext - West - Lower Wall - Canopy Assembly	3	13-Jun-19	17-Jun-19										
SECT-G&J-153	Ext - West - Lower Wall - Canopy Roofing	3	18-Jun-19	20-Jun-19										
SECT-G&J-171	Ext - North - Lower Wall - Complete	0		20-Jun-19										
Upper Wall		16	10-May-19	03-Jun-19										
SECT-G&J-141	Ext - West - Upper Wall - Framing & Sheathing	6	10-May-19	17-May-19										
SECT-G&J-142	Ext - West - Upper Wall - WRB (includes flashings)	3	20-May-19	22-May-19										
SECT-G&J-148	Ext - West - Upper Wall - Metal Panels	7	23-May-19	03-Jun-19										
SECT-G&J-151	Ext - West - Upper Wall - Complete	0		03-Jun-19										
South		31	04-Apr-19	16-May-19										
Lower Wall		31	04-Apr-19	16-May-19										
SECT-G-421	Ext - South - Lower Wall - Framing & Sheathing	7	04-Apr-19	12-Apr-19										
SECT-G-425	Ext - South - Lower Wall - WRB (includes flashings)	4	15-Apr-19	18-Apr-19										
SECT-G-426	Ext - South - Lower Wall - Exterior Glazing Systems	4	19-Apr-19	24-Apr-19										
SECT-G-430	Ext - South - Lower Wall - Brick Masonry (inc. insulation & lintels)	10	25-Apr-19	08-May-19										
SECT-G-431	Ext - South - Lower Wall - Clean & Seal	3	09-May-19	13-May-19										
SECT-G-433	Ext - South - Lower Wall - Canopy Assembly	3	09-May-19	13-May-19										
SECT-G-434	Ext - South - Lower Wall - Canopy Roofing	3	14-May-19	16-May-19										
SECT-G-431.1	Ext - South - Lower Wall - Complete	0		16-May-19										
Upper Wall		24	15-Apr-19	16-May-19										
SECT-G-422	Ext - South - Upper Wall - Framing & Sheathing	8	15-Apr-19	24-Apr-19										
SECT-G-423	Ext - South - Upper Wall - WRB (includes flashings)	6	25-Apr-19	02-May-19										
SECT-G-429	Ext - South - Upper Wall - Metal Panels	10	03-May-19	16-May-19										
SECT-G-429.1	Ext - South - Upper Wall - Complete	0		16-May-19										
Roof		51	11-Mar-19	21-May-19										
Sloped Roof (auditorium)		34	03-Apr-19	21-May-19										

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

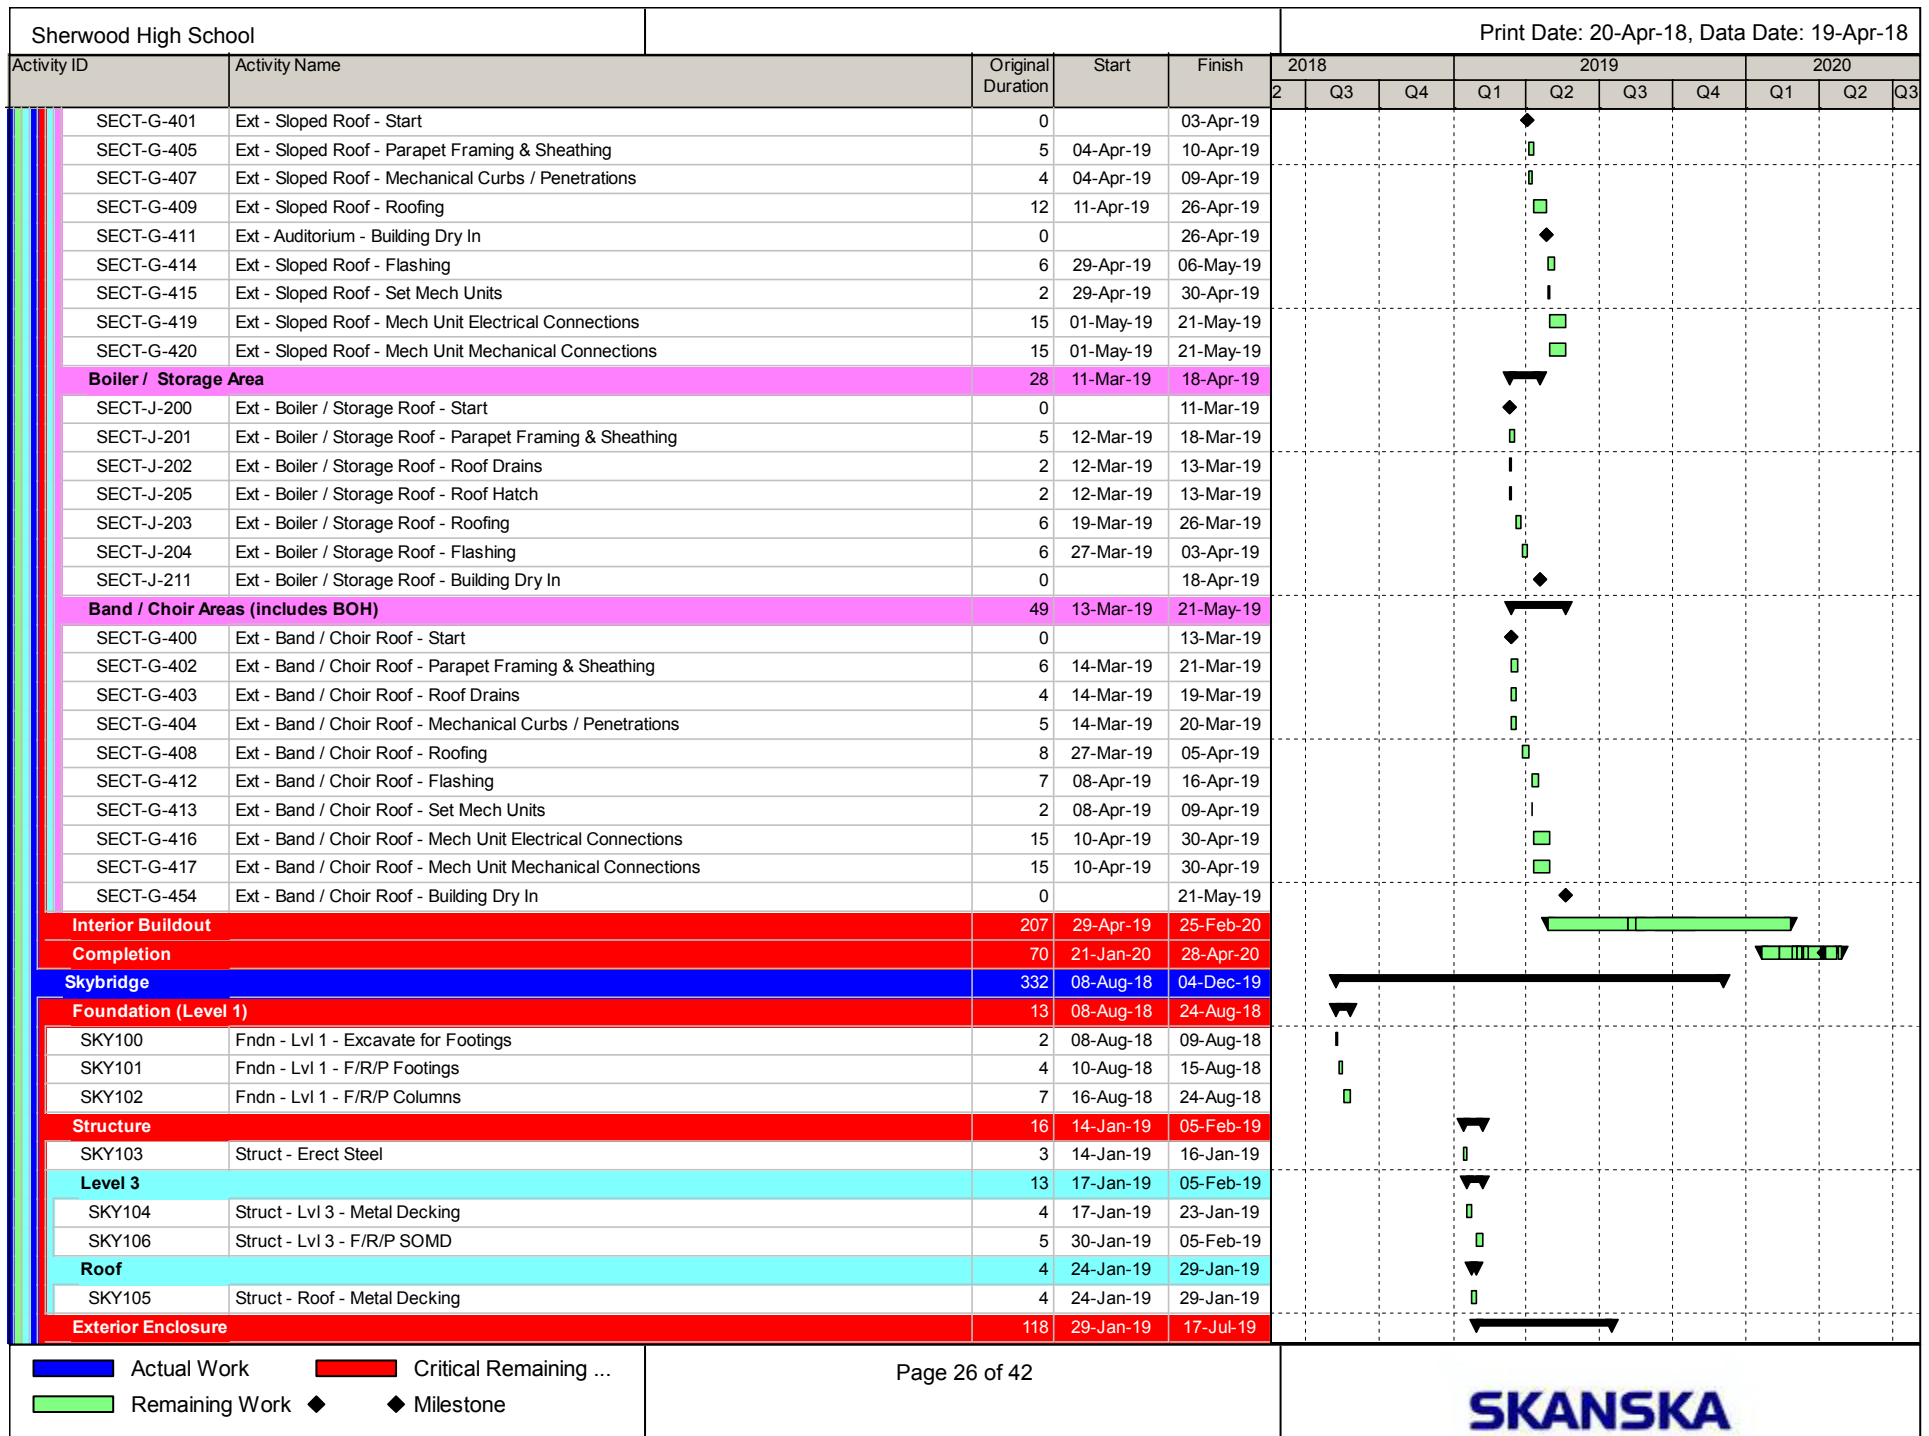

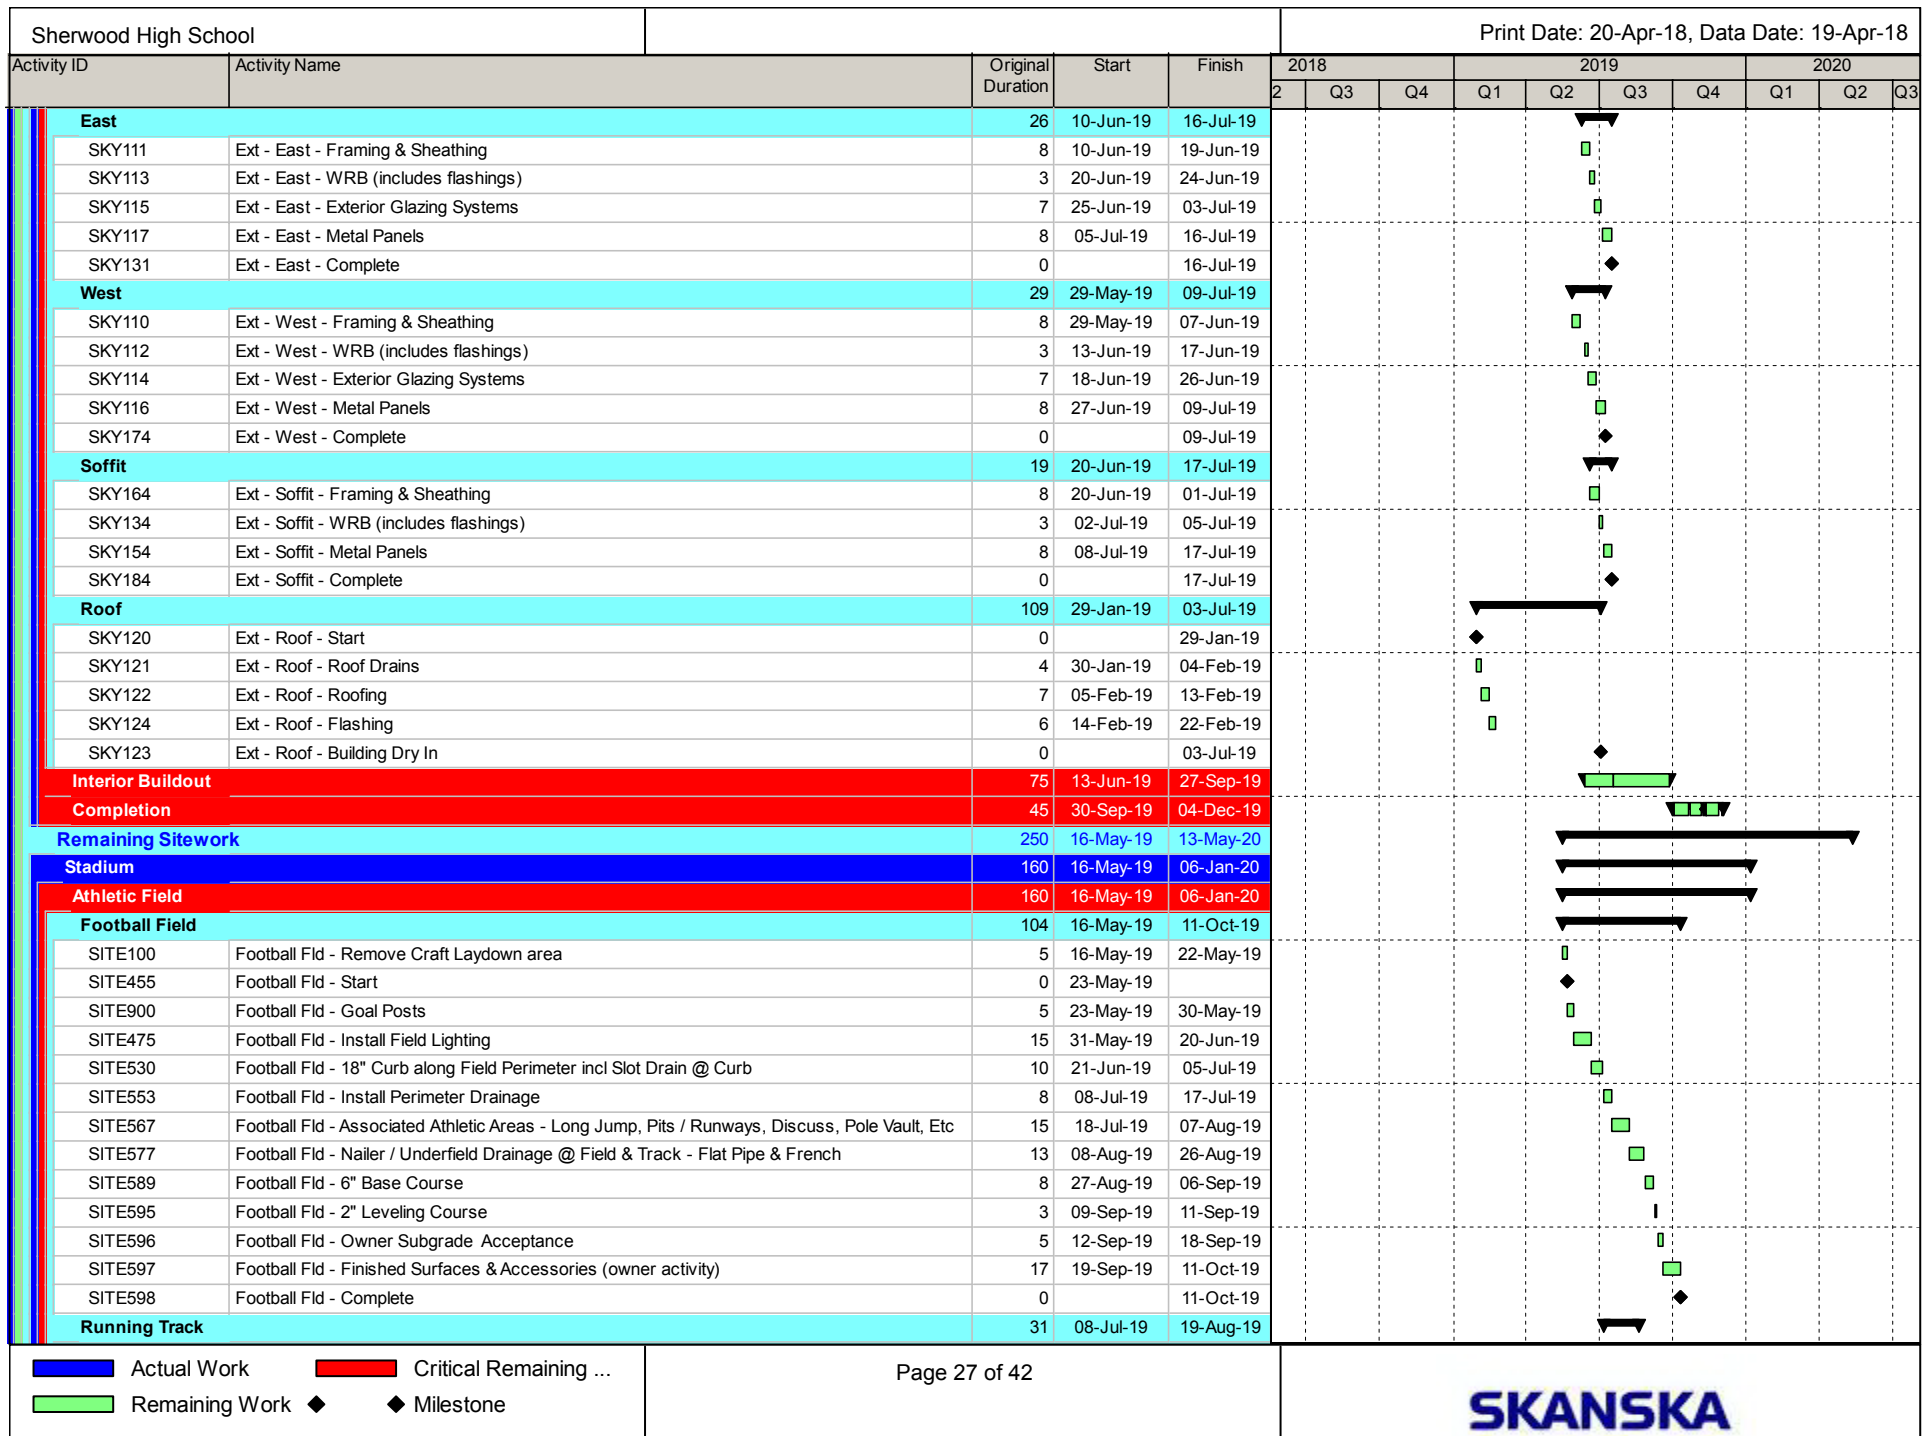

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18										
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020			
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
SITE551	Running Trk - Leveling Aggregate and Final Grading	5	08-Jul-19	12-Jul-19											
SITE552	Running Trk - Start	0	08-Jul-19												
SITE563	Running Trk - Asphalt Paving at Track	4	15-Jul-19	18-Jul-19											
SITE572	Running Trk - Resilient Track Surface	10	19-Jul-19	01-Aug-19											
SITE576	Running Trk - Paint Track Striping	5	02-Aug-19	08-Aug-19											
SITE580	Running Trk - Misc. Track Finishes	5	09-Aug-19	15-Aug-19											
SITE585	Running Trk - Contractor Prepunch	2	16-Aug-19	19-Aug-19											
SITE586	Running Trk - Complete	0		19-Aug-19											
Field Accessories (long jump, javelin, shot put)		30	20-Nov-19	06-Jan-20											
SITE1026	Fld Acc. - Field Accessories Installations	30	20-Nov-19	06-Jan-20											
SITE1016	Fld Acc. - Start	0	20-Nov-19												
SITE1036	Fld Acc. - Complete	0		06-Jan-20											
Remaining Landscape Areas		53	19-Jul-19	02-Oct-19											
SITE104	Stadium - Landscapes - Start	0	19-Jul-19												
SITE910	Stadium - Landscapes - UG Stormwater Piping	4	19-Jul-19	24-Jul-19											
SITE130	Stadium - Landscapes - F/R/P Stairs	4	25-Jul-19	30-Jul-19											
SITE131	Stadium - Landscapes - F/R/P Light Pole Bases	5	25-Jul-19	31-Jul-19											
SITE132	Stadium - Landscapes - UG Electrical	5	25-Jul-19	31-Jul-19											
SITE158	Stadium - Landscapes - Irrigation Sleeves	2	01-Aug-19	02-Aug-19											
SITE177	Stadium - Landscapes - Fine Grade for Sidewalks	6	05-Aug-19	12-Aug-19											
SITE199	Stadium - Landscapes - F/R/P Sidewalks	7	13-Aug-19	21-Aug-19											
SITE227	Stadium - Landscapes - Irrigation	10	22-Aug-19	05-Sep-19											
SITE228	Stadium - Landscapes - Set Light Fixtures / Poles	6	22-Aug-19	29-Aug-19											
SITE229	Stadium - Landscapes - Handrail	2	22-Aug-19	23-Aug-19											
SITE291	Stadium - Landscapes - Place Top Soil	4	06-Sep-19	11-Sep-19											
SITE316	Stadium - Landscapes - Planting / Seeding	10	12-Sep-19	25-Sep-19											
SITE366	Stadium - Landscapes - Contractor Prepunch	5	26-Sep-19	02-Oct-19											
SITE397	Stadium - Landscapes - Complete	0		02-Oct-19											
Outbuildings - Concessions, Restrooms, Ticketing		72	19-Jul-19	30-Oct-19											
Exterior		52	19-Jul-19	01-Oct-19											
SITE173	Outbuildings - Start	0	19-Jul-19												
SITE890	Outbuildings - Ext - Excavate Footings	3	19-Jul-19	23-Jul-19											
SITE186	Outbuildings - Ext - F/R/P Footings	5	24-Jul-19	30-Jul-19											
SITE204	Outbuildings - Ext - Plumbing Underground	8	31-Jul-19	09-Aug-19											
SITE217	Outbuildings - Ext - Electrical Underground	5	05-Aug-19	09-Aug-19											
SITE252	Outbuildings - Ext - CMU to FF	3	12-Aug-19	14-Aug-19											
SITE263	Outbuildings - Ext - F/R/P Slab	4	15-Aug-19	20-Aug-19											
SITE264	Outbuildings - Ext - Vapor Barrier	1	15-Aug-19	15-Aug-19											
SITE265	Outbuildings - Ext - Prep Slab	1	15-Aug-19	15-Aug-19											
SITE288	Outbuildings - Ext - CMU Walls	10	21-Aug-19	04-Sep-19											
SITE289	Outbuildings - Ext - Set Door Frames	1	21-Aug-19	21-Aug-19											
SITE343	Outbuildings - Ext - Install Top Plate	3	03-Sep-19	05-Sep-19											
SITE352	Outbuildings - Ext - Set Trusses	3	06-Sep-19	10-Sep-19											

Actual Work

Remaining Work


Critical Remaining ...

Milestone

Page 28 of 42

SKANSKA

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ ◆ Milestone

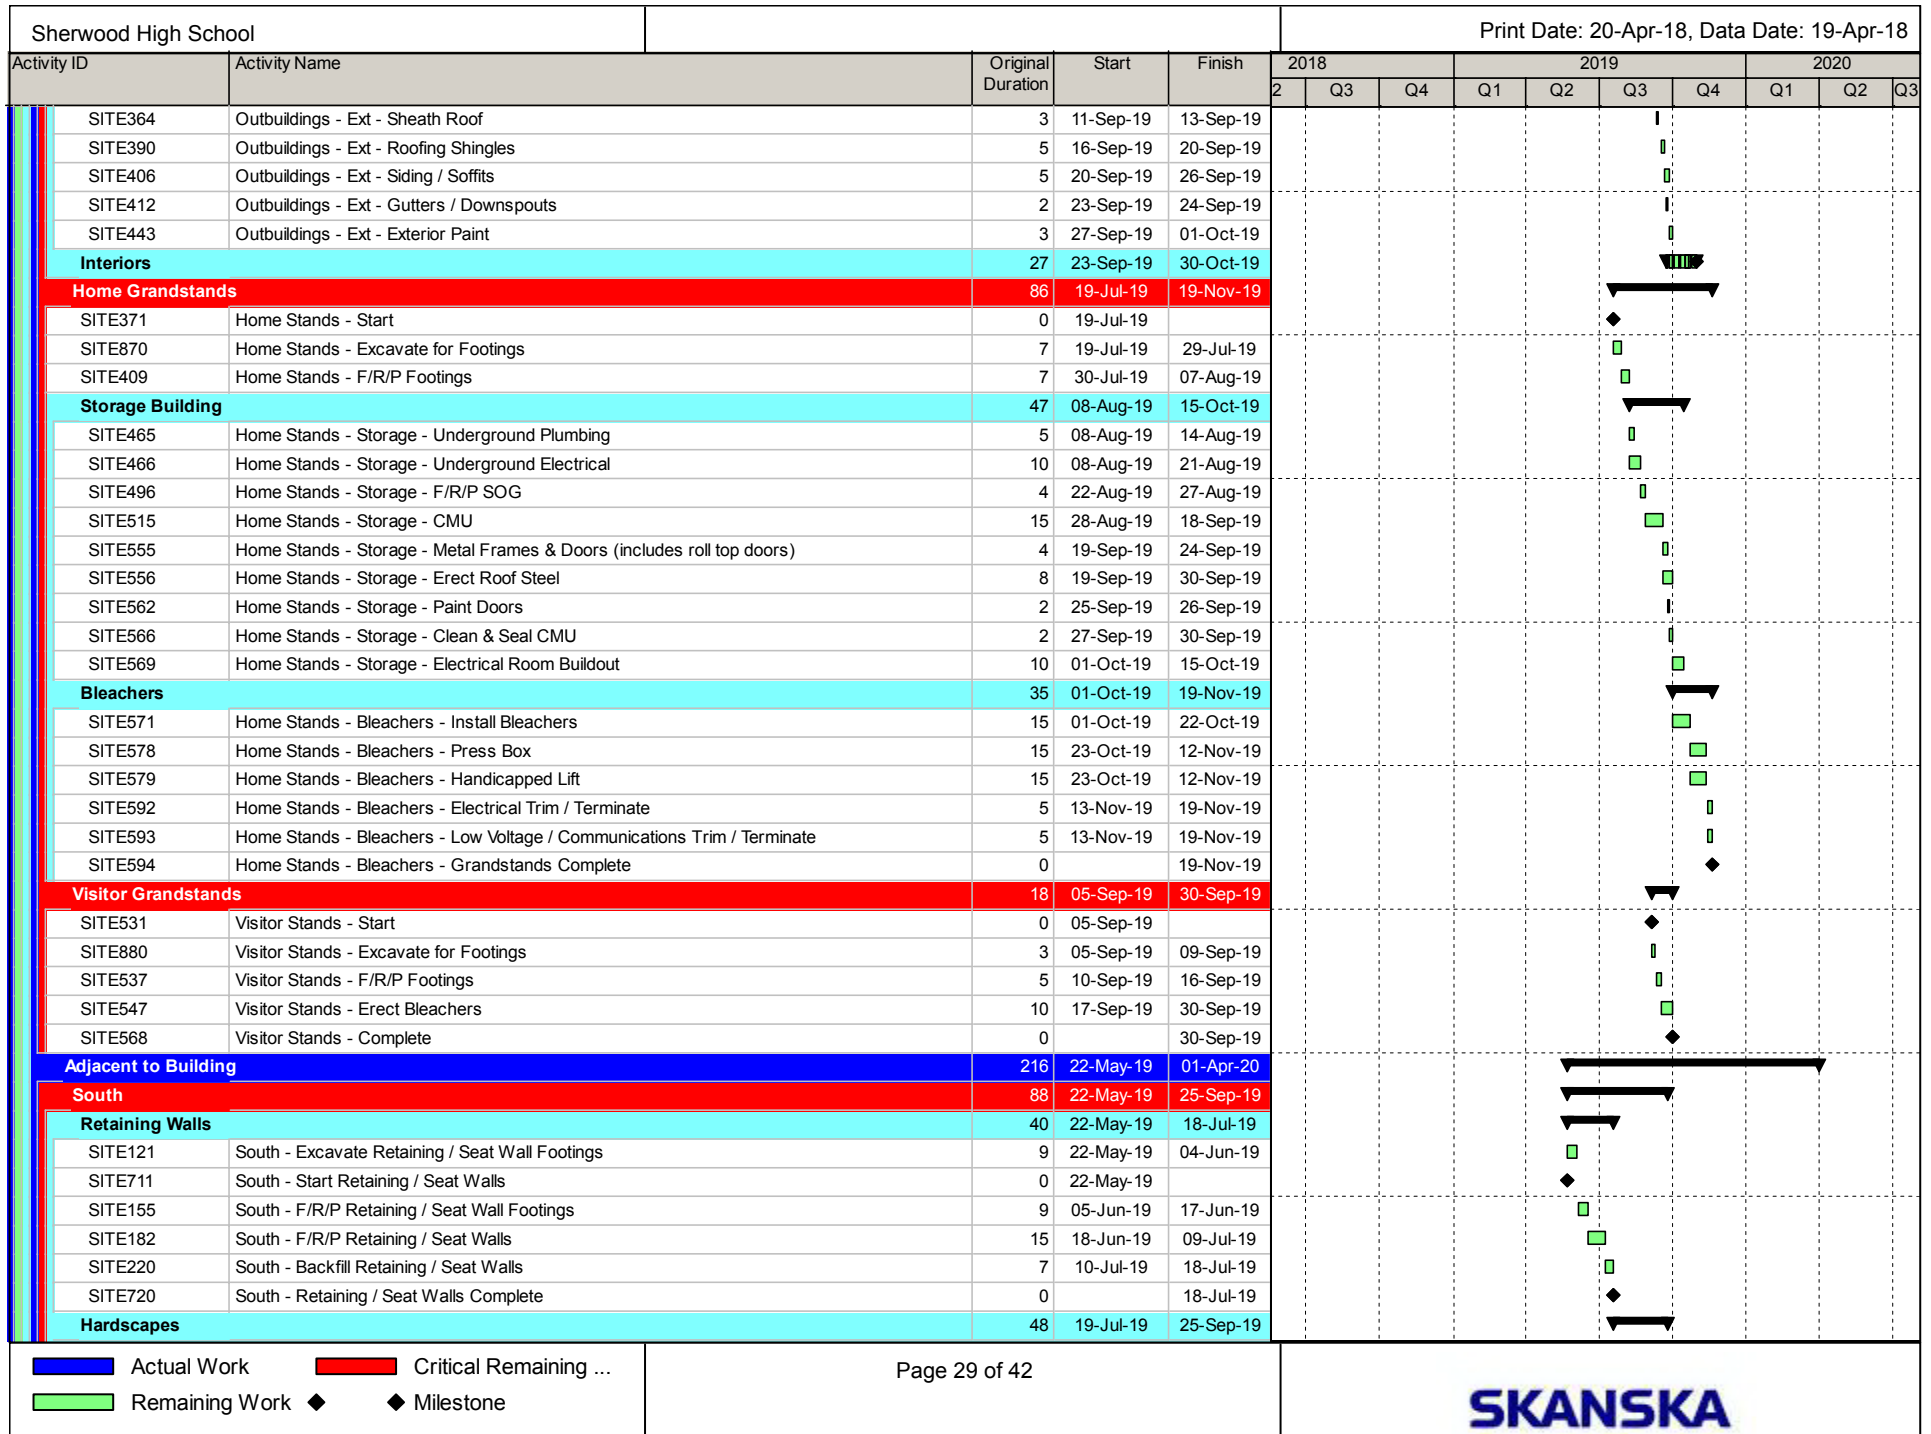

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SITE684	South - Start Hardscapes / Landscaping	0	19-Jul-19								◆			
SITE685	South - F/R/P Light Pole Bases	9	19-Jul-19	31-Jul-19							■			
SITE686	South - UG Electrical	7	19-Jul-19	29-Jul-19							■			
SITE687	South - SD Line Connections	4	19-Jul-19	24-Jul-19							■			
SITE730	South - F/R/P Stairs	5	19-Jul-19	25-Jul-19							■			
SITE693	South - Irrigation Sleeves	2	30-Jul-19	31-Jul-19										
SITE695	South - Fine Grade for Flatwork	6	01-Aug-19	08-Aug-19							■			
SITE698	South - F/R/P Sidewalks	8	09-Aug-19	20-Aug-19							■			
SITE699	South - F/R/P Concrete Patio	10	09-Aug-19	22-Aug-19							■			
SITE700	South - Irrigation	8	21-Aug-19	30-Aug-19							■			
SITE701	South - Set Light Fixtures / Poles	6	21-Aug-19	28-Aug-19							■			
SITE703	South - Handrail	5	23-Aug-19	29-Aug-19							■			
SITE704	South - Place Top Soil	2	03-Sep-19	04-Sep-19										
SITE706	South - Planting / Seeding	5	05-Sep-19	11-Sep-19							■			
SITE708	South - Accessories (bike racks, seating, garbage cans, etc.)	5	12-Sep-19	18-Sep-19							■			
SITE709	South - Contractor Prepunch	5	19-Sep-19	25-Sep-19							■			
SITE710	South - Hardscapes / Landscaping Complete	0		25-Sep-19								◆		
West		55	21-Jun-19	09-Sep-19							┌			
Utility Connections		16	21-Jun-19	15-Jul-19							└			
SITE191	West - Start Utility Connections	0	21-Jun-19								◆			
SITE212	West - UG Electrical Feeds	4	21-Jun-19	26-Jun-19							■			
SITE128	West - UG Sanitary Connection	3	21-Jun-19	25-Jun-19							■			
SITE171	West - UG Gas Connection	3	24-Jun-19	26-Jun-19							■			
SITE235	West - F/R/P Equipment Pads	2	27-Jun-19	28-Jun-19							■			
SITE250	West - Set / Make Up / Energize Transformers	10	01-Jul-19	15-Jul-19							■			
Hardscapes		51	27-Jun-19	09-Sep-19							└			
SITE920	West - Excavate for CMU Screen Wall	2	27-Jun-19	28-Jun-19							◆			
SITE654	West - Start Hardscapes / Landscaping	0	27-Jun-19								■			
SITE655	West - F/R/P Light Pole Bases	3	27-Jun-19	01-Jul-19							■			
SITE656	West - UG Site Electrical	4	27-Jun-19	02-Jul-19							■			
SITE740	West - Excavate Accessible Ramp (to footings)	1	27-Jun-19	27-Jun-19										
SITE659	West - SD Line Connections	7	28-Jun-19	09-Jul-19							■			
SITE660	West - F/R/P Accessible Ramp	6	28-Jun-19	08-Jul-19							■			
SITE930	West - F/R/P Footings for CMU Screen Wall	5	01-Jul-19	08-Jul-19							■			
SITE940	West - Screen Wall CMU	10	09-Jul-19	22-Jul-19							■			
SITE665	West - Handrail	2	09-Jul-19	10-Jul-19										
SITE667	West - Irrigation Sleeves	1	10-Jul-19	10-Jul-19										
SITE950	West - F/R/P Curbs	4	23-Jul-19	26-Jul-19							■			
SITE670	West - Fine Grade for Remaining Flatwork	5	29-Jul-19	02-Aug-19							■			
SITE672	West - F/R/P Sidewalks	4	05-Aug-19	08-Aug-19							■			
SITE673	West - F/R/P Concrete Service Enclosure Slab	3	05-Aug-19	07-Aug-19							■			
SITE960	West - Gate	5	09-Aug-19	15-Aug-19							■			
SITE675	West - Irrigation	5	09-Aug-19	15-Aug-19							■			

Actual Work

Remaining Work

Critical Remaining ...

◆

Milestone

Page 30 of 42

SKANSKA


Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18										
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020			
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
SITE676	West - Set Light Fixtures / Poles	3	09-Aug-19	13-Aug-19											
SITE680	West - Place Top Soil	1	16-Aug-19	16-Aug-19											
SITE681	West - Planting / Seeding	3	19-Aug-19	21-Aug-19											
SITE682	West - Set / Make Up Generator	10	19-Aug-19	30-Aug-19											
SITE683	West - Set Trash Compactor	2	22-Aug-19	23-Aug-19											
SITE692	West - Contractor Prepunch	5	03-Sep-19	09-Sep-19											
SITE694	West - Hardscapes / Landscaping Complete	0		09-Sep-19											
North		99	09-Jul-19	26-Nov-19											
Utility Connections		22	09-Jul-19	07-Aug-19											
SITE315	North - Start Utility Connections	0	09-Jul-19												
SITE321	North - UG Vaults / Fire & Domestic Connections	8	09-Jul-19	18-Jul-19											
SITE322	North - Grease Interceptor Vault	2	09-Jul-19	10-Jul-19											
SITE323	North - Sanitary Connections	7	09-Jul-19	17-Jul-19											
SITE331	North - Set & Connect Grease Interceptor	5	11-Jul-19	17-Jul-19											
SITE353	North - UG Stormwater Piping	10	18-Jul-19	31-Jul-19											
SITE408	North - UG CCTV Cable	5	01-Aug-19	07-Aug-19											
SITE688	North - Utility Connections Complete	0		07-Aug-19											
Main Entrance Canopy		30	08-Aug-19	19-Sep-19											
SITE860	North - Canopy - Excavate Footings	2	08-Aug-19	09-Aug-19											
SITE861	North - Canopy - F/R/P Footings	5	12-Aug-19	16-Aug-19											
SITE862	North - Canopy - Erect Steel	8	19-Aug-19	28-Aug-19											
SITE863	North - Canopy - Roofing / Sheet Metal Assembly	6	29-Aug-19	06-Sep-19											
SITE874	North - Canopy - Paint	4	09-Sep-19	12-Sep-19											
SITE864	North - Canopy - Misc Finshes	5	13-Sep-19	19-Sep-19											
Hardscapes		77	08-Aug-19	26-Nov-19											
SITE628	North - Start Hardscapes / Landscaping	0	08-Aug-19												
SITE629	North - F/R/P Stairs	8	08-Aug-19	19-Aug-19											
SITE750	North - Excavate Retaining Wall Footings	2	08-Aug-19	09-Aug-19											
SITE632	North - F/R/P Retaining Wall Footings	3	12-Aug-19	14-Aug-19											
SITE633	North - F/R/P Retaining Walls	4	15-Aug-19	20-Aug-19											
SITE635	North - Backfill Retaining Walls	1	21-Aug-19	21-Aug-19											
SITE636	North - F/R/P Light Pole Bases	8	22-Aug-19	03-Sep-19											
SITE637	North - UG Electrical	9	22-Aug-19	04-Sep-19											
SITE638	North - SD Line Connections	4	22-Aug-19	27-Aug-19											
SITE641	North - Irrigation Sleeves	2	05-Sep-19	06-Sep-19											
SITE643	North - Fine Grade for Flatwork	6	20-Sep-19	27-Sep-19											
SITE644	North - F/R/P Sidewalks	8	30-Sep-19	09-Oct-19											
SITE645	North - F/R/P Concrete Patio	10	30-Sep-19	11-Oct-19											
SITE648	North - Irrigation	10	10-Oct-19	24-Oct-19											
SITE649	North - Set Light Fixtures / Poles	6	10-Oct-19	18-Oct-19											
SITE650	North - Handrail	8	15-Oct-19	24-Oct-19											
SITE658	North - Place Top Soil	2	25-Oct-19	28-Oct-19											
SITE661	North - Planting / Seeding	6	29-Oct-19	05-Nov-19											

Actual Work Remaining Work Critical Remaining ... Milestone

Page 31 of 42

SKANSKA

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

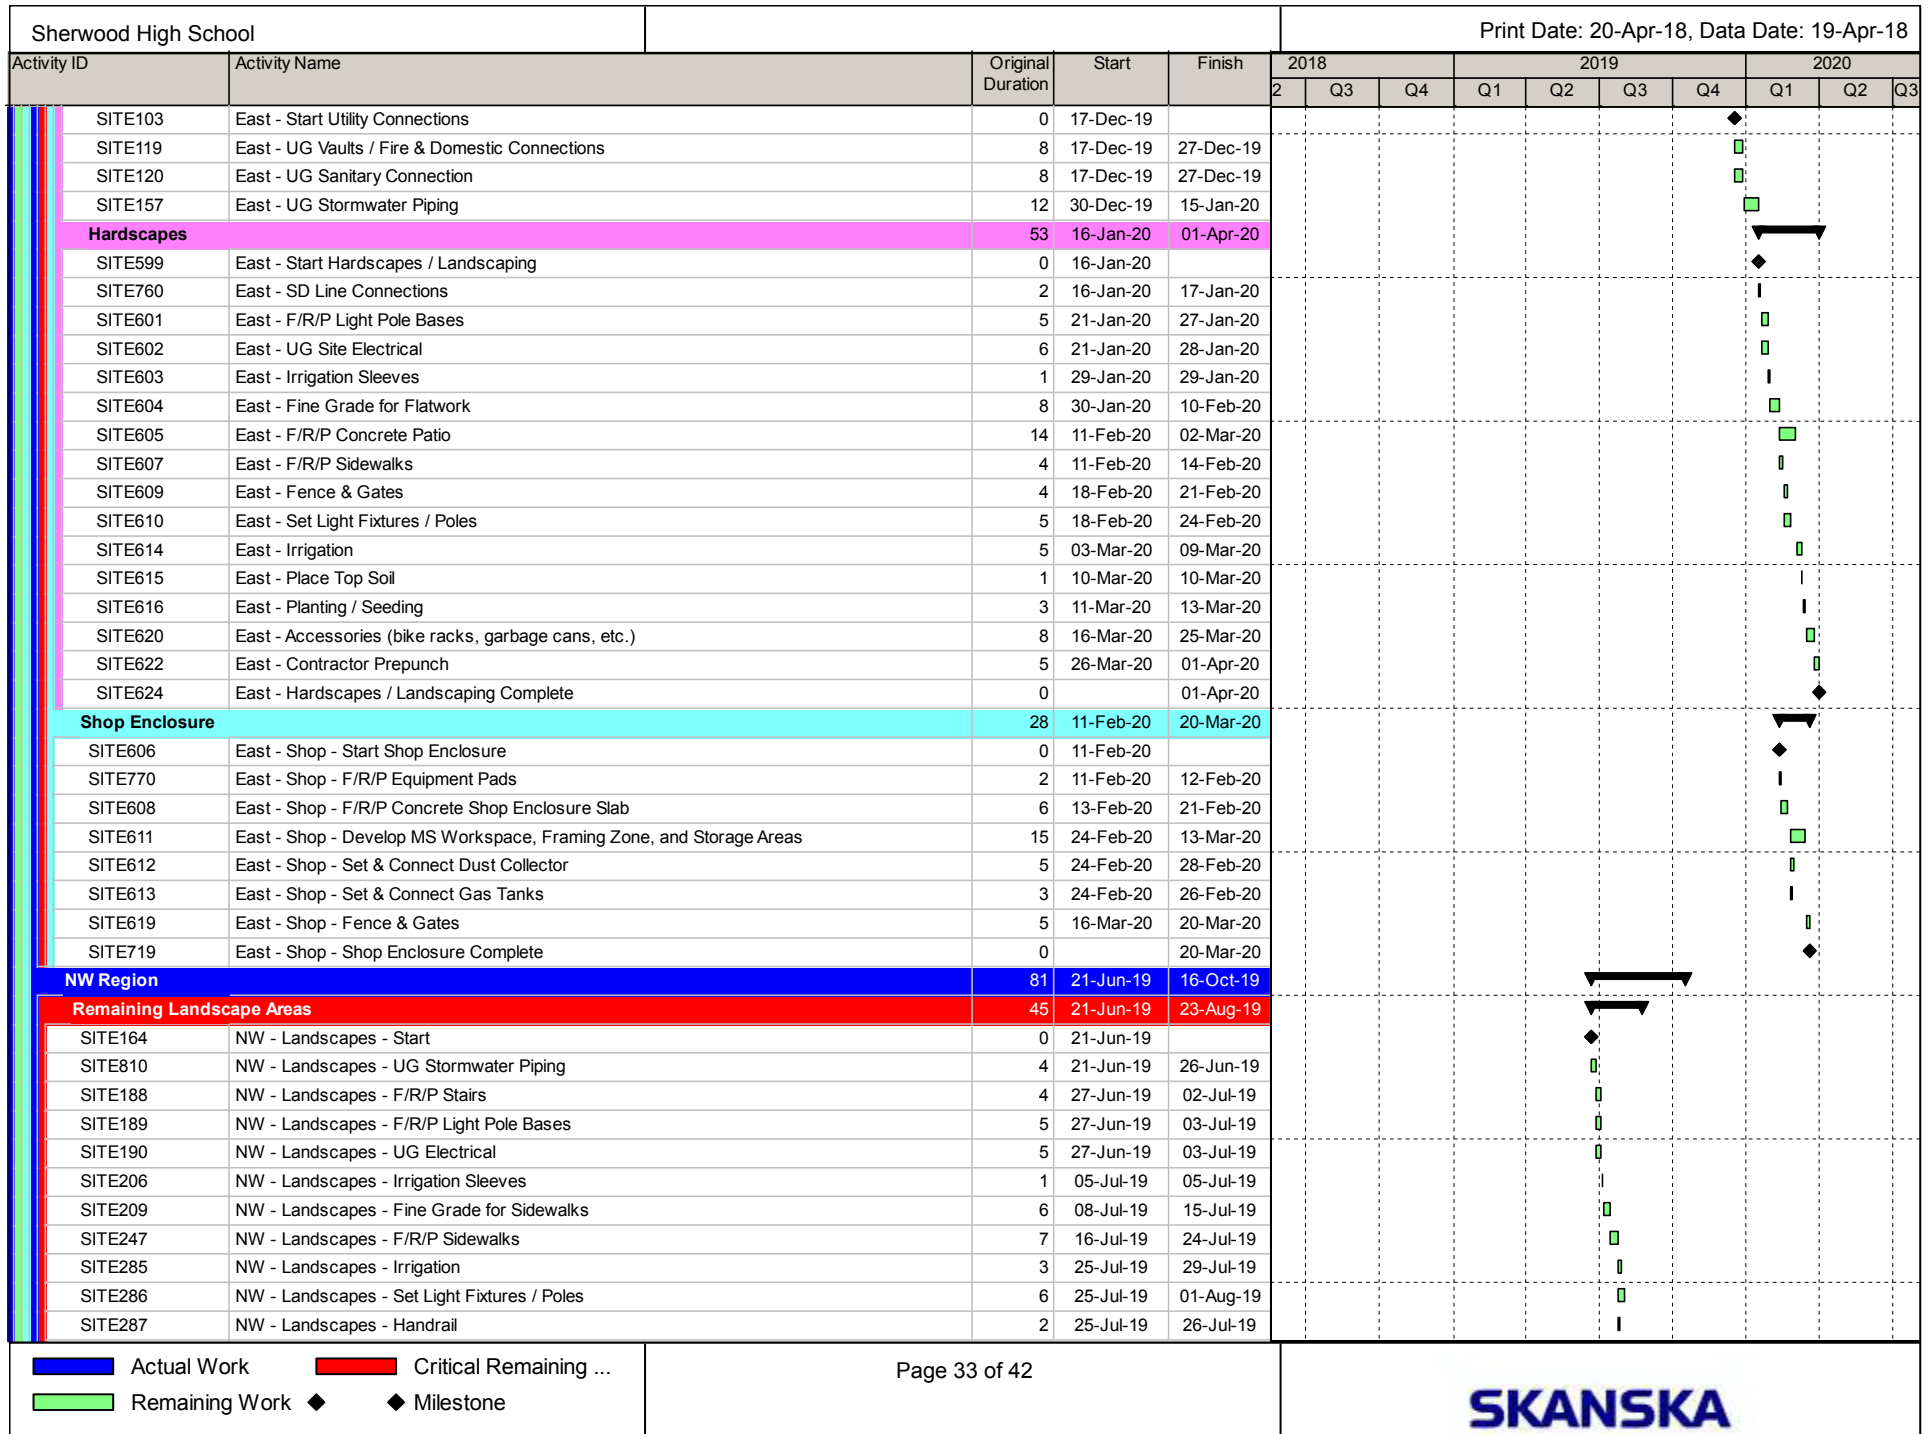

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18										
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020			
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
SITE304	NW - Landscapes - Place Top Sol	4	30-Jul-19	02-Aug-19											
SITE327	NW - Landscapes - Planting / Seeding	10	05-Aug-19	16-Aug-19											
SITE386	NW - Landscapes - Contractor Prepunch	5	19-Aug-19	23-Aug-19											
SITE407	NW - Landscapes - Complete	0		23-Aug-19											
NW Multi-Use Field		63	21-Jun-19	19-Sep-19											
SITE215	NW - Multi-Use - Start Hardscapes	0	21-Jun-19												
SITE800	NW - Multi-Use - Storm Drainage	5	21-Jun-19	27-Jun-19											
SITE249	NW - Multi-Use - Establish Subgrade	2	28-Jun-19	01-Jul-19											
SITE256	NW - Multi-Use - Storage - Excavate for Footings / SOG	1	02-Jul-19	02-Jul-19											
SITE257	NW - Multi-Use - Set Sport Light Pole Bases	5	02-Jul-19	09-Jul-19											
SITE258	NW - Multi-Use - Site Electrical	8	02-Jul-19	12-Jul-19											
SITE262	NW - Multi-Use - Storage - F/R/P Footings / SOG	2	03-Jul-19	05-Jul-19											
SITE277	NW - Multi-Use - Storage - CMU	5	08-Jul-19	12-Jul-19											
SITE307	NW - Multi-Use - Storage - Metal Frames & Doors	1	15-Jul-19	15-Jul-19											
SITE308	NW - Multi-Use - Storage - Erect Roof Steel	2	15-Jul-19	16-Jul-19											
SITE309	NW - Multi-Use - Tennis Cts - Installation	15	15-Jul-19	02-Aug-19											
SITE310	NW - Multi-Use - Field Drainage	10	15-Jul-19	26-Jul-19											
SITE314	NW - Multi-Use - Storage - Paint Doors	1	16-Jul-19	16-Jul-19											
SITE319	NW - Multi-Use - Storage - Interiors	10	17-Jul-19	30-Jul-19											
SITE320	NW - Multi-Use - Storage - Clean & Seal CMU	1	17-Jul-19	17-Jul-19											
SITE357	NW - Multi-Use - Fine Grade Subgrade	4	29-Jul-19	01-Aug-19											
SITE391	NW - Multi-Use - Set Sport Light Poles	3	02-Aug-19	06-Aug-19											
SITE401	NW - Multi-Use - Engineered Soil	3	07-Aug-19	09-Aug-19											
SITE414	NW - Multi-Use - Natural Turf	10	12-Aug-19	23-Aug-19											
SITE478	NW - Multi-Use - Accessories (bike racks, seating, garbage cans, etc.)	3	26-Aug-19	28-Aug-19											
SITE479	NW - Multi-Use - Landscaping	5	26-Aug-19	30-Aug-19											
SITE480	NW - Multi-Use - Field Lighting	5	26-Aug-19	30-Aug-19											
SITE495	NW - Multi-Use - Fence	8	03-Sep-19	12-Sep-19											
SITE525	NW - Multi-Use - Contractor Prepunch	5	13-Sep-19	19-Sep-19											
SITE536	NW - Multi-Use - Hardscapes Complete	0		19-Sep-19											
Parking		65	21-Jun-19	23-Sep-19											
Lot 1		54	21-Jun-19	06-Sep-19											
SITE115	NW - Parking 1 - Start	0	21-Jun-19												
SITE116	NW - Parking 1 - Prep Subgrade	5	21-Jun-19	27-Jun-19											
SITE150	NW - Parking 1 - Storm Drainage	5	28-Jun-19	05-Jul-19											
SITE169	NW - Parking 1 - Electrical / Telecom	5	08-Jul-19	12-Jul-19											
SITE195	NW - Parking 1 - Excavate for Curbs & Sidewalks	4	15-Jul-19	18-Jul-19											
SITE207	NW - Parking 1 - Irrigation Sleeves	1	19-Jul-19	19-Jul-19											
SITE211	NW - Parking 1 - F/R/P Curbs & Islands	6	22-Jul-19	29-Jul-19											
SITE248	NW - Parking 1 - F/R/P Light Pole Bases	5	30-Jul-19	05-Aug-19											
SITE276	NW - Parking 1 - F/R/P Sidewalks	5	06-Aug-19	12-Aug-19											
SITE306	NW - Parking 1 - Fine Grade Parking Lot Sub Base	4	13-Aug-19	16-Aug-19											
SITE329	NW - Parking 1 - Paving - Lift 1	1	19-Aug-19	19-Aug-19											

Actual Work Remaining Work Critical Remaining ... Milestone

Page 34 of 42

SKANSKA

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18										
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020			
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
SITE554	NW - Rdwy - Complete	0		16-Oct-19											
Roadways		123	09-Jul-19	03-Jan-20											
SW Haide Rd		19	09-Jul-19	02-Aug-19											
RDWY112	SW Haide Rd - Fine Grade for Sidewalks	5	09-Jul-19	15-Jul-19											
RDWY109	SW Haide Rd - Asphalt - Lift 2	2	09-Jul-19	10-Jul-19											
RDWY139	SW Haide Rd - Start Finish Work	0	09-Jul-19												
RDWY111	SW Haide Rd - Set Light Poles	5	11-Jul-19	17-Jul-19											
RDWY110	SW Haide Rd - Landscaping @ Planter Strip	8	11-Jul-19	22-Jul-19											
RDWY113	SW Haide Rd - F/R/P Sidewalks	15	11-Jul-19	31-Jul-19											
RDWY114	SW Haide Rd - Striping	2	23-Jul-19	24-Jul-19											
RDWY115	SW Haide Rd - Signage	2	01-Aug-19	02-Aug-19											
RDWY116	SW Haide Rd - Finish Work Complete	0		02-Aug-19											
Road A		12	17-Dec-19	03-Jan-20											
RDWY126	Road A - Landscaping @ Planter Strip	10	17-Dec-19	31-Dec-19											
RDWY131	Road A - Signage	2	17-Dec-19	18-Dec-19											
RDWY136	Road A - Start Finish Work	0	17-Dec-19												
RDWY130	Road A - Striping	2	02-Jan-20	03-Jan-20											
RDWY132	Road A - Finish Work Complete	0		03-Jan-20											
SW Region		61	17-Dec-19	16-Mar-20											
W Parking Lot		12	17-Dec-19	03-Jan-20											
SITE347	SW - Parking - Landscaping	7	17-Dec-19	26-Dec-19											
SITE600	SW - Parking - Start Finish Work	0	17-Dec-19												
SITE380	SW - Parking - Striping	2	27-Dec-19	30-Dec-19											
SITE381	SW - Parking - Signage	2	27-Dec-19	30-Dec-19											
SITE382	SW - Parking - Set Light Poles / Electrical Trim	5	27-Dec-19	03-Jan-20											
SITE383	SW - Parking - Accessories (bike racks)	2	27-Dec-19	30-Dec-19											
SITE404	SW - Parking - Finish Work Complete	0		03-Jan-20											
Roadway		41	17-Dec-19	14-Feb-20											
SITE111	SW - Rdwy - Start	0	17-Dec-19												
SITE112	SW - Rdwy - Prep Subgrade	5	17-Dec-19	23-Dec-19											
SITE149	SW - Rdwy - F/R/P Light Pole Bases	2	24-Dec-19	26-Dec-19											
SITE154	SW - Rdwy - UG Electrical	5	27-Dec-19	03-Jan-20											
SITE180	SW - Rdwy - Fine Grade for Curbs & Sidewalks	3	06-Jan-20	08-Jan-20											
SITE193	SW - Rdwy - F/R/P Curbs	7	09-Jan-20	17-Jan-20											
SITE218	SW - Rdwy - F/R/P Sidewalks	7	21-Jan-20	29-Jan-20											
SITE260	SW - Rdwy - Fine Grade for Asphalt	2	30-Jan-20	31-Jan-20											
SITE268	SW - Rdwy - Adjust Manhole Covers	1	31-Jan-20	31-Jan-20											
SITE275	SW - Rdwy - Asphalt	2	03-Feb-20	04-Feb-20											
SITE282	SW - Rdwy - Set Light Poles	3	05-Feb-20	07-Feb-20											
SITE283	SW - Rdwy - Signage	2	05-Feb-20	06-Feb-20											
SITE284	SW - Rdwy - Striping	1	05-Feb-20	05-Feb-20											
SITE303	SW - Rdwy - Contractor Prepunch	5	10-Feb-20	14-Feb-20											
SITE333	SW - Rdwy - Complete	0		14-Feb-20											

Actual Work

Remaining Work

Critical Remaining ...

Milestone

Page 36 of 42

SKANSKA

 Actual Work
 Critical Remaining ...
 Remaining Work
 Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18									
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020		
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SITE271	SE - Rdwy - Set Light Poles	3	19-Dec-19	23-Dec-19										
SITE272	SE - Rdwy - Signage	1	19-Dec-19	19-Dec-19										
SITE273	SE - Rdwy - Striping	1	19-Dec-19	19-Dec-19										
SITE293	SE - Rdwy - Contractor Prepunch	5	24-Dec-19	31-Dec-19										
SITE325	SE - Rdwy - Finish Work Complete	0		31-Dec-19										
Remaining Landscape Areas		53	17-Dec-19	04-Mar-20										
SITE105	SE - Landscapes - Start	0	17-Dec-19											
SITE850	SE - Landscapes - UG Stormwater Piping	4	17-Dec-19	20-Dec-19										
SITE134	SE - Landscapes - F/R/P Stairs	4	23-Dec-19	27-Dec-19										
SITE135	SE - Landscapes - F/R/P Light Pole Bases	5	23-Dec-19	30-Dec-19										
SITE136	SE - Landscapes - UG Electrical	5	23-Dec-19	30-Dec-19										
SITE159	SE - Landscapes - Irrigation Sleeves	2	31-Dec-19	02-Jan-20										
SITE178	SE - Landscapes - Fine Grade for Sidewalks	6	03-Jan-20	10-Jan-20										
SITE200	SE - Landscapes - F/R/P Sidewalks	7	13-Jan-20	22-Jan-20										
SITE230	SE - Landscapes - Irrigation	10	23-Jan-20	05-Feb-20										
SITE231	SE - Landscapes - Set Light Fixtures / Poles	6	23-Jan-20	30-Jan-20										
SITE232	SE - Landscapes - Handrail	2	23-Jan-20	24-Jan-20										
SITE292	SE - Landscapes - Place Top Soil	4	06-Feb-20	11-Feb-20										
SITE317	SE - Landscapes - Planting / Seeding	10	12-Feb-20	26-Feb-20										
SITE367	SE - Landscapes - Contractor Prepunch	5	27-Feb-20	04-Mar-20										
SITE398	SE - Landscapes - Complete	0		04-Mar-20										
SE Multi-Use Field		60	17-Dec-19	13-Mar-20										
SITE241	SE - Multi-Use - Start Hardscapes	0	17-Dec-19											
SITE840	SE - Multi-Use - Storm Drainage	5	17-Dec-19	23-Dec-19										
SITE266	SE - Multi-Use - Establish Subgrade	2	24-Dec-19	26-Dec-19										
SITE279	SE - Multi-Use - Set Sport Light Pole Bases	5	27-Dec-19	03-Jan-20										
SITE280	SE - Multi-Use - Site Electrical	8	27-Dec-19	08-Jan-20										
SITE326	SE - Multi-Use - Field Drainage	10	09-Jan-20	23-Jan-20										
SITE384	SE - Multi-Use - Fine Grade Subgrade	4	24-Jan-20	29-Jan-20										
SITE405	SE - Multi-Use - Engineered Soil	3	30-Jan-20	03-Feb-20										
SITE418	SE - Multi-Use - Natural Turf	10	04-Feb-20	18-Feb-20										
SITE486	SE - Multi-Use - Accessories (bike racks, seating, garbage cans, etc.)	3	19-Feb-20	21-Feb-20										
SITE487	SE - Multi-Use - Landscaping	5	19-Feb-20	25-Feb-20										
SITE488	SE - Multi-Use - Field Lighting	5	19-Feb-20	25-Feb-20										
SITE497	SE - Multi-Use - Fence	8	26-Feb-20	06-Mar-20										
SITE570	SE - Multi-Use - Contractor Prepunch	5	09-Mar-20	13-Mar-20										
SITE575	SE - Multi-Use - Hardscapes Complete	0		13-Mar-20										
Baseball Fields		71	17-Dec-19	30-Mar-20										
Varsity (Primary)		71	17-Dec-19	30-Mar-20										
SITE741	SE - V - Baseball Fields - Start Finish Work	0	17-Dec-19											
SITE427	SE - V - Baseball Fields - UG Site Electrical	9	17-Dec-19	30-Dec-19										
SITE431	SE - V - Baseball Fields - Set Sport Light Pole Bases	5	17-Dec-19	23-Dec-19										
SITE467	SE - V - Baseball Fields - Finegrade for Sidewalks	6	24-Dec-19	02-Jan-20										

■ Actual Work
 ■ Critical Remaining ...
 ■ Remaining Work
 ◆ Milestone

Sherwood High School					Print Date: 20-Apr-18, Data Date: 19-Apr-18											
Activity ID	Activity Name	Original Duration	Start	Finish	2018			2019				2020				
					2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3		
SITE482	SE - V - Baseball Fields - SD Lines / Ball Field Drainage (perf lines)	15	31-Dec-19	22-Jan-20												
SITE523	SE - V - Baseball Fields - F/R/P Hardscapes	8	16-Jan-20	28-Jan-20												
SITE534	SE - V - Baseball Fields - Outfield Top Soil	3	23-Jan-20	27-Jan-20												
SITE540	SE - V - Baseball Fields - Irrigation	5	28-Jan-20	03-Feb-20												
SITE543	SE - V - Baseball Fields - Fencing	10	29-Jan-20	11-Feb-20												
SITE549	SE - V - Baseball Fields - Infield Soil	2	04-Feb-20	05-Feb-20												
SITE559	SE - V - Baseball Fields - Warning Track Install	12	06-Feb-20	24-Feb-20												
SITE564	SE - V - Baseball Fields - Accessories (bike racks, seating, garbage cans, etc.)	3	12-Feb-20	14-Feb-20												
SITE574	SE - V - Baseball Fields - Natural Turf	15	25-Feb-20	16-Mar-20												
SITE582	SE - V - Baseball Fields - Bases	2	17-Mar-20	18-Mar-20												
SITE583	SE - V - Baseball Fields - Field Lighting	5	17-Mar-20	23-Mar-20												
SITE588	SE - V - Baseball Fields - Contractor Prepunch	5	24-Mar-20	30-Mar-20												
SITE591	SE - V - Baseball Fields - Finish Work Complete	0		30-Mar-20												
Dugouts		21	17-Dec-19	16-Jan-20												
SITE428	SE - V - Baseball Fields - Dugouts - Excavate for Footings / SOG	2	17-Dec-19	18-Dec-19												
SITE444	SE - V - Baseball Fields - Dugouts - F/R/P Footings / SOG	4	19-Dec-19	24-Dec-19												
SITE472	SE - V - Baseball Fields - Dugouts - CMU	10	26-Dec-19	09-Jan-20												
SITE506	SE - V - Baseball Fields - Dugouts - Erect Roof Steel	3	10-Jan-20	14-Jan-20												
SITE507	SE - V - Baseball Fields - Dugouts - Clean & Seal CMU	2	10-Jan-20	13-Jan-20												
SITE520	SE - V - Baseball Fields - Dugouts - Benches	2	15-Jan-20	16-Jan-20												
Pressbox / Restrooms		50	17-Dec-19	28-Feb-20												
SITE429	SE - V - Baseball Fields - Press / RR - Build Press Box / Restrooms	50	17-Dec-19	28-Feb-20												
Batting Cage		23	17-Dec-19	21-Jan-20												
SITE430	SE - V - Baseball Fields - Batting Cage - Excavate for Footings / SOG	1	17-Dec-19	17-Dec-19												
SITE434	SE - V - Baseball Fields - Batting Cage - UG Electrical	3	18-Dec-19	20-Dec-19												
SITE460	SE - V - Baseball Fields - Batting Cage - F/R/P Footing / SOG	5	23-Dec-19	30-Dec-19												
SITE483	SE - V - Baseball Fields - Batting Cage - CMU	6	31-Dec-19	08-Jan-20												
SITE503	SE - V - Baseball Fields - Batting Cage - Erect Roof Steel	3	09-Jan-20	13-Jan-20												
SITE512	SE - V - Baseball Fields - Batting Cage - Metal Frames & Doors	2	14-Jan-20	15-Jan-20												
SITE513	SE - V - Baseball Fields - Batting Cage - Downspouts	2	14-Jan-20	15-Jan-20												
SITE514	SE - V - Baseball Fields - Batting Cage - Electrical OH / Pull Wire / Trim Out	5	14-Jan-20	21-Jan-20												
SITE522	SE - V - Baseball Fields - Batting Cage - Clean & Seal CMU	2	16-Jan-20	17-Jan-20												
SITE526	SE - V - Baseball Fields - Batting Cage - Paint Doors	1	21-Jan-20	21-Jan-20												
Jr Varsity (Secondary)		71	17-Dec-19	30-Mar-20												
SITE761	SE - JV - Baseball Fields - Start Finish Work	0	17-Dec-19													
SITE419	SE - JV - Baseball Fields - UG Site Electrical	9	17-Dec-19	30-Dec-19												
SITE421	SE - JV - Baseball Fields - Set Sport Light Pole Bases	5	17-Dec-19	23-Dec-19												
SITE462	SE - JV - Baseball Fields - Finegrade for Sidewalks	6	24-Dec-19	02-Jan-20												
SITE477	SE - JV - Baseball Fields - SD Lines / Ball Field Drainage (perf lines)	15	31-Dec-19	22-Jan-20												
SITE517	SE - JV - Baseball Fields - F/R/P Hardscapes	8	15-Jan-20	27-Jan-20												
SITE533	SE - JV - Baseball Fields - Outfield Top Soil	3	23-Jan-20	27-Jan-20												
SITE538	SE - JV - Baseball Fields - Irrigation	5	28-Jan-20	03-Feb-20												
SITE539	SE - JV - Baseball Fields - Fencing	10	28-Jan-20	10-Feb-20												

Actual Work

Remaining Work

◆

Critical Remaining ...

◆

Milestone

Page 40 of 42

SKANSKA

■ Actual Work ■ Critical Remaining ...
■ Remaining Work ◆ Milestone

