


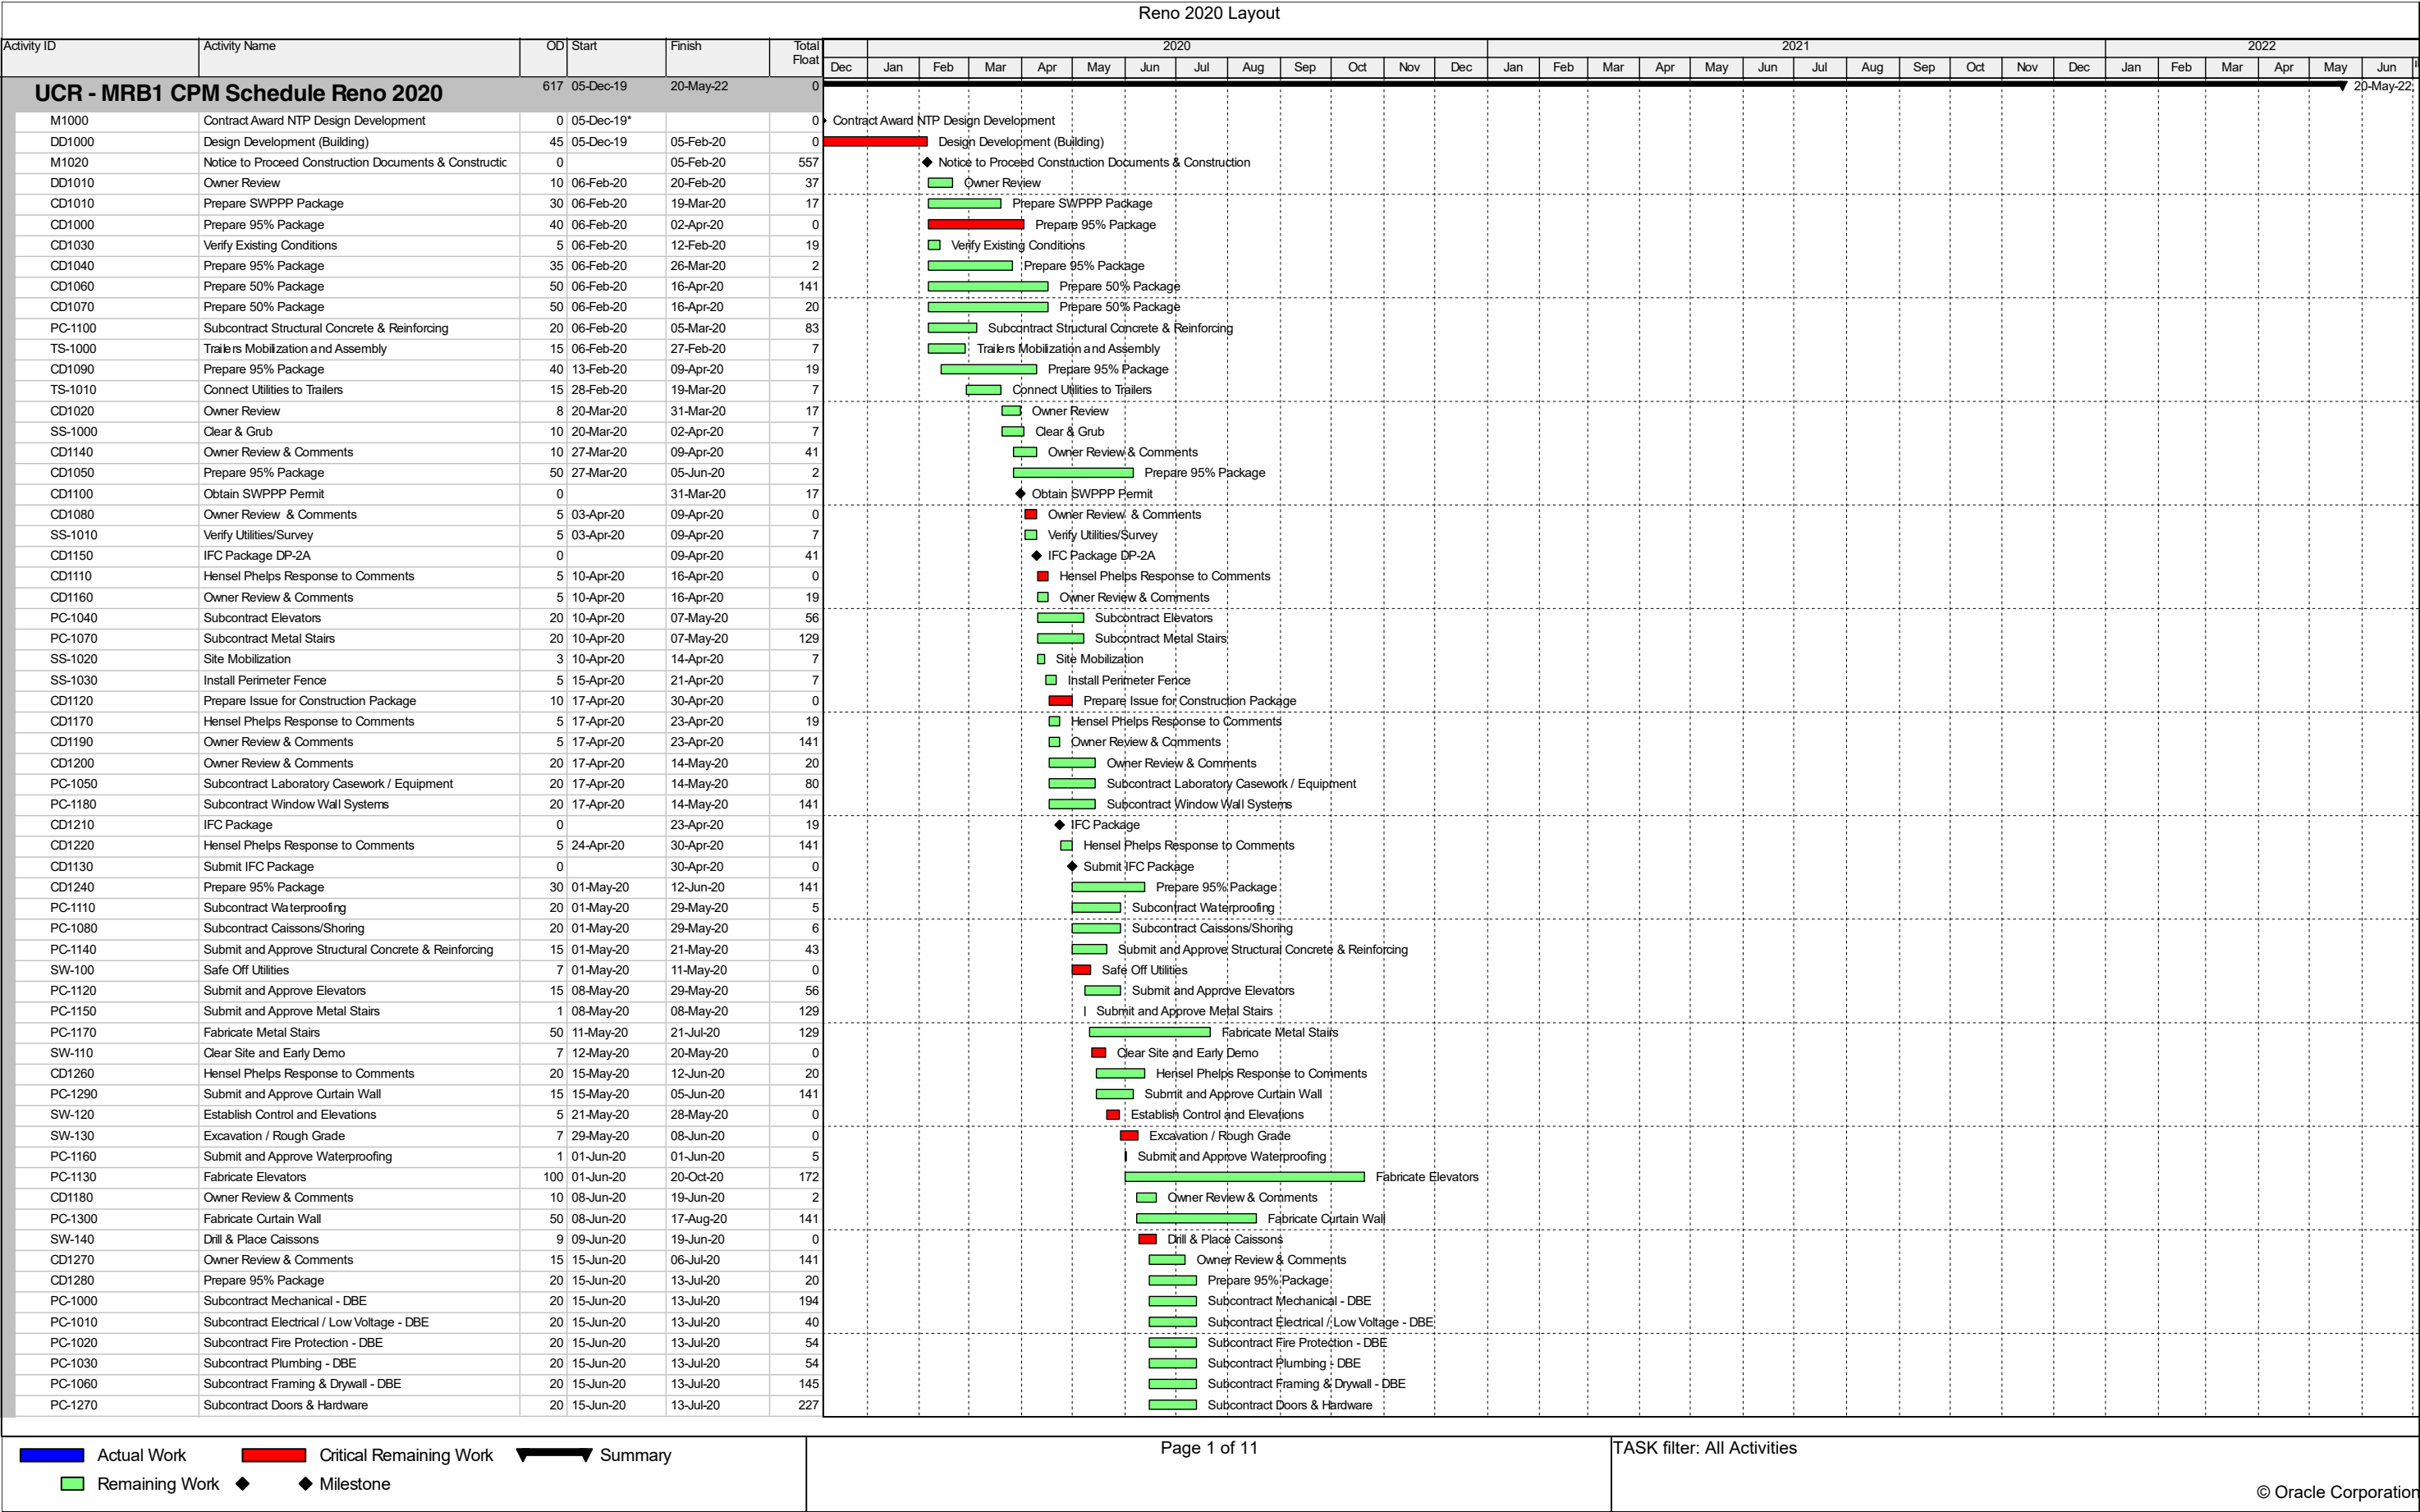

[illegible]

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 5 of 11

TASK filter: All Activities

© Oracle Corporation

Reno 2020 Layout

Activity ID

Activity Name

OD

Start

Finish

Total Float

ST3-160

Reinforcing

4

28-Dec-20

04-Jan-21

25

MMR-130

Dry Wall Tape & Finish

10

29-Dec-20

13-Jan-21

170

L3D2-130

Place Deck Level 3 Area 2

1

30-Dec-20

30-Dec-20

4

L2D3-150

Strip Formwork/ Install Reshore - L2 Deck - Area 3 on L1

6

04-Jan-21

11-Jan-21

28

L3CW1-120

Place Columns & Walls - Level 3 Area 1

1

04-Jan-21

04-Jan-21

4

L3D2-140

Cure Deck

5

04-Jan-21

08-Jan-21

16

L3CW2-100

Single Side Columns & Walls

3

04-Jan-21

06-Jan-21

4

L1D1-160

Remove Reshore - L1 Deck - Area 1 on LL

6

05-Jan-21

12-Jan-21

23

L3CW1-130

Strip Columns & Walls

1

05-Jan-21

05-Jan-21

4

L3D3-110

MEP Layout

1

05-Jan-21

05-Jan-21

0

MER-130

Dry Wall Tape & Finish

5

05-Jan-21

11-Jan-21

160

AL-340

Formwork

5

05-Jan-21

11-Jan-21

132

ST1-160

Set Stair

5

05-Jan-21

11-Jan-21

38

ST2-130

Set Stair

5

05-Jan-21

11-Jan-21

38

ST3-170

Cast in Place Stair 3

1

05-Jan-21

05-Jan-21

25

L3CW2-110

Level 3 Area 2 Columns & Walls Reinforcing

3

06-Jan-21

08-Jan-21

4

L3D3-120

Reinforcing

6

06-Jan-21

13-Jan-21

0

L4D1-100

Formwork

5

06-Jan-21

12-Jan-21

4

EXG-140

Window Systems LL

12

06-Jan-21

22-Jan-21

48

ST3-180

Formwork

5

06-Jan-21

12-Jan-21

25

L3D2-150

Strip Formwork/ Install Reshore - L3 Deck - Area 2 on L2

6

11-Jan-21

18-Jan-21

16

L3CW2-120

Place Columns & Walls - Level 3 Area 2

1

11-Jan-21

11-Jan-21

4

L3CW2-130

Strip Columns & Walls

1

12-Jan-21

12-Jan-21

4

EXG-130

Exterior Framing L1

14

12-Jan-21

01-Feb-21

28

MER-140

Doors & Hardware

2

12-Jan-21

13-Jan-21

160

AL-350

Reinforcing

5

12-Jan-21

18-Jan-21

132

ST1-170

Stair 1 Reinforcing

3

12-Jan-21

14-Jan-21

38

ST2-140

Stair 2 Reinforcing

3

12-Jan-21

14-Jan-21

38

L4D1-110

MEP Layout

1

13-Jan-21

13-Jan-21

4

L4D2-100

Formwork

5

13-Jan-21

19-Jan-21

4

ST3-190

Embeds & MEP Rough-in

6

13-Jan-21

21-Jan-21

25

LLE-100

Interior Wall Framing, Clips and Headers

30

13-Jan-21

25-Feb-21

23

L3D3-130

Place Deck Level 3 Area 3

1

14-Jan-21

14-Jan-21

0

L4D1-120

Reinforcing

6

14-Jan-21

22-Jan-21

4

MER-150

Paint

2

14-Jan-21

15-Jan-21

160

MMR-140

Doors & Hardware

3

14-Jan-21

18-Jan-21

170

L3D3-140

Cure Deck

5

15-Jan-21

22-Jan-21

7

L3CW3-160

Single Side Columns & Walls

3

15-Jan-21

19-Jan-21

0

ST1-180

Place Stair 1

2

15-Jan-21

18-Jan-21

38

ST2-150

Place Stair 2

2

15-Jan-21

18-Jan-21

38

MER-160

Set Equipment

35

18-Jan-21

09-Mar-21

160

L1D2-160

Remove Reshore - L1 Deck - Area 2 on LL

6

19-Jan-21

27-Jan-21

16

L3CW3-170

Level 3 Area 3 Columns & Walls Reinforcing

3

19-Jan-21

22-Jan-21

0

MMR-150

Paint

5

19-Jan-21

26-Jan-21

170

AL-360

Cast in Place Atrium

1

19-Jan-21

19-Jan-21

132

L4D2-110

MEP Layout

1

21-Jan-21

21-Jan-21

4

L4D2-120

Reinforcing

6

22-Jan-21

29-Jan-21

4

ST3-200

Reinforcing

4

22-Jan-21

27-Jan-21

25

L3D3-150

Strip Formwork/ Install Reshore - L3 Deck - Area 3 on L2

6

25-Jan-21

01-Feb-21

7

L3CW3-180

Place Columns & Walls - Level 3 Area 3

1

25-Jan-21

25-Jan-21

0

L4D1-130

Place Deck Level 4 Area 1

1

25-Jan-21

25-Jan-21

4

L3CW3-190

Strip Columns & Walls

1

26-Jan-21

26-Jan-21

0

L4D1-140

Cure Deck

5

26-Jan-21

01-Feb-21

17

L4CW1-100

Single Side Columns & Walls

3

26-Jan-21

28-Jan-21

4

L4D3-100

Formwork

5

27-Jan-21

02-Feb-21

0

L4CW1-110

Level 4 Area 1 Columns & Walls Reinforcing

3

28-Jan-21

01-Feb-21

4

ST3-210

Cast in Place Stair 3

1

28-Jan-21

28-Jan-21

25

L4D2-130

Place Deck Level 4 Area 2

1

01-Feb-21

01-Feb-21

4

L1D3-160

Remove Reshore - L1 Deck - Area 3 on LL

6

02-Feb-21

09-Feb-21

7

L4D1-150

Strip Formwork/ Install Reshore - L4 Deck - Area 1 on L3

6

02-Feb-21

09-Feb-21

17

L4CW1-120

Place Columns & Walls - Level 4 Area 1

1

02-Feb-21

02-Feb-21

4

L4D2-140

Cure Deck

5

02-Feb-21

08-Feb-21

31

L4CW2-100

Single Side Columns & Walls

3

02-Feb-21

04-Feb-21

4

EXG-150

MEP in Wall Rough-ins L1

2

02-Feb-21

03-Feb-21

28

EXG-170

Exterior Framing L2

14

02-Feb-21

22-Feb-21

29

Reno 2020 Layout																																			
Activity ID	Activity Name	OD	Start	Finish	Total Float	2020												2021												2022					
						Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
L4CW1-130	Strip Columns & Walls	1	03-Feb-21	03-Feb-21	4																														
L4D3-110	MEP Layout	1	03-Feb-21	03-Feb-21	0																														
L4CW2-110	Level 4 Area 2 Columns & Walls Reinforcing	3	04-Feb-21	08-Feb-21	4																														
L4D3-120	Reinforcing	6	04-Feb-21	11-Feb-21	0																														
RD1-100	Formwork	5	04-Feb-21	10-Feb-21	4																														
EXG-160	Sheathing and Waterproofing L1	12	04-Feb-21	22-Feb-21	28																														
L4D2-150	Strip Formwork/ Install Reshore - L4 Deck -Area 2 on L3	6	09-Feb-21	17-Feb-21	31																														
L4CW2-120	Place Columns & Walls - Level 4 Area 2	1	09-Feb-21	09-Feb-21	4																														
L2D1-160	Remove Reshore - L2 Deck - Area 1 on L1	6	10-Feb-21	18-Feb-21	36																														
L4CW2-130	Strip Columns & Walls	1	10-Feb-21	10-Feb-21	4																														
AL-370	Formwork	5	10-Feb-21	17-Feb-21	107																														
ST1-190	Set Stair	5	10-Feb-21	17-Feb-21	23																														
ST2-160	Set Stair	5	10-Feb-21	17-Feb-21	23																														
ST3-220	Formwork	5	10-Feb-21	17-Feb-21	17																														
LLW-100	Interior Wall Framing, Clips and Headers	30	10-Feb-21	24-Mar-21	7																														
RD1-110	MEP Layout	1	11-Feb-21	11-Feb-21	14																														
RD2-100	Formwork	5	11-Feb-21	18-Feb-21	4																														
L4D3-130	Place Deck Level 4 Area 3																																		

[illegible]

[illegible]

Reno 2020 Layout

Activity ID	Activity Name	OD	Start	Finish	Total Float	2020												2021												2022					
						Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
ER-240	Level 4 Finishes	6	21-Sep-21	28-Sep-21	50																														
L2L-150	Install Ceiling Systems	25	21-Sep-21	25-Oct-21	9																														
L3L-150	Install Ceiling Systems	25	21-Sep-21	25-Oct-21	9																														
L4L-150	Install Ceiling Systems	25	21-Sep-21	25-Oct-21	0																														
ST1-270	Paint	5	22-Sep-21	28-Sep-21	70																														
ST4-140	Handrails	6	22-Sep-21	29-Sep-21	64																														
EL-210	Adjust & Test Elevators	5	28-Sep-21	04-Oct-21	47																														
ER-250	Level 4 Set Equipment and Energize	15	29-Sep-21	19-Oct-21	50																														
IDFR-180	Level 3 Panels/Equipment	15	29-Sep-21	19-Oct-21	35																														
CX-160	Air Test & Balance	10	01-Oct-21	14-Oct-21	23																														
LLE-180	Furniture Installation	7	01-Oct-21	11-Oct-21	26																														
EXS-140	Framing and Plaster	3	04-Oct-21	06-Oct-21	39																														
L1O-160	Install Flooring Systems	15	06-Oct-21	26-Oct-21	23																														
L1L-160	Install Equipment	7	06-Oct-21	14-Oct-21	23																														
SI-130	Irrigation	15	07-Oct-21	27-Oct-21	23																														
EXW-130	Framing and Plaster	18	11-Oct-21	03-Nov-21	19																														
LLE-190	Interior Glazing	5	12-Oct-21	18-Oct-21	26																														
L4O-160	Install Flooring Systems	15	13-Oct-21	02-Nov-21	18																														
AL-270	Wood Slat Wall	20	13-Oct-21	09-Nov-21	54																														
CX-100	Final Pressure Inspection/Piping	10	13-Oct-21	26-Oct-21	45																														
LLW-170	Doors and Hardware	10	14-Oct-21	27-Oct-21	7																														
L1L-170	Flooring Systems	15	15-Oct-21	04-Nov-21	23																														
CX-210	Prefunctional Testing	5	15-Oct-21	21-Oct-21	23																														
LLE-200	Work to complete	5	19-Oct-21	25-Oct-21	26																														
IDFR-210	Level 4 Panels/Equipment	15	20-Oct-21	09-Nov-21	35																														
L2O-160	Install Flooring Systems	15	21-Oct-21	10-Nov-21	12																														
L3O-160	Install Flooring Systems	15	21-Oct-21	10-Nov-21	12																														
CX-220	Owner Functional Testing and Sign-Off	5	22-Oct-21	28-Oct-21	23																														
L2L-160	Install Equipment	7	26-Oct-21	03-Nov-21	9																														
L3L-160	Install Equipment	7	26-Oct-21	03-Nov-21	9																														
L4L-160	Install Equipment	7	26-Oct-21	03-Nov-21	0																														
LLE-210	Punchlist	5	26-Oct-21	01-Nov-21	26																														
L1O-170	Doors and Hardware	10	27-Oct-21	09-Nov-21	23																														
SI-140	Landscape	15	28-Oct-21	18-Nov-21	23																														
LLW-180	Furniture Installation	7	28-Oct-21	05-Nov-21	7																														
CX-230	Start-up Equipment	10	29-Oct-21	12-Nov-21	23																														
LLE-220	Final Clean	5	02-Nov-21	08-Nov-21	26																														
L4O-170	Doors and Hardware	10	03-Nov-21	17-Nov-21	18																														
EL-170	Finish Elevator Steel and Rails at Equipment/Controls	10	03-Nov-21	17-Nov-21	11																														
EX-100	HP Work Completion List	10	04-Nov-21	18-Nov-21	19																														
L2L-170	Flooring Systems	15	04-Nov-21	29-Nov-21	9																														
L3L-170	Flooring Systems	15	04-Nov-21	29-Nov-21	9																														
L4L-170	Flooring Systems	15	04-Nov-21	29-Nov-21	0																														
L1L-180	Doors and Hardware	10	05-Nov-21	19-Nov-21	23																														
LLW-190	Interior Glazing	5	08-Nov-21	15-Nov-21	7																														
L1O-180	Furniture Installation	7	10-Nov-21	19-Nov-21	23																														
AL-280	Flooring Tile	10	10-Nov-21	24-Nov-21	54																														
CX-190	Prefunctional Testing	5	10-Nov-21	17-Nov-21	35																														
L2O-170	Doors and Hardware	10	12-Nov-21	29-Nov-21	12																														
L3O-170	Doors and Hardware	10	12-Nov-21	29-Nov-21	12																														
LLW-200	Work to complete	5	16-Nov-21	22-Nov-21	7																														
L4O-180	Furniture Installation	7	18-Nov-21	30-Nov-21	18																														
EL-180	Adjust & Test Elevators	5	18-Nov-21	24-Nov-21	11																														
CX-200	Owner Functional Testing and Sign-Off	5	18-Nov-21	24-Nov-21	40																														
EX-110	Owner/Architect Punch List	10	19-Nov-21	06-Dec-21	19																														
SI-150	Site Furnishings	5	19-Nov-21	29-Nov-21	23																														
L1O-190	Interior Glazing	5	22-Nov-21	30-Nov-21	23																														
L1L-190	Interior Glazing	5	22-Nov-21	30-Nov-21	23																														
LLW-210	Punchlist	5	23-Nov-21	01-Dec-21	7																														
AL-290	Punchlist	1	29-Nov-21	29-Nov-21	54																														
L2O-180	Furniture Installation	7	30-Nov-21	08-Dec-21	12																														

Reno 2020 Layout																																			
Activity ID	Activity Name	OD	Start	Finish	Total Float	2020												2021												2022					
						Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SI-160	Striping and Painting	3	30-Nov-21	02-Dec-21	23																														
L1O-200	Work to complete	5	01-Dec-21	07-Dec-21	23																														
L1L-200	Work to Complete	5	01-Dec-21	07-Dec-21	23																														
L4O-190	Interior Glazing	5	01-Dec-21	07-Dec-21	18																														
LLW-220	Final Clean	5	02-Dec-21	08-Dec-21	7																														
CO-110	Jobsite Demobilization	3	03-Dec-21	07-Dec-21	23																														
ST2-210	Paint	5	07-Dec-21	13-Dec-21	19																														
L1O-210	Punchlist	5	08-Dec-21	14-Dec-21	23																														
L1L-210	Punchlist	5	08-Dec-21	14-Dec-21	23																														
L4O-200	Work to complete	5	08-Dec-21	14-Dec-21	18																														
CO-120	Restore Landcape Areas	10	08-Dec-21	21-Dec-21	23																														
L2O-190	Interior Glazing	5	09-Dec-21	15-Dec-21	12																														
L3O-190	Interior Glazing	5	09-Dec-21	15-Dec-21	12																														
CX-240	Air/Gas/Vacuum Piping Test	10	09-Dec-21	22-Dec-21	7																														
L2L-190	Interior Glazing	5	14-Dec-21	20-Dec-21	9																														
L3L-190	Interior Glazing	5	14-Dec-21	20-Dec-21	9																														
L4L-190	Interior Glazing	5	14-Dec-21	20-Dec-21	9																														
CX-270	Fire Alarm Pre Test	10	14-Dec-21	28-Dec-21	0																														
L1O-220	Final Clean	5	15-Dec-21	21-Dec-21	23																														
L1L-220	Final Clean	5	15-Dec-21	21-Dec-21	23																														
L4O-210	Punchlist	5	15-Dec-21	21-Dec-21	18																														
L2O-200	Work to complete	5	16-Dec-21	22-Dec-21	12																														
L3O-200	Work to complete	5	16-Dec-21	22-Dec-21	12																														
L2L-200	Work to Complete	5	21-Dec-21	28-Dec-21	9																														
L3L-200	Work to Complete	5	21-Dec-21	28-Dec-21	9																														
L4L-200	Work to Complete	5	21-Dec-21	28-Dec-21	9																														
L4O-220	Final Clean	5	22-Dec-21	29-Dec-21	18																														
L2O-210	Punchlist	5	23-Dec-21	30-Dec-21	12																														
L3O-210	Punchlist	5	23-Dec-21	30-Dec-21	12																														
CX-250	Prefunctional Testing	5	23-Dec-21	30-Dec-21	7																														
L2L-210	Punchlist	5	29-Dec-21	05-Jan-22	9																														
L3L-210	Punchlist	5	29-Dec-21	05-Jan-22	9																														
L4L-210	Punchlist	5	29-Dec-21	05-Jan-22	9																														
CX-110	Prefunctional Testing	5	29-Dec-21	05-Jan-22	4																														
CX-290	Prefunction Fire Alarm Testing	12	29-Dec-21	14-Jan-22	0																														
L2O-220	Final Clean	5	03-Jan-22	07-Jan-22	12																														
L3O-220	Final Clean	5	03-Jan-22	07-Jan-22	12																														
CX-260	Owner Functional Testing and Sign-Off	5	03-Jan-22	07-Jan-22	12																														
L2L-220	Final Clean	5	06-Jan-22	12-Jan-22	9																														
L3L-220	Final Clean	5	06-Jan-22	12-Jan-22	9																														
L4L-220	Final Clean	5	06-Jan-22	12-Jan-22	9																														
CX-120	Owner Functional Testing and Sign-Off	5	06-Jan-22	12-Jan-22	9																														
CO-100	Prepare O&Ms	10	06-Jan-22	19-Jan-22	4																														
CX-300	Functional Fire Alarm Testing	7	17-Jan-22	26-Jan-22	0																														
CO-130	Admin Closeout	15	27-Jan-22	16-Feb-22	0																														
M1070	Weather Allowance	45	17-Feb-22	21-Apr-22	0																														
M1030	Substantial Completion	0		22-Apr-22	0																														
M1040	Project Completion	0		20-May-22*	0																														
