


Line	Activity ID	Name	Duration	Start	Finish	Predecessors	Successors	2021				2022				2023				2024					
								F	A	J	A	O	D	F	A	J	A	O	D	F	A	J	A	O	D
1	Milestones																								
2	0020	Notice of Award - Anticipated		1/15/2021 *	1/15/2021		Notice to Proceed, Concept Validation																		
3	0060	All Properties Released for Construction		1/15/2021 *	1/15/2021	Notice of Award - Anticipated	Secure Phase 2 Site (North)																		
4	0030	Notice to Proceed		5/4/2021	5/4/2021	Notice of Award - Anticipated, Concept	MDP Approved (Goal of Sound																		
5	1810	Interim Trail Secure & Open to Public (ERC Interim and South Trail)		11/11/2021	11/11/2021	Interim Trail Construction, Surfacing & Temporary																			
6	0040	MDP Approved (Goal of Sound Transit and Hensel Phelps)		11/17/2021	11/17/2021	Notice to Proceed, MDP Design and Approval	Site Clearing & Demo																		
7	1650	Maintenance Building Dry In		11/2/2023	11/2/2023	Exterior Skin - Maintenance & Shop Bldg., Roofing -	Finishes - Admin Area																		
8	1651	LRV Storage Available for Sound Transit		4/9/2024	4/9/2024	OCS/TPSS/Signalling/Lighting																			
9	1660	Sound Transit Controlled Float	60d	8/27/2024	10/25/2024	Startup & Commission - MOW Building, Startup &	Substantial Completion and																		
10	0050	Substantial Completion and Acceptance		10/25/2024	10/25/2024 *	Sound Transit Controlled Float	Project Acceptance																		
11	1800	Project Acceptance	1d	11/25/2024	11/25/2024	Substantial Completion and Acceptance																			
12	Design Summary																								
13	1110	Concept Validation Period	77d	1/15/2021	5/3/2021	Notice of Award - Anticipated	Notice to Proceed																		
14	1120	MDP Design and Approval	286d	2/5/2021	11/17/2021	Notice of Award - Anticipated	MDP Approved (Goal of Sound																		
15	1130	Design Package 1 - Erosion Control, Demolition Plan, Trails	80d	5/4/2021	8/25/2021	Notice to Proceed	Interim Trail Construction,																		
16	1140	Design Package 2 - King County Sewer Relocation	120d	5/4/2021	10/21/2021	Notice to Proceed	King County Sewer Replacement/Reloc:																		
17	1150	Design Package 3 - Civil/Grading/TPSS	180d	5/4/2021	1/19/2022	Notice to Proceed	Mass Earthwork & Preload North																		
18	1160	Design Package 4 - Buildings & Systems	220d	5/4/2021	3/16/2022	Notice to Proceed	Building Pad Preparation -																		
19	Mobilization																								
20	1200	Secure Phase 2 Site (North)	5d	1/15/2021	1/21/2021	All Properties Released for Construction	Setup TESC at Phase 2 Site																		
21	1210	Setup TESC at Phase 2 Site (North)	10d	1/22/2021	2/4/2021	Secure Phase 2 Site (North)	Abatement - Phase 2 (North), Interim																		
22	1170	Mobilize & Secure Phase 1 Site (South)	20d	7/29/2021	8/25/2021	Notice to Proceed, Design Package 1 - Erosion Control,	Setup TESC at Phase 1 Site																		
23	1180	Setup TESC at Phase 1 Site (South)	15d	8/26/2021	9/16/2021	Mobilize & Secure Phase 1 Site (South)	Office Trailer & Utility Setup,																		
24	1190	Office Trailer & Utility Setup	80d	9/17/2021	1/12/2022	Setup TESC at Phase 1 Site (South)	Site Clearing & Demo																		
25	Demo & Abatement																								
26	1220	Abatement - Phase 1 (South)	15d	9/17/2021	10/7/2021	Setup TESC at Phase 1 Site (South)	Demo - Phase 1 (South)																		
27	1230	Demo - Phase 1 (South)	35d	10/8/2021	11/29/2021	Abatement - Phase 1 (South)	Abatement - Phase 2 (North)																		
28	1240	Abatement - Phase 2 (North)	20d	11/30/2021	12/28/2021	Setup TESC at Phase 2 Site (North), Demo - Phase 1	Demo - Phase 2 (North)																		
29	1250	Demo - Phase 2 (North)	40d	12/29/2021	2/23/2022	Abatement - Phase 2 (North)	King County Sewer Replacement/Reloc:																		
30	Early Sitework																								
31	1260	Interim Trail Construction, Surfacing & Temporary Fencing	40d	9/17/2021	11/11/2021	Setup TESC at Phase 1 Site (South), Design Package 1 -	Site Clearing & Demo, Interim																		
32	1270	King County Sewer Replacement/Relocation	30d	2/24/2022	4/6/2022	Design Package 2 - King County Sewer Relocation,	Building Pad Preparation -																		
33	1280	Site Clearing & Demo	20d	2/24/2022	3/23/2022	Demo - Phase 2 (North), MDP Approved (Goal of	Mass Earthwork & Preload North																		
34	1290	Mass Earthwork & Preload North Storage Tracks	40d	3/24/2022	5/18/2022	Design Package 3 - Wet, Civil/Grading/TPSS, Site	Site Utilities - Wet, Building Pad																		

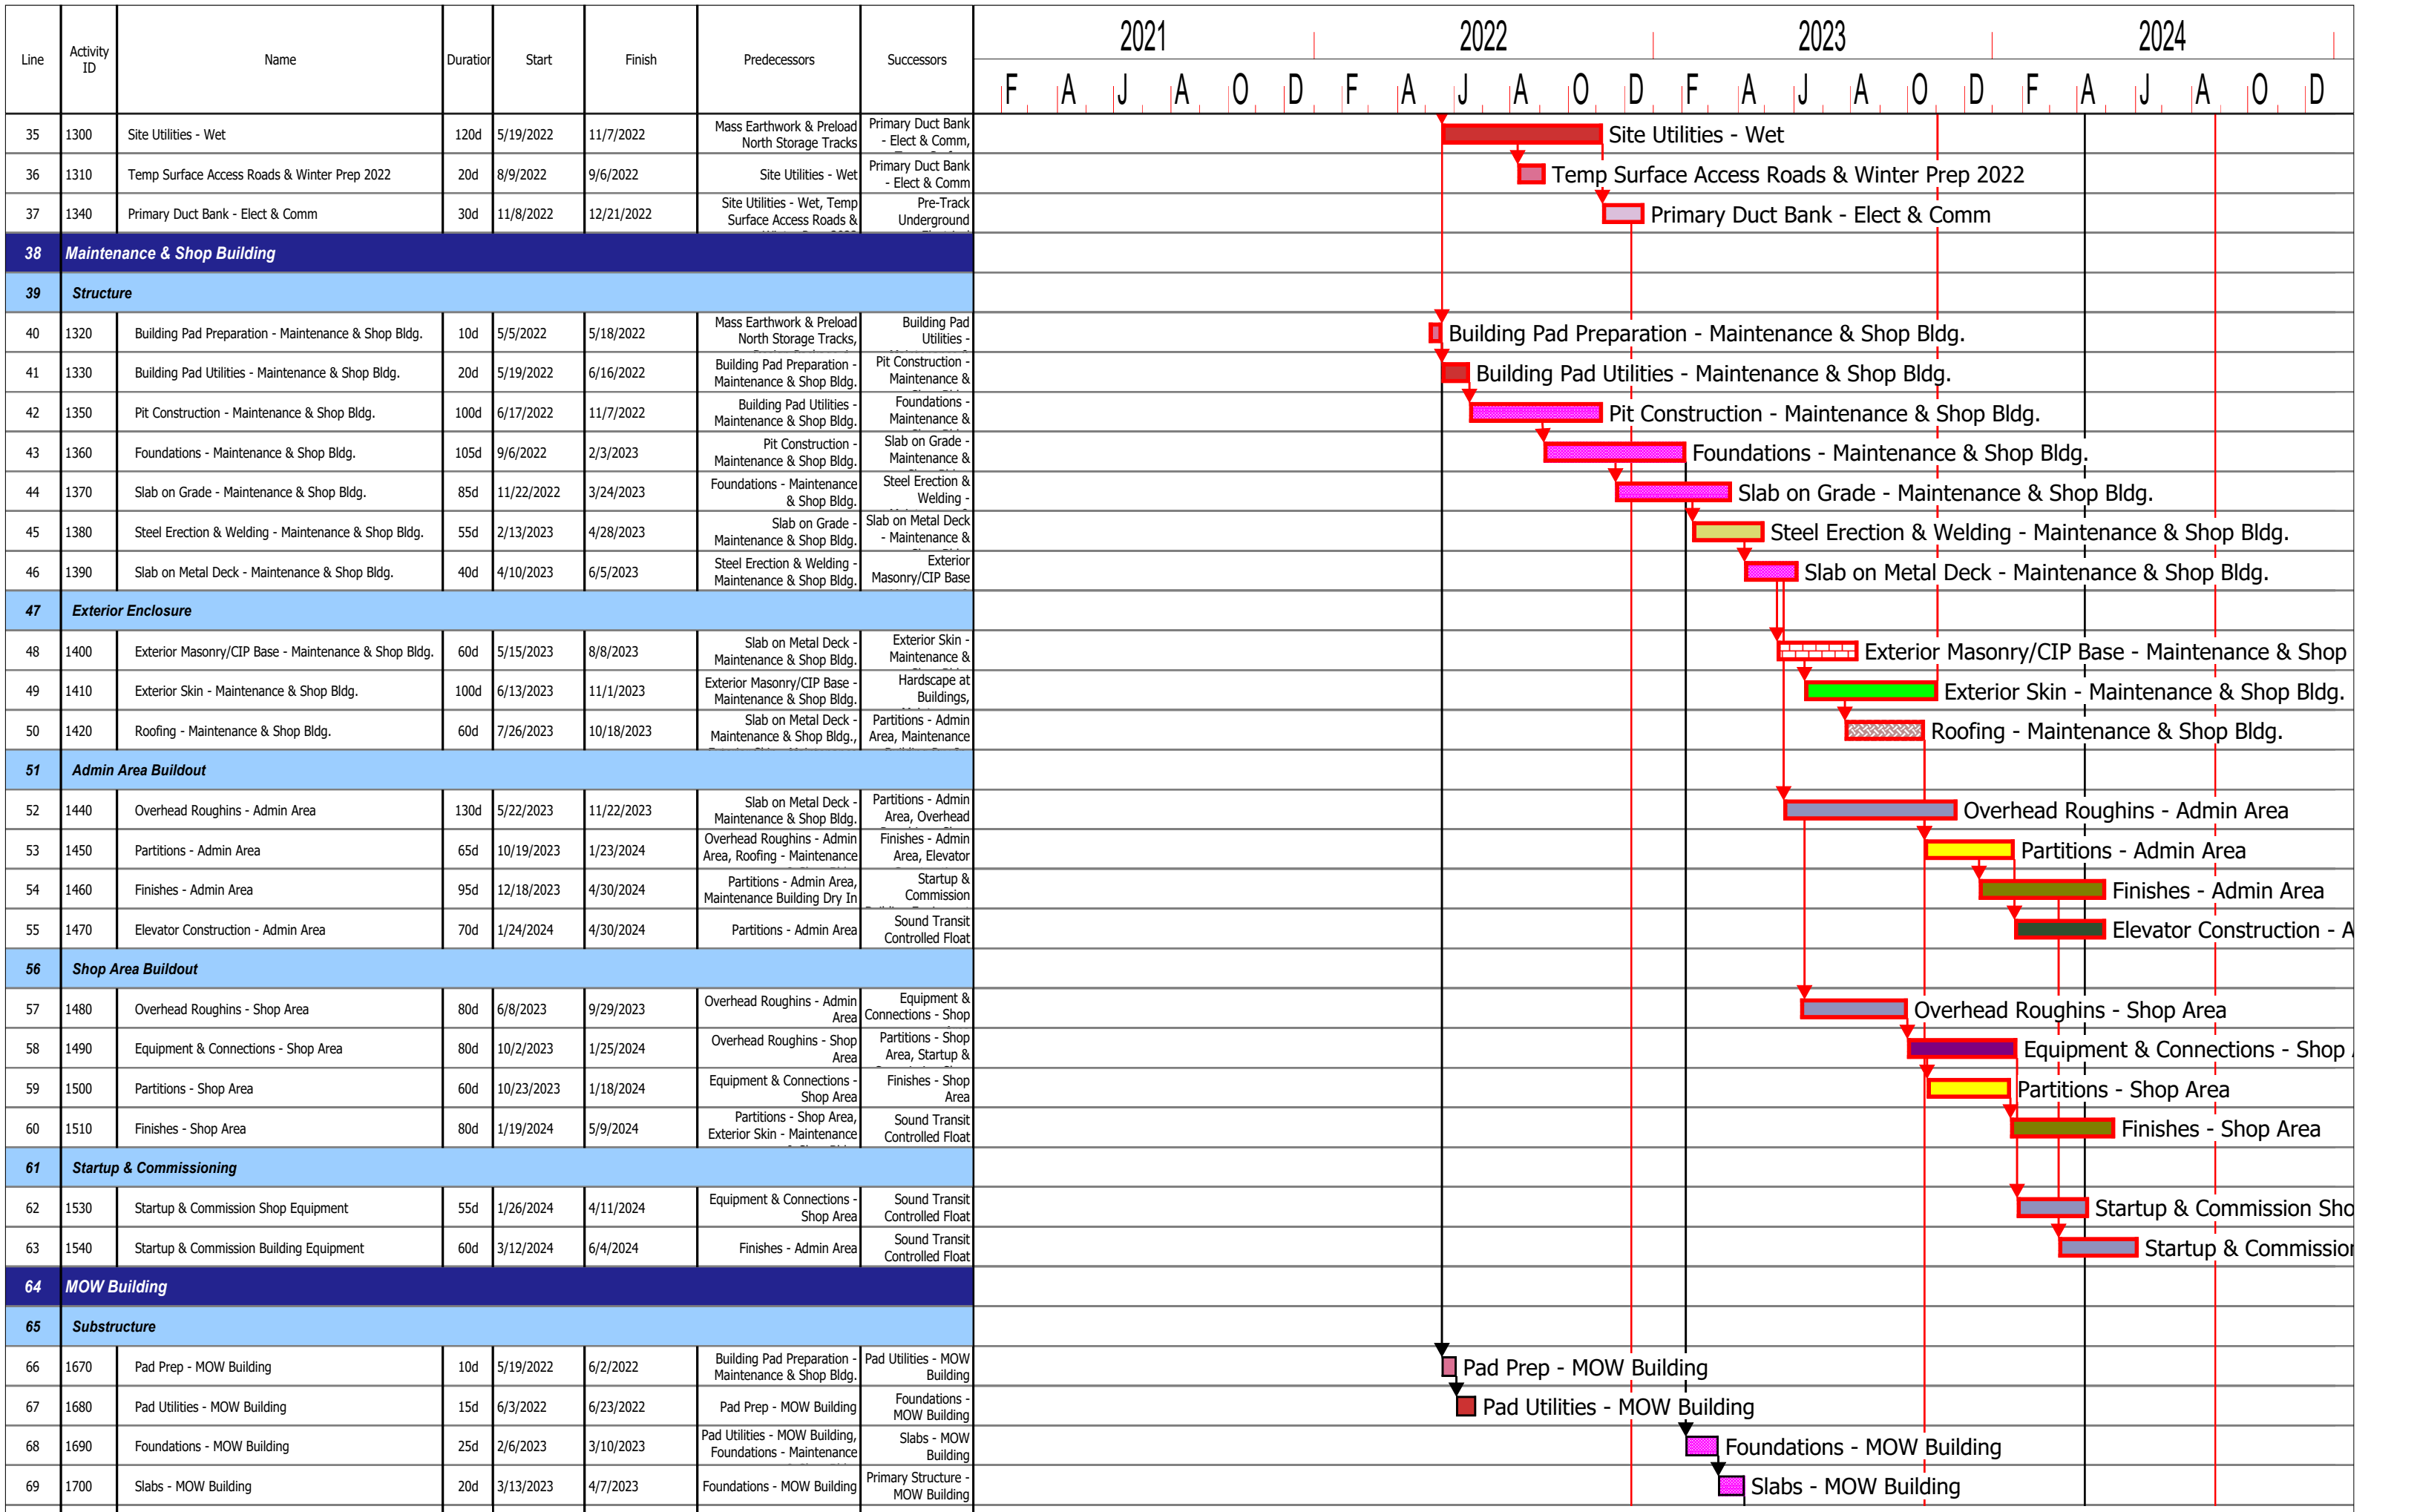

Line	Activity ID	Name	Duration	Start	Finish	Predecessors	Successors	2021												2022												2023												2024											
								F	A	J	A	O	D	F	A	J	A	O	D	F	A	J	A	O	D	F	A	J	A	O	D																								
70	Superstructure & Exterior Enclosure																																																						
71	1710	Primary Structure - MOW Building	10d	4/10/2023	4/21/2023	Slabs - MOW Building	Secondary Structure - MOW																																																
72	1720	Secondary Structure - MOW Building	15d	4/24/2023	5/12/2023	Primary Structure - MOW Building	Exterior Masonry/CIP Base																																																
73	1730	Exterior Masonry/CIP Base - MOW Building	20d	5/15/2023	6/12/2023	Secondary Structure - MOW Building																																																	
74	1740	Exterior Skin - MOW Building	40d	10/5/2023 *	12/1/2023		Hardscape at Buildings																																																
75	1750	Roofing - MOW Building	27d	10/19/2023	11/28/2023	Roofing - Maintenance & Shop Bldg.	OH Roughins - MOW Building																																																
76	Interior Construction																																																						
77	1760	OH Roughins - MOW Building	35d	11/29/2023	1/18/2024	Roofing - MOW Building	Partitions - MOW Building,																																																
78	1761	Equipment & Connections - MOW Building	20d	1/19/2024	2/15/2024	OH Roughins - MOW Building	Partitions - MOW Building																																																
79	1770	Partitions - MOW Building	45d	2/16/2024	4/18/2024	OH Roughins - MOW Building, Equipment &	Building Finishes - MOW Building																																																
80	1780	Building Finishes - MOW Building	50d	4/19/2024	6/28/2024	Partitions - MOW Building	Startup & Commission -																																																
81	1790	Startup & Commission - MOW Building	40d	7/1/2024	8/26/2024	Building Finishes - MOW Building	Sound Transit Controlled Float																																																
82	Trackwork																																																						
83	1550	Pre-Track Underground Electrical	135d	12/8/2022	6/19/2023	Primary Duct Bank - Elect & Comm	Fine Grading / Track Drainage /																																																
84	1560	Fine Grading / Track Drainage / Subballast	135d	2/6/2023	8/15/2023	Pre-Track Underground Electrical	Trackwork, Pad Prep &																																																
85	1570	Trackwork	225d	4/28/2023	3/18/2024	Fine Grading / Track Drainage / Subballast	OCS/TPSS/Signalling/Hardscape at Yard &																																																
86	1573	TPSS Basement	45d	6/20/2023	8/22/2023	Pre-Track Underground Electrical	Set & Connect TPSS																																																
87	1583	Guard House Foundation	20d	6/20/2023	7/18/2023	Pre-Track Underground Electrical	Guard House Structure																																																
88	1576	Guard House Structure	25d	7/19/2023	8/22/2023	Guard House Foundation	Guard House Interior Build Out																																																
89	1571	Pad Prep & Foundations - North Signal House	20d	8/16/2023	9/13/2023	Fine Grading / Track Drainage / Subballast	Set & Fitout North & South Signal																																																
90	1572	Pad Prep & Foundations - South Signal House	20d	8/16/2023	9/13/2023	Fine Grading / Track Drainage / Subballast	Set & Fitout North & South Signal																																																
91	1577	Guard House Interior Build Out	20d	8/23/2023	9/20/2023	Guard House Structure	Guard House MEP																																																
92	1580	OCS/TPSS/Signalling/Lighting/Comm	150d	9/6/2023	4/8/2024	Trackwork	Commission Train Systems/TPSS/Sign																																																
93	1578	Guard House MEP	25d	9/21/2023	10/25/2023	Guard House Interior Build Out																																																	
94	1574	Set & Fitout North & South Signal House	10d	3/19/2024	4/1/2024	Pad Prep & Foundations - North Signal House, Pad	Commission Train Systems/TPSS/Sign																																																
95	1575	Set & Connect TPSS	10d	3/19/2024	4/1/2024	TPSS Basement, Trackwork	Commission Train Systems/TPSS/Sign																																																
96	1590	Commission Train Systems/TPSS/Signal/Etc.	60d	4/2/2024	6/25/2024	OCS/TPSS/Signalling/Lighting/ Set & Fitout North & South S	Sound Transit Controlled Float																																																
97	Site Finishes																																																						
98	1610	Hardscape at Buildings	60d	12/4/2023	2/27/2024	Exterior Skin - Maintenance & Shop Bldg., Exterior Skin -	Landscaping & Irrigation,																																																
99	1620	Hardscape at Yard & Streetscapes	60d	2/6/2024	4/29/2024	Trackwork	Landscaping & Irrigation																																																
100	1611	Smoker's Pavillion Structure	15d	2/28/2024	3/19/2024	Hardscape at Buildings	Smoker's Pavillion Exterior Skin																																																
101	1612	Bike Enclosure Structure	15d	2/28/2024	3/19/2024	Hardscape at Buildings	Bike Enclosure Exterior Skin																																																
102	1613	Smoker's Pavillion Exterior Skin	10d	3/20/2024	4/2/2024	Smoker's Pavillion Structure																																																	
103	1614	Bike Enclosure Exterior Skin	15d	3/20/2024	4/9/2024	Bike Enclosure Structure																																																	
104	1640	Landscaping & Irrigation	25d	4/24/2024	5/29/2024	Hardscape at Yard & Streetscapes, Hardscape at	Sound Transit Controlled Float																																																
