


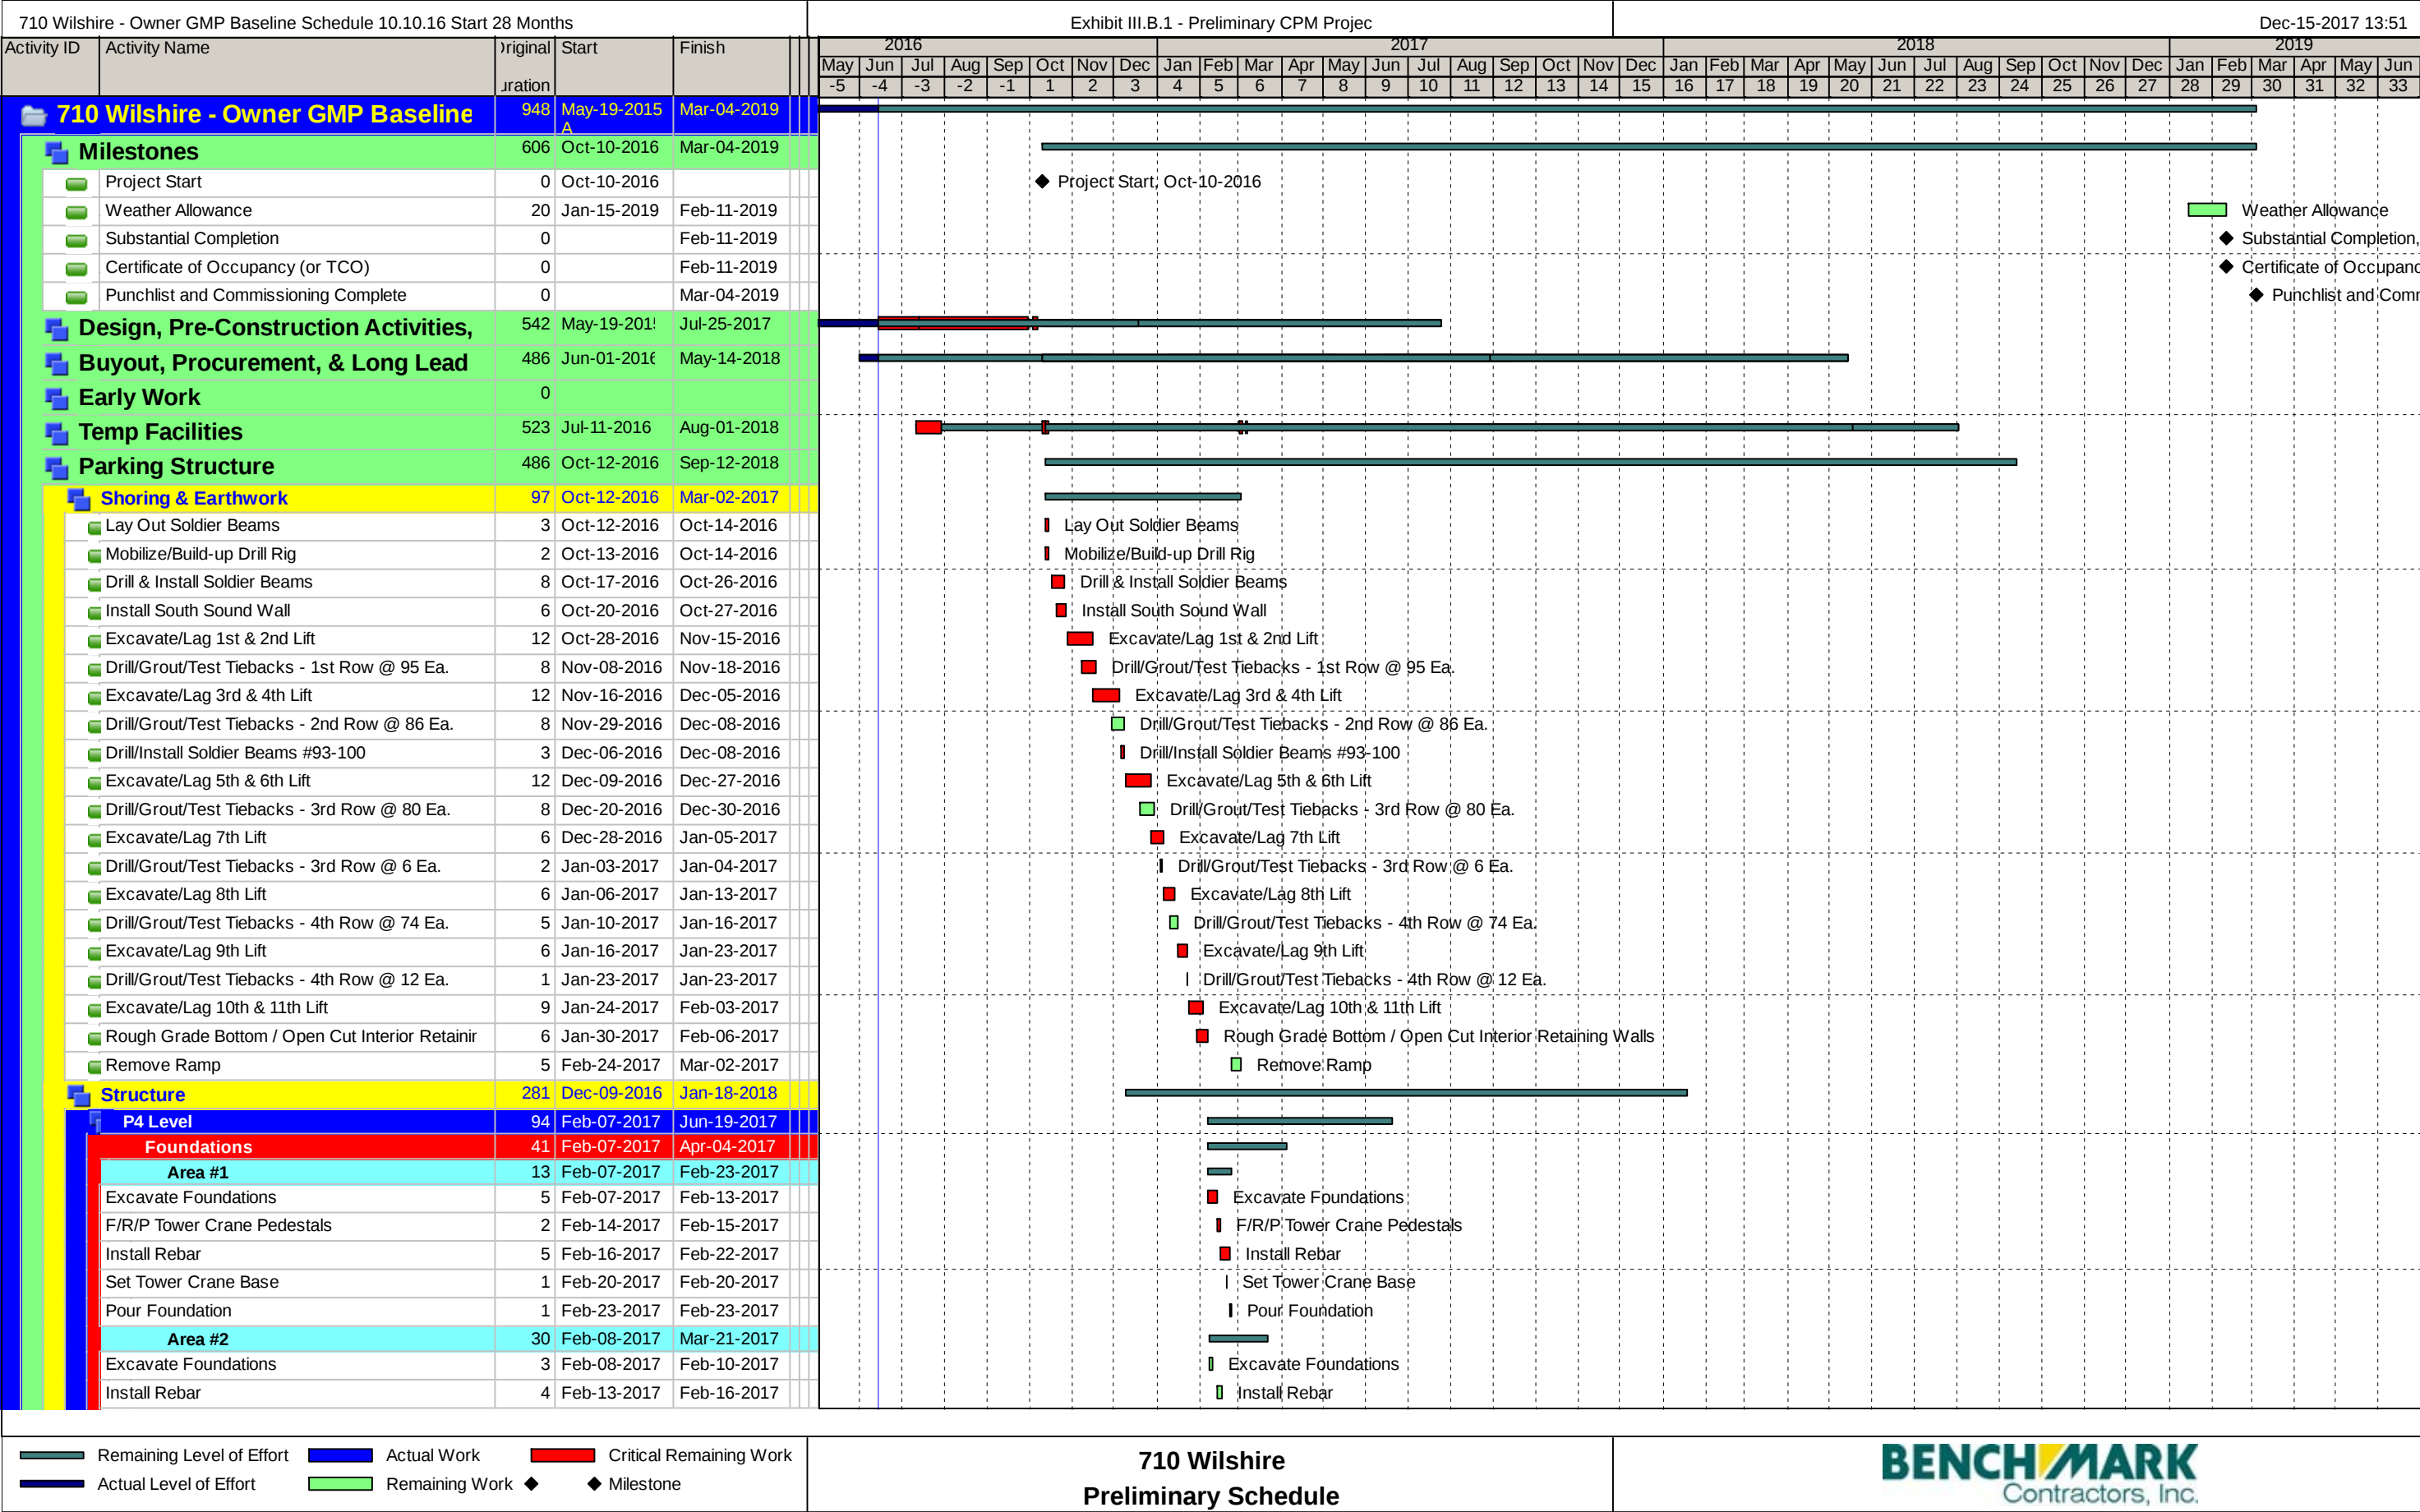

710 Wilshire - Owner GMP Baseline Schedule 10.10.16 Start 28 Months					Exhibit III.B.1 - Preliminary CPM Project																	Dec-15-2017 13:51																									
Activity ID	Activity Name	Original Duration	Start	Finish		2016												2017												2018												2019					
						May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun				
						-5	-4	-3	-2	-1	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33				
	Shoot #6	14	Mar-27-2017	Apr-13-2017																																											
	Form Walls	4	Mar-27-2017	Mar-30-2017																																											
	Install Rebar	5	Mar-31-2017	Apr-06-2017																																											
	Wires/Shoot/Rebound Cleanup	5	Apr-07-2017	Apr-13-2017																																											
	Shoot #7	32	Apr-12-2017	May-25-2017																																											
	Install Scaffolding	5	Apr-12-2017	Apr-18-2017																																											
	Install Waterproofing	5	Apr-19-2017	Apr-25-2017																																											
	Install Rebar	8	Apr-27-2017	May-08-2017																																											
	Wires/Shoot/Rebound Cleanup	10	May-12-2017	May-25-2017																																											
	Columns - Set #1	5	Mar-02-2017	Mar-08-2017																																											
	Install Rebar	2	Mar-02-2017	Mar-03-2017																																											
	Form Columns - 22 Ea.	2	Mar-06-2017	Mar-07-2017																																											
	Pour Columns	1	Mar-08-2017	Mar-08-2017																																											
	Columns - Set #2	5	Apr-05-2017	Apr-11-2017																																											
	Install Rebar	2	Apr-05-2017	Apr-06-2017																																											
	Form Columns - 22 Ea.	2	Apr-07-2017	Apr-10-2017																																											
	Pour Columns	1	Apr-11-2017	Apr-11-2017																																											
	Slab On Grade	36	Apr-28-2017	Jun-19-2017																																											
	SOG #1	25	Apr-28-2017	Jun-02-2017																																											
	MEP Underground	12	Apr-28-2017	May-15-2017																																											
	Backfill Footings	5	May-16-2017	May-22-2017																																											
	Form Diamond BO'S	4	May-23-2017	May-26-2017																																											
	Fine Grade SOG	2	May-23-2017	May-24-2017																																											
	Install Reinforcement	4	May-25-2017	May-31-2017																																											
	Place SOG	2	Jun-01-2017	Jun-02-2017																																											
	SOG #2	16	May-26-2017	Jun-19-2017																																											
	MEP Underground	5	May-26-2017	Jun-02-2017																																											
	Backfill Footings	5	Jun-01-2017	Jun-07-2017																																											
	Form Diamond BO'S	4	Jun-08-2017	Jun-13-2017																																											
	Fine Grade SOG	2	Jun-08-2017	Jun-09-2017																																											
	Install Reinforcement	4	Jun-12-2017	Jun-15-2017																																											
	Place SOG	2	Jun-16-2017	Jun-19-2017																																											
	P3 Level	18	Jun-15-2017	Jul-11-2017																																											

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

710 Wilshire

Preliminary Schedule



[illegible]

[illegible]

710 Wilshire - Owner GMP Baseline Schedule 10.10.16 Start 28 Months					Exhibit III.B.1 - Preliminary CPM Project																				Dec-15-2017 13:51																					
Activity ID	Activity Name	Original Duration	Start	Finish	2016												2017												2018												2019					
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun				
					-5	-4	-3	-2	-1	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33				
	Columns - Set #1		6	Aug-30-2017	Sep-07-2017																																									
	Install Rebar		2	Aug-30-2017	Aug-31-2017																																									
	Form Columns - 27 Ea.		3	Sep-01-2017	Sep-06-2017																																									
	Pour Columns		2	Sep-06-2017	Sep-07-2017																																									
	Columns - Set #2		6	Sep-12-2017	Sep-19-2017																																									
	Install Rebar		2	Sep-12-2017	Sep-13-2017																																									
	Form Columns - 22 Ea.		3	Sep-14-2017	Sep-18-2017																																									
	Pour Columns		2	Sep-18-2017	Sep-19-2017																																									
	Columns - Set #3		6	Sep-25-2017	Oct-02-2017																																									
	Install Rebar		2	Sep-25-2017	Sep-26-2017																																									
	Form Columns - 25 Ea.		3	Sep-27-2017	Sep-29-2017																																									
	Pour Columns		2	Sep-29-2017	Oct-02-2017																																									
	Build-Out		178	Jan-03-2018	Sep-12-2018																																									
	Hotel and Retail		412	Jul-06-2017	Feb-20-2019																																									
	Structure		131	Sep-19-2017	Mar-26-2018																																									
	Level 2		91	Sep-19-2017	Jan-29-2018																																									
	Deck #12		86	Sep-19-2017	Jan-22																																									

[illegible]

[illegible]

[illegible]

[illegible]

