Activity ID	Activity Name	OD	Start	Finish	TF
MS-20	Notice to Proceed (NTP)	0	06-Mar-23*		0
MS-10	Notice of Award	0	06-Mar-23*		0
A-SUB-20	Prep and Submit Temp Underground Submittals	10	06-Mar-23	15-Mar-23	0
A-SUB-50	Prep and Submit PG&E Application for Permanent Power	40	16-Mar-23	24-Apr-23	0
A-SUB-70	Prep and Submit Generator Equipment Submittals	40	25-Apr-23	03-Jun-23	0
A-SUB-100	Owner Review and Aprove Submittals Generator	28	04-Jun-23	01-Jul-23	0
COR-031-10	Generator Manufacturer Selection and Redesign EOC	5	02-Jul-23	06-Jul-23	0
COR-031-30	PCO Development by Hensel Phelps Generator EOC	30	07-Jul-23	05-Aug-23	0
COR-031-40	PCO Approval by Owner Generator EOC	15	06-Aug-23	20-Aug-23	0
COR-031-110	Prep and Re-submit Main Gear Submittals EOC	40	21-Aug-23	29-Sep-23	0
COR-031-130	Owner Review and Approve Submittals Main Gear EOC	28	30-Sep-23	27-Oct-23	0
COR-031-210	PG&E Review and Approve Main Gear EOC	21	28-Oct-23	17-Nov-23	0
COR-031-140	Fab and Deliver Main Gear EOC	100	18-Nov-23	25-Feb-24	0
C-EOC-FIN1-40	Set Main Switchgear MER LV 1	3	26-Feb-24	28-Feb-24	0
COR-345-40	PG&E to Inspect Main Gear Installation EOC (COR 345)	15	29-Feb-24	20-Mar-24	0
COR-345-50	Finalize PG&E Easement	5	21-Mar-24	27-Mar-24	0
COR-345-130	City of Sunnyvale Easement Approval and File	5	28-Mar-24	03-Apr-24	0
COR-345-150	PG&E to Schedule Construction Activities	50	04-Apr-24	12-Jun-24	0
C-EOC-YARD-170	Install PG&E Transformer Electrical Yard	10	13-Jun-24	26-Jun-24	0
C-EOC-YARD-180	Terminate Feeders (Transformer to Main Gear)	10	27-Jun-24	10-Jul-24	0
C-EOC-YARD-190	Install Generators Electrical Yard	15	11-Jul-24	31-Jul-24	0
C-EOC-YARD-200	Pull and Terminate Feeders (Generator to Emergency Panels)	10	01-Aug-24	14-Aug-24	0
C-EOC-CXE-10	Generator Pre-Functional Testing	15	15-Aug-24	04-Sep-24	0
C-EOC-CXE-20	Generator Functional Testing	15	05-Sep-24	25-Sep-24	0
C-EOC-CXFA-40	FA FM Testing	3	26-Sep-24	30-Sep-24	0
A-RAIN-EOC10	March 2023	4	01-Oct-24	04-Oct-24	0
A-RAIN-EOC20	April 2023	2	05-Oct-24	06-Oct-24	0
A-RAIN-EOC30	May 2023	1	07-Oct-24	07-Oct-24	0
A-RAIN-EOC40	September 2023	2	08-Oct-24	09-Oct-24	0
A-RAIN-EOC50	October 2023	4	10-Oct-24	13-Oct-24	0
A-RAIN-EOC60	November 2023	4	14-Oct-24	17-Oct-24	0
A-RAIN-EOC70	December 2023	5	18-Oct-24	22-Oct-24	0
A-RAIN-EOC80	January 2024	5	23-Oct-24	27-Oct-24	0
A-RAIN-EOC90	February 2024	4	28-Oct-24	31-Oct-24	0
A-RAIN-EOC100	March 2024	4	01-Nov-24	04-Nov-24	0
A-RAIN-EOC110	April 2024	2	05-Nov-24	06-Nov-24	0
A-RAIN-EOC120	May 2024	1	07-Nov-24	07-Nov-24	0
A-RAIN-EOC130	September 2024	2	08-Nov-24	11-Nov-24	0
A-RAIN-EOC140	October 2024	4	12-Nov-24	15-Nov-24	0
A-RAIN-EOC150	November 2024	4	18-Nov-24	21-Nov-24	0
A-RAIN-EOC160	December 2024	5	22-Nov-24	28-Nov-24	0
C-EOC-AHJ-10	AHJ Inspection for EOC	6	29-Nov-24	06-Dec-24	0
BULLETIN-31-10	Bulletin 31 DPS- Issuance by Owner- COR 1107	30	07-Dec-24	05-Jan-25	0
C-EOC-OWNER-60	Owner Move In LV1	1	09-Dec-24	09-Dec-24	0
C-EOC-OWNER-70	Owner Move In LV2	1	09-Dec-24	09-Dec-24	0
C-EOC-PH3-100	(CITY) Department Relocate / Vacate DPS- EOC	1	10-Dec-24	10-Dec-24	0
C-EOC-PH4-30	MEPF Cut and Cap / Make-Safe	15	11-Dec-24	31-Dec-24	0
C-EOC-PH4-40	Area #1- Soft Demolition	10	01-Jan-25	14-Jan-25	0
BULLETIN-31-20	Bulletin 31 DPS- Pricing by HP - COR 1107	14	06-Jan-25	19-Jan-25	0
BULLETIN-31-50	Bulletin 31 DPS- RFI 2405 Conduit Routing Owner Aproval- COR 1107	14	06-Jan-25	19-Jan-25	0
C-EOC-PH4-60	Area #2- Soft Demolition	15	08-Jan-25	28-Jan-25	0
C-EOC-PH4-70	Area #1- Demo Concrete Slab & Establish Subgrade	10	15-Jan-25	28-Jan-25	0
BULLETIN-31-40	Bulletin 31 DPS- Material Procurement- COR 1107	7	20-Jan-25	26-Jan-25	0
BULLETIN-31-30	Bulletin 31 DPS- Pricing Approval by Owner- COR 1107	7	20-Jan-25	26-Jan-25	0
COR1107-10	Install Over Head Electrical and Comm Conduits- COR 1107	7	27-Jan-25	04-Feb-25	0
C-EOC-PH4-90	Area #2- Demo Concrete Slab & Establish Subgrade	10	29-Jan-25	11-Feb-25	0
C-EOC-PH4-110	Area #1 (Restroom / Shower)- UG Plumbing Rough-in	10	29-Jan-25	11-Feb-25	0
COR1107-20	Install Communications Rack, Ground and Power- COR 1107	5	05-Feb-25	11-Feb-25	0
C-EOC-PH4-120	Area #1 (Restroom / Shower)- Drill and Epoxy Slab Dowels	5	12-Feb-25	18-Feb-25	0

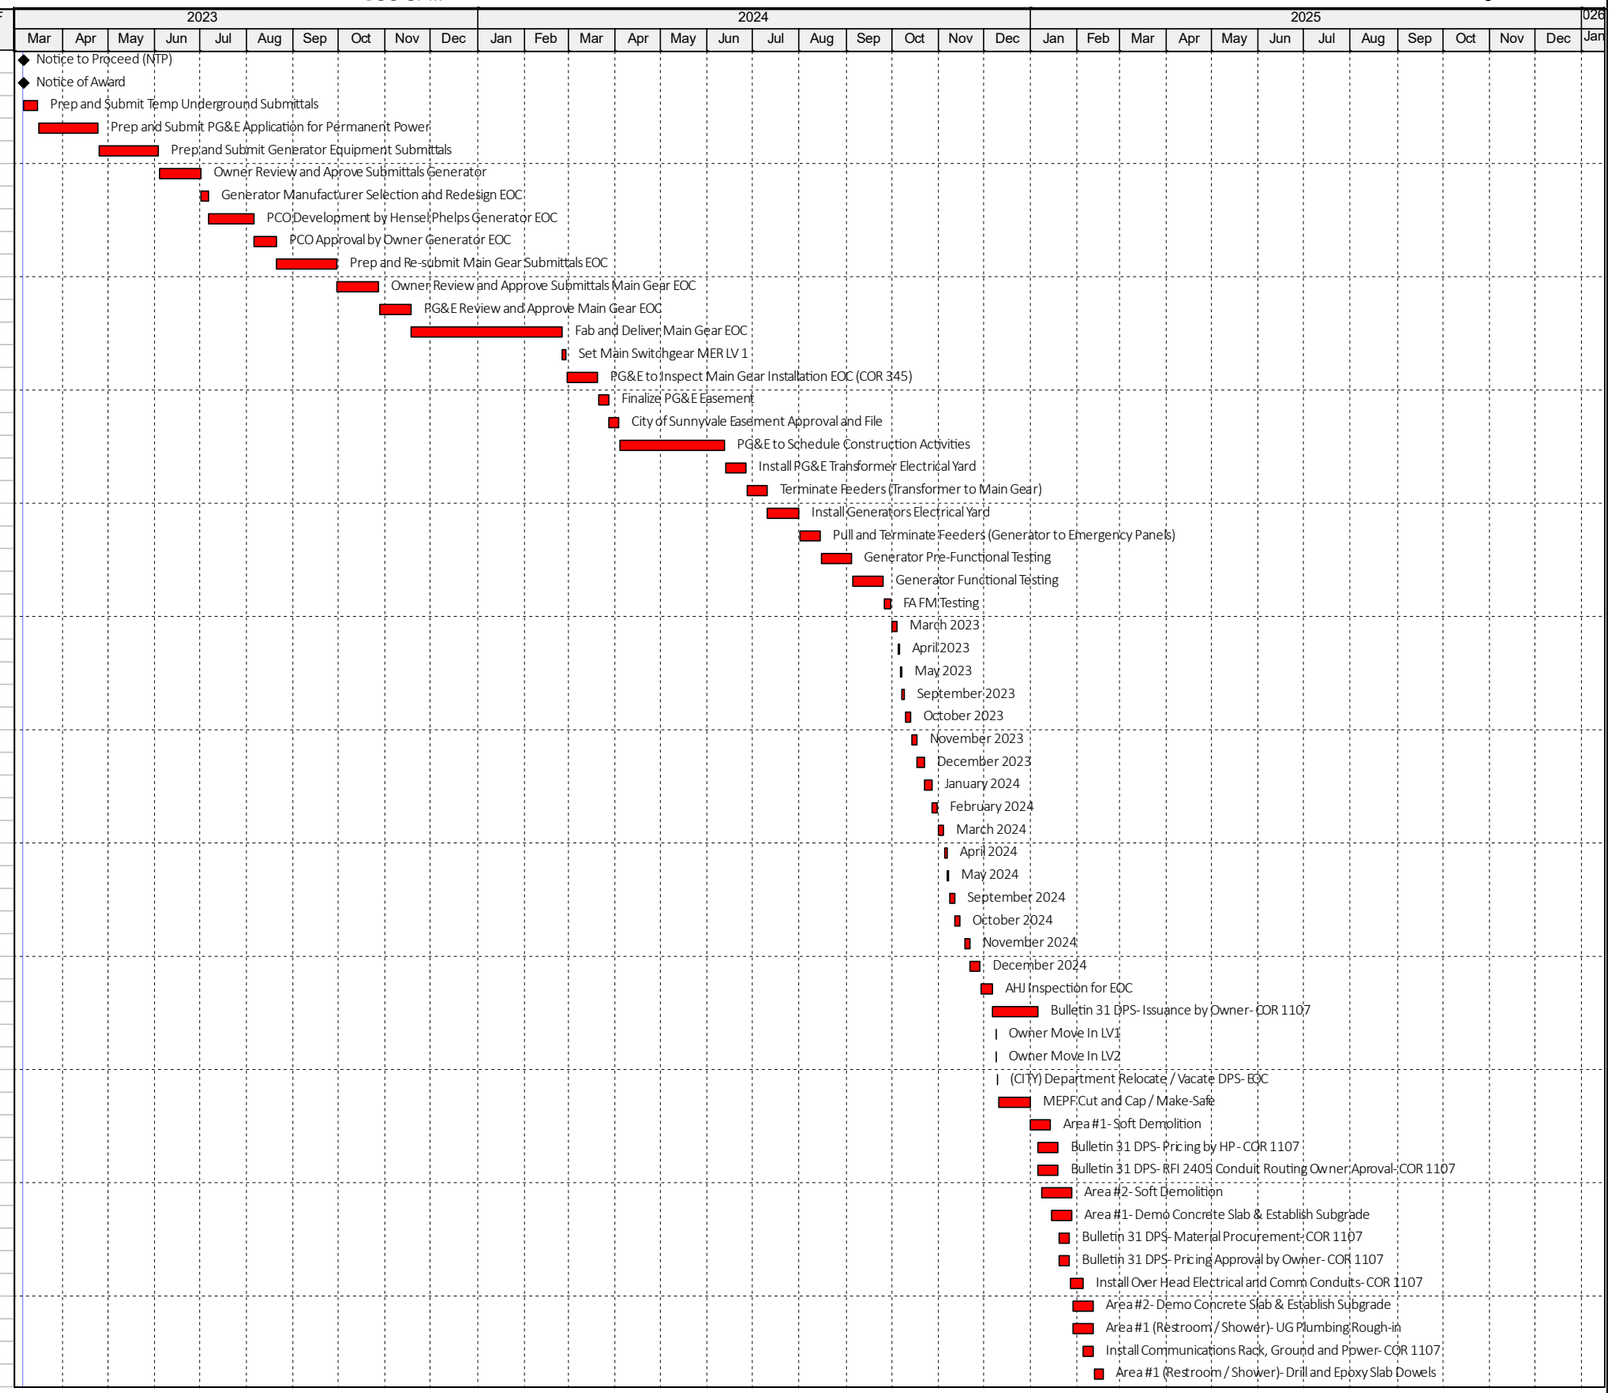

Actual Work | Critical Remaining Work | Remaining Work | ◆ Milestone

SCC CPM Sunnyvale Civic Center - CPM
Data Date: 06-Mar-23

Activity ID	Activity Name	OD	Start	Finish	TF
C-EOC-PH4-130	Area #2 (Evidence Room)- UG Plumbing Rough-in	10	12-Feb-25	25-Feb-25	0
COR1107-30	Pull, Dress, Label and Terminate Cabeling- COR 1107	5	12-Feb-25	18-Feb-25	0
C-EOC-PH4-140	Area #1 (Restroom / Shower)- FRP SOG	5	19-Feb-25	25-Feb-25	0
COR1107-40	Install CFCI Equipment- COR 1107	3	19-Feb-25	21-Feb-25	0
COR1107-50	Owner to Install Network Equipment- COR 1107	3	24-Feb-25	26-Feb-25	0
C-EOC-PH4-150	Area #2 (Evidence Room)- Drill and Epoxy Slab Dowels	5	26-Feb-25	04-Mar-25	0
C-EOC-PH4-170	OH Fire Protection Rough-in	5	26-Feb-25	04-Mar-25	0
C-EOC-PH4-180	OH Fire Alarm Rough-in	5	26-Feb-25	04-Mar-25	0
COR1107-60	Owner to Pull and Terminate Cabling- COR 1107	3	27-Feb-25	03-Mar-25	0
COR1107-70	Activate Data Room- COR 1107	3	04-Mar-25	06-Mar-25	0
C-EOC-PH4-160	Area #2 (Evidence Room)- FRP SOG	5	05-Mar-25	11-Mar-25	0
C-EOC-PH4-190	OH Mechanical Rough-in	10	05-Mar-25	18-Mar-25	0
C-CH-CXBFA-40	FA FM Testing	10	07-Mar-25	20-Mar-25	0
C-EOC-PH4-610	OH Fire Protection Rough-in	5	12-Mar-25	18-Mar-25	0
C-EOC-PH4-200	OH Plumbing Rough-in	5	19-Mar-25	25-Mar-25	0
C-EOC-PH4-430	OH Fire Protection Rough-in	5	19-Mar-25	25-Mar-25	0
A-RAIN-CH10	March 2023	4	21-Mar-25	24-Mar-25	0
A-RAIN-CH20	April 2023	2	25-Mar-25	26-Mar-25	0
C-EOC-PH4-210	OH Electrical / Data Rough-in	5	26-Mar-25	01-Apr-25	0
C-EOC-PH4-440	OH Fire Alarm Rough-in	5	26-Mar-25	01-Apr-25	0
A-RAIN-CH30	May 2023	1	27-Mar-25	27-Mar-25	0
A-RAIN-CH40	September 2023	2	28-Mar-25	29-Mar-25	0
A-RAIN-CH50	October 2023	4	30-Mar-25	02-Apr-25	0
C-EOC-PH4-220	Metal Stud Framing- Walls	10	02-Apr-25	15-Apr-25	0
C-EOC-PH4-450	OH Mechanical Rough-in	5	02-Apr-25	08-Apr-25	0
A-RAIN-CH60	November 2023	4	03-Apr-25	06-Apr-25	0
A-RAIN-CH70	December 2023	5	07-Apr-25	11-Apr-25	0
C-EOC-PH4-460	OH Plumbing Rough-in	5	09-Apr-25	15-Apr-25	0
A-RAIN-CH80	January 2023	5	12-Apr-25	16-Apr-25	0
C-EOC-PH4-240	Metal Stud Framing- Ceilings	5	16-Apr-25	22-Apr-25	0
C-EOC-PH4-470	OH Electrical / Data Rough-in	5	16-Apr-25	22-Apr-25	0
A-RAIN-CH90	February 2023	4	17-Apr-25	20-Apr-25	0
A-RAIN-CH100	March 2023	4	21-Apr-25	24-Apr-25	0
C-EOC-PH4-250	MEPFSS Rough-in @ Drywall Ceilings- Install	10	23-Apr-25	06-May-25	0
C-EOC-PH4-480	Metal Stud Framing- Walls	5	23-Apr-25	29-Apr-25	0
A-RAIN-CH110	April 2024	2	25-Apr-25	26-Apr-25	0
A-RAIN-CH120	May 2024	1	27-Apr-25	27-Apr-25	0
A-RAIN-CH130	September 2024	2	28-Apr-25	29-Apr-25	0
A-RAIN-CH140	October 2024	4	30-Apr-25	03-May-25	0
C-EOC-PH4-810	Plywood Wall Board- Install	5	30-Apr-25	06-May-25	0
A-RAIN-CH150	November 2024	4	04-May-25	07-May-25	0
C-EOC-PH4-270	Dywall / Tape / Finish- Ceilings	10	07-May-25	20-May-25	0
C-EOC-PH4-820	Electrical Equipment (Panels, UPS, etc.)- Install	10	07-May-25	20-May-25	0
A-RAIN-CH160	December 2024	5	08-May-25	12-May-25	0
A-RAIN-CH170	January 2025	5	13-May-25	17-May-25	0
A-RAIN-CH180	February 2025	4	18-May-25	21-May-25	0
C-EOC-PH4-280	Paint- 1st Coat	5	21-May-25	27-May-25	0
C-EOC-PH4-830	Electrical Wiring- Pull and Terminate	10	21-May-25	03-Jun-25	0
A-RAIN-CH190	March 2025	4	22-May-25	25-May-25	0
A-RAIN-CH200	April 2025	2	26-May-25	27-May-25	0
C-EOC-PH4-290	ACT Ceiling Grid- Install	5	28-May-25	03-Jun-25	0
A-RAIN-CH210	May 2025	1	28-May-25	28-May-25	0
C-CH-AHJ-10	AHJ Inspection for City Hall	4	29-May-25	03-Jun-25	0
MS-40	City Hall Substantial Completion	0		03-Jun-25*	0
CM-CH-200	City Hall Fire Marshal Sign-Off (TCO)	0		03-Jun-25	0
C-CH-PH3-10	CH- (CITY) Department Relocate / Vacate City Hall	10	04-Jun-25	17-Jun-25	0
C-CH-OWNER-120	Owner Move In LV1	10	04-Jun-25	17-Jun-25	0
C-CH-OWNER-130	Owner Move In LV2	10	04-Jun-25	17-Jun-25	0
C-CH-OWNER-140	Owner Move In LV3	10	04-Jun-25	17-Jun-25	0

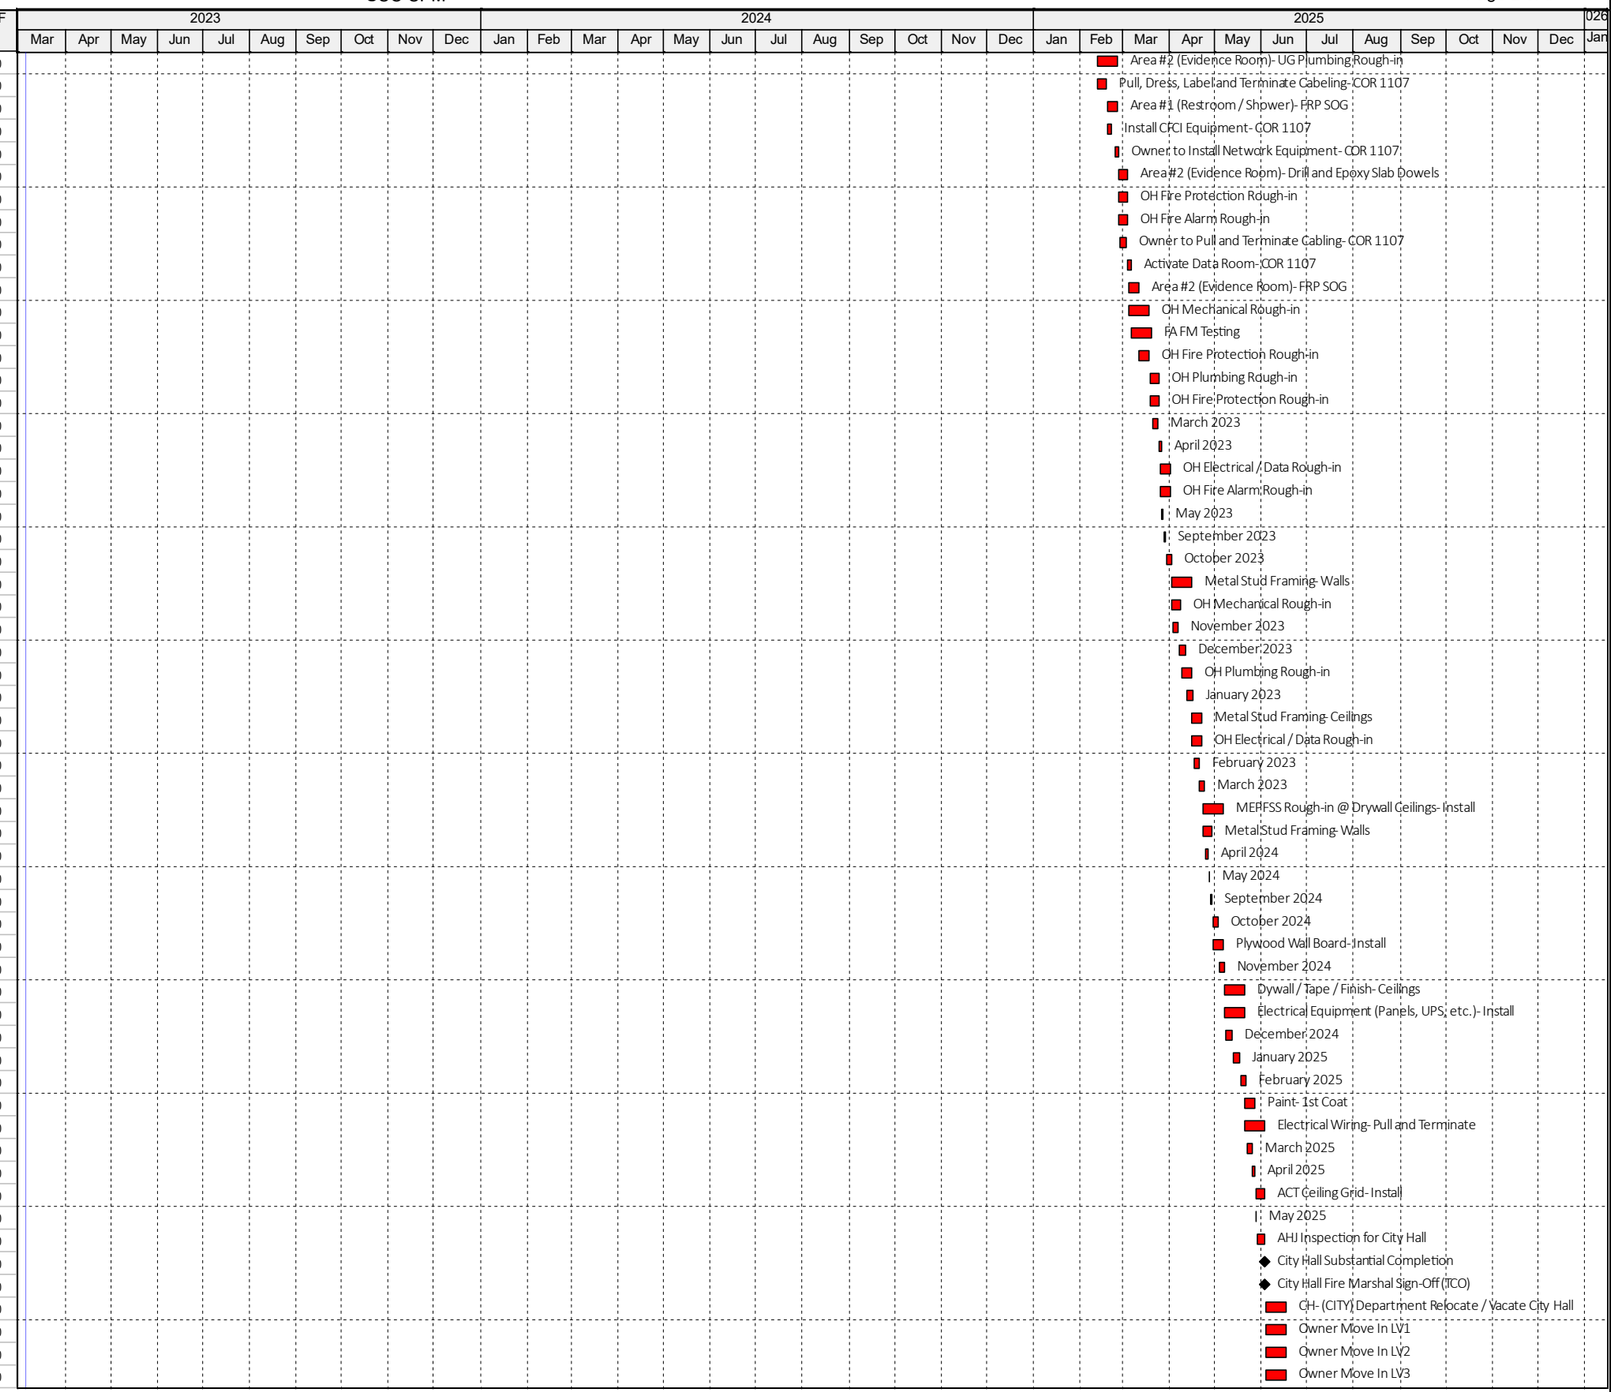

Actual Work
Critical Remaining Work
Remaining Work
Milestone

Activity ID	Activity Name	OD	Start	Finish	TF
C-CH-OWNER-150	Owner Move In LV4	10	04-Jun-25	17-Jun-25	0
C-EOC-PH4-300	MEPFSS Ceiling Devices @ ACT-Install	10	04-Jun-25	17-Jun-25	0
C-EOC-PH4-840	Special Systems Buildout (Cabinets, Racks, Cable Tray, etc.)	10	04-Jun-25	17-Jun-25	0
C-CH-DEMO-30	CH- MEPF Cut and Cap / Make-Safe	4	18-Jun-25	23-Jun-25	0
C-EOC-PH4-310	Flooring- Tile- Install	10	18-Jun-25	01-Jul-25	0
C-EOC-PH4-850	Fiber / Copper Rough-in	5	18-Jun-25	24-Jun-25	0
C-CH-DEMO-40	CH- Hazardous Material Abatment	10	24-Jun-25	07-Jul-25	0
C-EOC-PH4-860	Fiber / Copper / Low Voltage Cabling- Pull Cable	5	25-Jun-25	01-Jul-25	0
C-EOC-PH4-320	Wall Tile- Install	10	02-Jul-25	15-Jul-25	0
C-EOC-PH4-870	Terminate & Test Low Voltage Cabling	5	02-Jul-25	08-Jul-25	0
C-CH-DEMO-50	CH- Demo Structure / Concrete / Hardscape	5	08-Jul-25	14-Jul-25	0
C-EOC-PH4-880	(CITY) Network Equipment- Install	5	09-Jul-25	15-Jul-25	0
C-CH-DEMO-60	CH- Backfill Basement & Establish Rough Grade	5	15-Jul-25	21-Jul-25	0
C-EOC-PH4-380	Doors and Hardware- Install	5	16-Jul-25	22-Jul-25	0
C-EOC-PH4-890	(CITY) Low Voltage Cabling- Final Terminations, Testing, Cross-Connects	5	16-Jul-25	22-Jul-25	0
C-PH6-GEN-10	Area #9- UG Utility Rough-in (SD and Electrical) @ Generator / Trash Enc	5	22-Jul-25	28-Jul-25	0
C-EOC-PH4-2010	Test, Balance & Cx Systems	5	23-Jul-25	29-Jul-25	0
C-EOC-PH4-900	(CITY) Activate Data Room	5	23-Jul-25	29-Jul-25	0
C-PH6-GEN-20	Area #9- FRP Grade Beam / Footing @ Generator / Trash Enclosure	5	29-Jul-25	04-Aug-25	0
C-EOC-PH4-2020	Fire Alarm- Pre-Test	5	30-Jul-25	05-Aug-25	0
C-PH6-GEN-30	Area #9- CMU Block Wall- Install	5	05-Aug-25	11-Aug-25	0
C-EOC-PH4-2040	Fire Alarm- Test w/ City & Fire Dep't.	10	06-Aug-25	19-Aug-25	0
C-PH6-GEN-40	Area #9- FRP SOG & Concrete Pads @ Generator / Trash Enclosure	5	12-Aug-25	18-Aug-25	0
C-PH6-GEN-60	Area #9- Generator & Load Bank- Install	15	19-Aug-25	08-Sep-25	0
C-EOC-PH4-2050	Fire / Life-Safety Inspections- City & Fire Dep't.	10	20-Aug-25	02-Sep-25	0
C-EOC-PH4-2060	Substantial Completion- DPS	7	03-Sep-25	11-Sep-25	0
C-PH6-GEN-140	Microgrid & BMS Interface Commissioning	15	09-Sep-25	29-Sep-25	0
MS-50	DPS T.I. Substantial Completion	0		11-Sep-25*	0
C-PH6-CX-10	Permanent Generator Pre-Functional Testing	5	30-Sep-25	06-Oct-25	0
C-PH6-CX-20	Permanent Generator FINAL Testing	5	07-Oct-25	13-Oct-25	0
COR-224-90	Remove Temporary Generator at City Hall (COR224)	3	14-Oct-25	16-Oct-25	0
MS-60	Complete Project Substantial Completion (Phase 6 Complete)	0		16-Oct-25*	0
MS-80	Project Complete	0		16-Oct-25	0

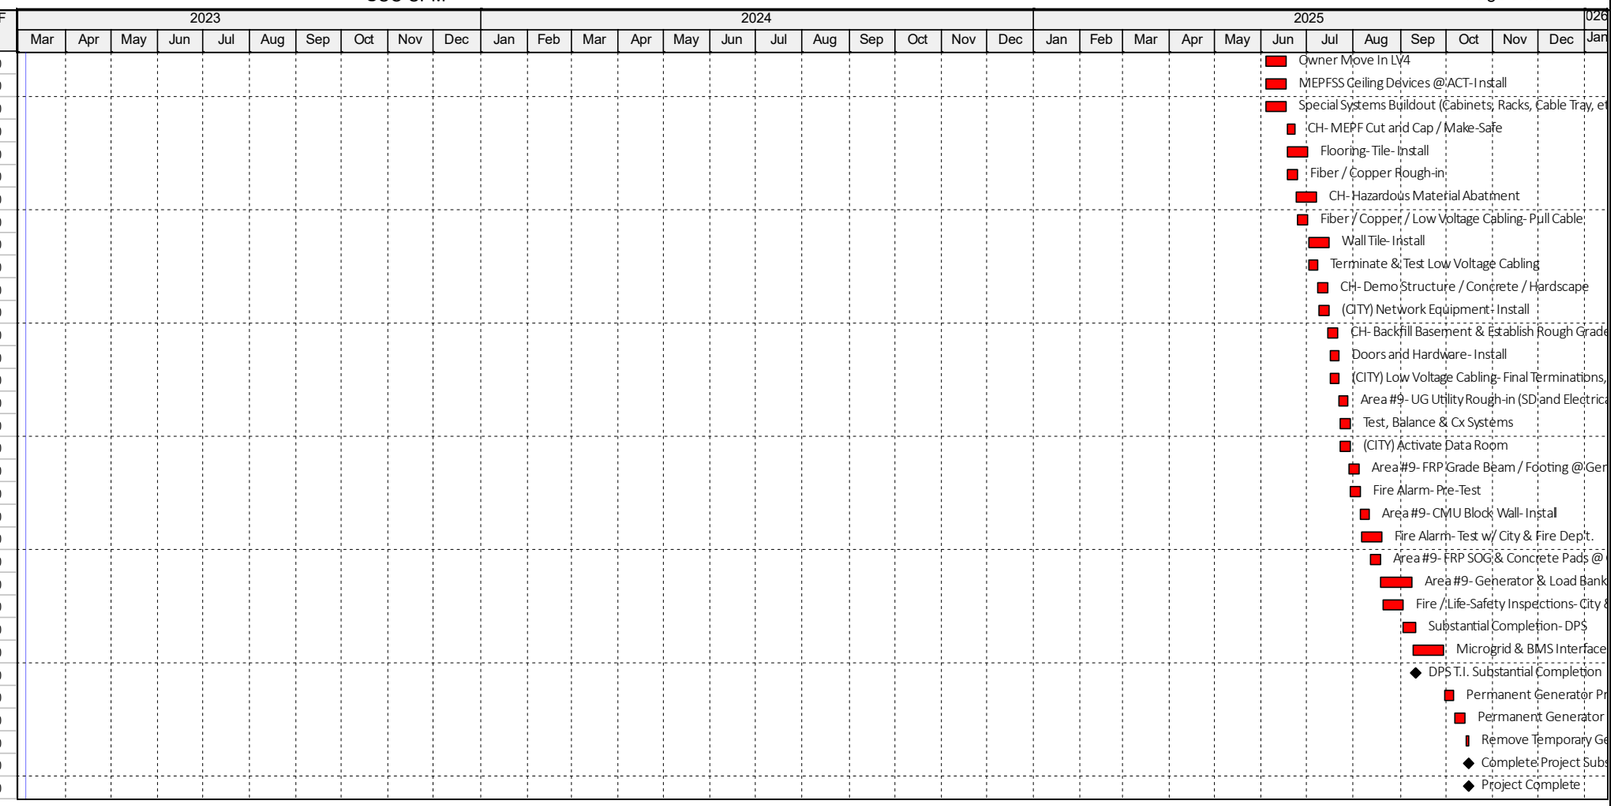

Actual Work | Critical Remaining Work
Remaining Work ◆ | ◆ Milestone

SCC CPM Sunnyvale Civic Center - CPM
Data Date: 06-Mar-23
