
	Duration		2 Dec 2, '12 Dec 9, '12 Dec 16, '12 Dec 23, '12 Dec 30, '12 Jan 6, '13 Jan 13, '13 Jan 20, '13 Jan 27, '13 Feb 3, '13 Feb 10, '13 Feb 10, '13 Feb 10, '13 Mar 3, '13 Mar 10, '13 Mar 17, '13 Mar 24, '13 Mar 31, '13 Apr 7, '13 Apr 7, '13 Apr 14, '13 Apr 14, '13 Apr 14, '13 Apr 14, '14 Apr 14, '15 S M T W T F S S
		Fri 11/30/12 Tue 3/5/13	Architectural Drawings - 50% CDs
Architectural Drawings - 50% CDs	16 days	Fri 11/30/12 Fri 12/21/12	
	0 days	Wed 12/5/12 Wed 12/5/12	12/5
backgrounds to MEPs	U uays	weu 12/3/12 weu 12/3/12	
-	14 days	Thu 12/6/12 Tue 12/25/12	Elect / Mech Design - 50% CEDs
CEDs	14 0893	110 12/0/12 100 12/23/12	
	15 days	Mon 12/24/12Fri 1/11/13	Structural Design - Stairs
-	5 days	Mon 12/24/12Fri 12/28/12	Bid Process - Drywall FP
			Arch / Mech Drawing Coordination
Arch / Mech Drawing Coordination	5 days	Mon Fri 12/28/12 12/24/12	
	0.1		Elect / Mech Design - 100% CDs
Elect / Mech Design - 100% CDs	9 days	Mon Thu 1/10/13 12/31/12	
	0 days		Architectural Drawings - 100% CDs
Architectural Drawings - 100% CDs	9 uays	Mon Thu 1/10/13 12/31/12	
	10 days		Early Release of Drywall, FP
Early Release of Drywall, FP		Mon 12/31/12Fri 1/11/13	
		Fri 1/11/13 Tue 1/22/13	Bid Process - 100% CDs
-		Fri 1/11/13 Wed 1/30/13	Permitting - 100% CDs
Bid Process - Structural & Stairs		Mon 1/14/13 Fri 1/18/13	Bid Process - Structural & Stairs
Bid Leveling / Establish GMP		Wed 1/23/13 Mon 1/28/13	Bid Leveling / Establish GMP
	3 days	Mon 1/21/13 Wed 1/23/13	Award Structural and Stair Subcontract
Subcontract			
		Mon 1/28/13 Mon 1/28/13	
Client Review & Approve GMP		Tue 1/29/13 Thu 1/31/13	Client Review & Approve GMP
Final GMP Approval	0 days	Thu 1/31/13 Thu 1/31/13	×1/31
Award Subcontracts	14 days	Fri 2/1/13 Sat 2/16/13	Award Subcontracts
Receive Insurance Certificates	14 days	Mon 2/18/13 Tue 3/5/13	Receive Insurance Certificates
Procure Long Lead Items	80 days	Mon 12/31/12Fri 4/5/13	· · · · · · · · · · · · · · · · · · ·
Early Procurement of LL1	20 days	Wed 1/23/13 Thu 2/14/13	Early Procurement of LL1
Lighting Submittals	7 days	Wed 1/23/13 Wed 1/30/13	Lighting Submittals
Mechanical Submittals	7 days	Wed 1/23/13 Wed 1/30/13	Mechanical Submittals
Lighting and Electrical	40 days	Thu 1/31/13 Mon 3/18/13	Lighting and Electrical
Mechanical Equipment	30 days	Thu 1/31/13 Wed 3/6/13	Mechanical Equipment
		Thu 1/31/13 Sat 2/16/13	Mechanical Duct
Fire Protection Shop Drawings		Mon Fri 1/11/13	Fire Protection Shop Drawings
	,.	12/31/12	
Stair Shop Drawings	8 days	Thu 1/24/13 Fri 2/1/13	Stair Shop Drawings
	10 days	Fri 2/1/13 Tue 2/12/13	Submittals
		Fri 2/1/13 Tue 2/12/13	Shop Drawings
Specialty Items (Fireplace,			Specialty Items (Fireplace, Living Wall,
Living Wall, etc)	,.		
Stair Shop Drawing Approval	3 davs	Sat 2/2/13 Tue 2/5/13	Stair Shop Drawing Approval
		Wed 2/6/13 Fri 2/22/13	Structural Steel
		Sat 2/2/13 Tue 2/19/13	Door Frames
		Wed 2/13/13 Tue 3/19/13	Doors and Hardware
		Wed 2/13/13 Tue 3/19/13 Wed 2/13/13 Tue 3/19/13	Flooring
-		Wed 2/13/13 Tue 3/19/13 Wed 2/13/13 Wed 3/13/13	Wall Coverings
-			Stone and Tile
		Wed 2/13/13 Thu 3/7/13	Stole and the Millwork
		Wed 2/13/13 Wed 3/13/13	
		Wed 2/13/13 Tue 3/19/13	Signage AV Equipment
		Wed 2/13/13 Wed 3/13/13	
			Security Equipment
-			Fiberglass Column Covers
		Wed 2/13/13 Tue 3/19/13	Window Shades
Operable Walls		Wed 2/13/13 Sat 3/30/13	Operable Walls
			3Form Panels and Tops
Mobilization	26 days	Wed 1/23/13 Thu 2/21/13	
Set up Onsite Office	4 days	Wed 1/23/13 Sat 1/26/13	Set up Onsite Office
	2 days	Wed 1/23/13 Thu 1/24/13	Implement Onsite Safety Program
Program			
Install Filter Media @ Return	2 days	Fri 1/25/13 Sat 1/26/13	📥 Install Filter Media @ Return Air Intakes
Air Intakes			
ASC Final Schedule - MB E Task		Milest	ne 🔶 Project Summary 🖵 🖳 External Milestone 🔄 Inactive Milestone 🔄 Manual Task 🖬 Manual Summary Rollup 📥 Start-only 🖬 Deadline 🖡
u 1/31/13 Split		Summ	ry External Tasks Inactive Task Inactive Summary 🖓 Duration-only Inactive Summary Finish-only I Progress

	u 1/31/13 Split		Summar	External Tasks Inactive Task Inactive Summary Unactive Summary Unactive Summary Unactive Summary Unactive Summary
niect: A	ASC Final Schedule - MB E Task		Mileston	e 🔶 Project Summary 🖓 External Milestone 🔶 Inactive Milestone 🔄 Manual Task 🖬 Manual Summary Rollup 🚃
	IT Set-up	5 days	Tue 3/26/13 Sat 3/30/13	
	Final Cleaning	4 days	Tue 3/26/13 Fri 3/29/13	
	Punchlist	7 days	Mon 3/25/13 Mon 4/1/13	
	Install AV Equipment	5 days	Mon 3/25/13 Fri 3/29/13	
_	Pre-test Life Safety System	2 days	Sat 3/23/13 Mon 3/25/13	
_	Install Signage	0 days 5 days	Thu 3/21/13 Tue 3/26/13	
_	Furniture Cabling Security System Activation	8 days 0 days	Sat 3/16/13 Mon 3/25/13 Sat 3/16/13 Sat 3/16/13	
_	Install office Furniture	8 days	Sat 3/16/13 Mon 3/25/13	
	Touch up and Detailing Project	t 7 days	Mon 3/11/13 Mon 3/18/13	
	Install Resilient Flooring	4 days	Mon 3/11/13 Thu 3/14/13	
	Install Window Film	5 days	Fri 3/8/13 Wed 3/13/13	
-	Install Doors and Hardware	5 days	Fri 3/8/13 Wed 3/13/13	
	Install Carpet Tile	7 days	Fri 3/8/13 Fri 3/15/13	
	Floor Preparation	3 days	Thu 3/7/13 Sat 3/9/13	
	Install Security Equipment	10 days	Tue 3/5/13 Fri 3/15/13	
	Install Glass @ Offices	4 days	Mon 3/4/13 Thu 3/7/13	
	Install Ceiling Tile	6 days	Thu 2/28/13 Wed 3/6/13	
	Inspections above Ceiling	2 days 0 days	Wed 2/27/13 Wed 2/27/13	▶ 2/27
	Measure for Glass	2 days	Tue 2/26/13 Wed 2/27/13	Measure for Glass
	Start-up / Commission HVAC Equipment	5 days	rue 2/20/13 Sat 3/2/13	Start-up /
	IT Jack / Trim / Test	8 days	Mon 2/25/13 Tue 3/5/13	Start-up /
	Install Millwork	10 days	Mon 2/25/13 Thu 3/7/13	
	Rock / Tape / Paint Hard Lids	•	Wed 2/20/13 Fri 3/1/13	Rock / Tape
	Install Registers @ Ceiling	7 days	Tue 2/19/13 Tue 2/26/13	Install Registers @ C
	Inspections for Hard Lids	0 days	Tue 2/19/13 Tue 2/19/13	
	Install Doors & Glazing Frame		Mon 2/18/13 Tue 2/26/13	Install Doors & Glazi
	Install Sprinkler Drops @ Ceiling Grid	8 days	Mon 2/18/13 Tue 2/26/13	Install Sprinkler Dro
	Install Lighting @ Ceiling	10 days	Sat 2/16/13 Wed 2/27/13	
	Install Ceiling Grid	7 days	Thu 2/14/13 Thu 2/21/13	Install Ceiling Grid
	Painting / WC @ Walls	12 days	Mon 2/11/13 Sat 2/23/13	Painting / WC @ Walls
	Install Sound Masking System	6 days	Wed 2/6/13 Tue 2/12/13	Install Sound Masking System
	Above Ceiling			
	Rough-in Voice/Data/Security	5 days	Sat 2/2/13 Thu 2/7/13	Rough-in Voice/Data/Security Above Ceiling
	Equipment			
	Install New Mechanical	10 days	Sat 2/2/13 Wed 2/13/13	Install New Mechanical Equipment
	Taping @ Walls and Soffits	10 days	Fri 2/1/13 Tue 2/12/13	Taping @ Walls and Soffits
	Framing / MEP Inspections	0 days	Thu 1/24/13 Thu 1/24/13	▲ 1/24
	Soffits, Reveals			
	Sheetrock / Insulation @ Wall	s, 10 days	Sat 1/26/13 Wed 2/6/13	Sheetrock / Insulation @ Walls, Soffits, Reveals
	Inspections @ Walls			
	Partial Framing / MEP	0 days	Thu 1/24/13 Thu 1/24/13	▶ 1/24
	Coring for Electrical/Data/AV/Security	2 uays	WI011/21/15	
_		2 days	Fri 1/18/13 Mon 1/21/13	Coring for Electrical/Data/AV/Security
	Layout Furniture for Floor Monuments	2 days	Wed 1/16/13 Thu 1/17/13	Layout Furniture for Floor Monuments
-	Rough-in MEPs above Ceiling		Mon 1/7/13 Fri 2/8/13	Rough-in MEPs above Ceiling
_	Rough-in MEPs @ Walls	12 days	Wed 1/9/13 Thu 1/24/13	Rough-in MEPs @ Walls
	Metal Stud Framing	12 days	Mon 1/7/13 Tue 1/22/13	Metal Stud Framing
-	Architects Approval of Layout		Fri 1/4/13 Fri 1/4/13	Architects Approval of Layout
	Sand & Seal Concrete Floors		Wed 1/2/13 Tue 1/8/13	Sand & Seal Concrete Floors
-	Layout Walls, Hard Lids, MEPs		Thu 12/27/12 Fri 1/4/13	
_	BEGIN 6 DAY WORK WEEK	0 days	Thu 12/27/12 Thu 12/27/12	◆ <u>12/27</u>
	onstruction 12th Floor	78 days	Thu 12/27/12 Mon 4/1/13	·
	Equipment			
	Pre-stocking of Materials and	20 days	Wed 1/30/13 Thu 2/21/13	Pre-stocking of Materials and Equ
	(all floors)			
	Install Temp Power & Lighting	10 davs	Mon 1/28/13 Thu 2/7/13	Install Temp Power & Lighting (all floors)
	Protection of Finishes to remain	5 days	Mon 1/28/13 Fri 2/1/13	Protection of Finishes to remain

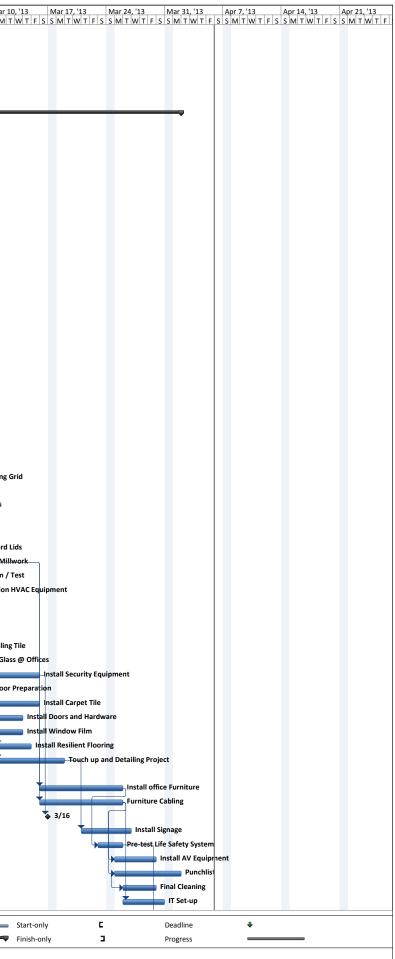

Duration	Start Finish	2 Dec 2, '12 Dec 9, '12 Dec 16, '12 Dec 23, '12 Dec 30, '12 Jan 6, '13 Jan 13, '13 Jan 20,
0 days	Fri 3/29/13 Fri 3/29/13	
0 days	Fri 3/29/13 Fri 3/29/13	♦ [★] 3/29
0 days	Mon 4/1/13 Mon 4/1/13	% 4/1
68 days	Thu 1/10/13 Mon 4/1/13	
7 days	Thu 1/10/13 Fri 1/18/13	Layout Walls, Hard Lids, MEPs
1 day	Mon 1/21/13 Mon 1/21/13	Architects Approval of Layout
25 days	Tue 1/22/13 Tue 2/19/13	Rough-in MEPs above Ceiling
5 days	Mon 1/21/13 Fri 1/25/13	Sand & Seal Concrete Floors
10 days	Tue 1/22/13 Fri 2/1/13	Metal Stud Framing
10 days	Thu 1/24/13 Mon 2/4/13	Rough-in MEPs @ Walls
2 days	Mon 1/28/13 Tue 1/29/13	Layout Furniture for Floor Monuments
1 day	Wed 1/30/13 Wed 1/30/13	The Partial Framing / MEP Inspections @ Walls
2 days	Wed 1/30/13 Thu 1/31/13	Coring for Electrical/Data/AV/Security
, 8 days	Thu 1/31/13 Fri 2/8/13	Sheetrock / Insulation @ Walls, Soffits, Reveals
0 days	Mon 2/4/13 Mon 2/4/13	2/4
10 days	Tue 2/5/13 Fri 2/15/13	Taping @ Walls and Soffits
5 days	Tue 2/5/13 Sat 2/9/13	Rough-in Voice/Data/Security Above Ceiling
10 days	Thu 2/7/13 Mon 2/18/13	
6 days	Fri 2/8/13 Thu 2/14/13	Install Sound Masking System
8 days	Tue 2/12/13 Wed 2/20/13	Painting / WC @ Walls
7 days	Sat 2/16/13 Sat 2/23/13	Install Ceiling Grid
10 days	Tue 2/19/13 Fri 3/1/13	Install Lighting @ Ceiling
8 days	Wed 2/20/13 Thu 2/28/13	Install Sprinkler Drops @ Ceiling Grid
7 days	Wed 2/20/13 Wed 2/27/13	Install Registers @ Ceiling
0 days	Thu 2/21/13 Thu 2/21/13	
8 days	Thu 2/21/13 Fri 3/1/13	T Jack / Trim / Test
9 days	Fri 2/22/13 Mon 3/4/13	Kock / Tape / Paint Hard Lids
5 days	Wed 2/27/13 Mon 3/4/13	Start-up / Commission HVAC Equipment
0 days	Fri 3/1/13 Fri 3/1/13	\$3/1
5 days	Sat 3/2/13 Thu 3/7/13	Install Ceiling Tile
5 days	Mon 3/4/13 Fri 3/8/13	Install Doors & Glazing Frames
		Floor Preparation
2 days	Fri 3/8/13 Sat 3/9/13	Measure for Glass
		→
5 days	Sat 3/9/13 Thu 3/14/13	Install Resilient Flooring
6 days	Wed 3/13/13 Tue 3/19/13	Tanan Install Carpet Tile
5 days	Thu 3/14/13 Tue 3/19/13	Install Glass @ Offices
7 days	Mon 3/18/13 Mon 3/25/13	Touch up and Detailing Project
4 days	Mon 3/18/13 Thu 3/21/13	
		Install Security Equipment
	Wed 3/20/13 Sat 3/23/13	Install Doors and Hardware
		Install office Furniture
		Furniture Cabling
		Install AV Equipment
5 days	Mon 3/25/13 Fri 3/29/13	Install Signage
		Pre-test Life Safety System
		Punchlist
		IT Set-up
		3/27
		Final Cleaning
		3/28
		\$3/28
		₩4/1
	Miles	one 🔶 Project Summary 🖓 🖅 External Milestone 🔶 Inactive Milestone 💠 Manual Task 🖬 🖬 Manual Summary Rollup 🔤 Start-only 🖬 Deadline 🔮
	0 days 0 days 7 days 1 day 25 days 10 days 2 days 10 days 2 days 1 day 3 days 1 day 3 days 1 days 5 days 1 days 3 days 1 days 3 days 1 days 3 da	0 daysFri 3/29/13Fri 3/29/130 daysFri 3/29/13Fri 3/29/130 daysMon 4/1/13Mon 4/1/1368 daysThu 1/10/13Fri 1/18/131 dayMon 1/21/13Mon 1/21/131 dayMon 1/21/13Fri 1/25/135 daysTue 1/22/13Fri 2/1/1310 daysTue 1/22/13Fri 2/21/1310 daysTue 1/24/13Mon 2/4/132 daysMon 1/28/13Tue 1/29/132 daysMcd 1/30/13Ked 1/30/132 daysMcd 1/30/13Fri 2/8/130 daysTue 2/5/13Fri 2/8/1310 daysTue 2/5/13Sta 2/9/1310 daysTue 2/5/13Sta 2/9/1310 daysTue 2/1213Mon 2/18/135 daysTue 2/1213Mon 2/18/1310 daysTue 2/1213Ked 2/20/1310 daysTue 2/1213Ked 2/20/1310 daysTue 2/1213Ked 2/20/1310 daysTue 2/113Fri 3/1138 daysTue 2/21/13Fri 3/139 daysFri 3/213Mon 3/4139 daysFri 3/213Sta 3/9/139 daysFri 3/113Sta 3/9/139 daysFri 3/13Sta 3/9/139 daysFri 3/13Sta 3/9/139 daysFri 3/13Sta 3/9/139 daysFri 3/213Kal/139 daysFri 3/213Kal/139 daysFri 3/213Kal/139 daysFri 3/213Kal/213 <trr>9 daysFri 3/213Kal/213</trr>

D Ta	ask Name	Duration	Start	Finish	2 Dec 2, '12 Dec 9, '12 Dec 16, '12 Dec 3, '12 Dec 3, '12 Dec 30, '12 Jan 6, '13 Jan 20, '
57	Layout Walls, Hard Lids, MEPs	5 days	Thu 1/17/13		
3	Rough-in MEPs above Ceiling	25 days	Mon 1/21/13	Mon 2/18/13	Rough-in MEPs above Ceiling
,	Sand & Seal Concrete Floors	5 days	Tue 1/22/13	Sat 1/26/13	Sand & Seal Concrete Floors
0	Architects Approval of Layout	1 day	Wed 1/23/13	Wed 1/23/13	Architects Approval of Layout
1	Metal Stud Framing		Thu 1/24/13		Metal Stud Framing
2	Rouch-in MEPs @ Walls		Sat 1/26/13		Rouch-in MEPs @ Walls
3	Layout Furniture for Floor	2 days	Wed 1/30/13		Layout Furniture for Floor Monuments
-	Monuments	_ aays			
4	Partial Framing / MEP	1 day	Fri 2/1/13	Fri 2/1/12	Tarial Framing / MEP Inspections @ Walls
•	Inspections @ Walls	1 day	111 2/ 1/ 13	1112/1/13	
		2	5.2/4/42	6-+ 2/2/42	Coring for Electrical/Data/AV/Security
55	Coring for Electrical/Data/AV/Security	2 days	Fri 2/1/13	Sat 2/2/13	
66	Sheetrock / Insulation @ Walls Soffits, Reveals	s, 8 days	Sat 2/2/13	Mon 2/11/13	Sheetrock / Insulation @ Walls, Soffits, Reveals
57		0 days	Wed 2/6/13		2/6
8		10 days			Taping @ Walls and Soffits
9	Rough-in Voice/Data/Security	5 days	Thu 2/7/13	Tue 2/12/13	Rough-in Voice/Data/Security Above Ceiling
	Above Ceiling				
)	Install New Mechanical	10 days	Sat 2/9/13	Wed 2/20/13	Install New Mechanical Equipment
	Equipment				
	Install Sound Masking System	6 days	Mon 2/11/13	Sat 2/16/13	Install Sound Masking System
	Painting / WC @ Walls	8 days	Thu 2/14/13	Fri 2/22/13	Painting / WC @ Walls
	Install Ceiling Grid	7 days	Tue 2/19/13	Tue 2/26/13	Install Ceiling Grid
	Install Lighting @ Ceiling	10 days	Thu 2/21/13	Mon 3/4/13	Install Lighting @ Ceiling
5	Install Sprinkler Drops @	8 days	Fri 2/22/13		Install Sprinkler Drops @ Ceiling Grid
	Ceiling Grid				
	Install Registers @ Ceiling	7 days	Fri 2/22/13	Fri 3/1/13	Install Registers @ Ceiling
	Inspections for Hard Lids	0 days	Sat 2/23/13		2/23
-	IT Jack / Trim / Test	8 days	Sat 2/23/13		IT Jack / Trim / Test
-	Rock / Tape / Paint Hard Lids		Mon 2/25/13		Rock / Tape / Paint Hard Lids
	Start-up / Commission HVAC		Fri 3/1/13		Start-up / Commission HVAC Equipment
	Equipment	Judys		.,	
1		0 days	Mon 2/4/12	Mon 2/4/12	3/4
_	Inspections above Ceiling	0 days	Mon 3/4/13		♦
2	Install Ceiling Tile	5 days	Tue 3/5/13		
	Install Doors & Glazing Frames		Wed 3/6/13		
1 -	Floor Preparation	2 days	Mon 3/11/13		Floor Preparation
5	Measure for Glass	2 days	Mon 3/11/13		
5	Install Millwork	7 days	Tue 3/12/13		
'	Install Resilient Flooring	5 days	Tue 3/12/13		Install Resilient Flooring
_	Install Carpet Tile	6 days	Fri 3/15/13	Thu 3/21/13	Install Carpet Tile
_		5 days	Sat 3/16/13	Thu 3/21/13	Install Glass @ Offices
)	Touch up and Detailing Project	t 7 days	Wed 3/20/13	Wed 3/27/13	Touch up and Detailing Project
	Install Window Film	4 days	Wed 3/20/13	Sat 3/23/13	Install Window Film
	Install Security Equipment	7 days	Fri 3/22/13	Fri 3/29/13	Install Security Equipment
	Install Doors and Hardware	4 days	Fri 3/22/13	Tue 3/26/13	Install Doors and Hardware
	Install office Furniture	8 days	Fri 3/22/13	Sat 3/30/13	Install office Furniture
	Furniture Cabling	6 days	Fri 3/22/13	Thu 3/28/13	Furniture Cabling
	Install Fireplace	5 days	Fri 3/22/13		Install Fireplace
	Install AV Equipment	5 days	Tue 3/26/13		Install AV Equipment
	Install Signage	5 days	Wed 3/27/13		
-		2 days	Wed 3/27/13 Wed 3/27/13		Pre-test Life Safety System
_	Punchlist		Wed 3/27/13 Wed 3/27/13		Punchlist
		5 days			IT Set-up
_	IT Set-up	5 days	Wed 3/27/13		▲ 3/29
_	Security System Activation	0 days	Fri 3/29/13		
	Final Cleaning	4 days	Thu 3/28/13		Final Cleaning
_	Life Safety Test	0 days	Fri 3/29/13		3/29
	Substantial Completion	0 days	Fri 3/29/13	Fri 3/29/13	♦ [*] 3/29
;	Tenant Occupancy	0 days	Mon 4/1/13	Mon 4/1/13	₩4/1
	ASC Final Schedule - MB E Task u 1/31/13 Split			Milesto	
