




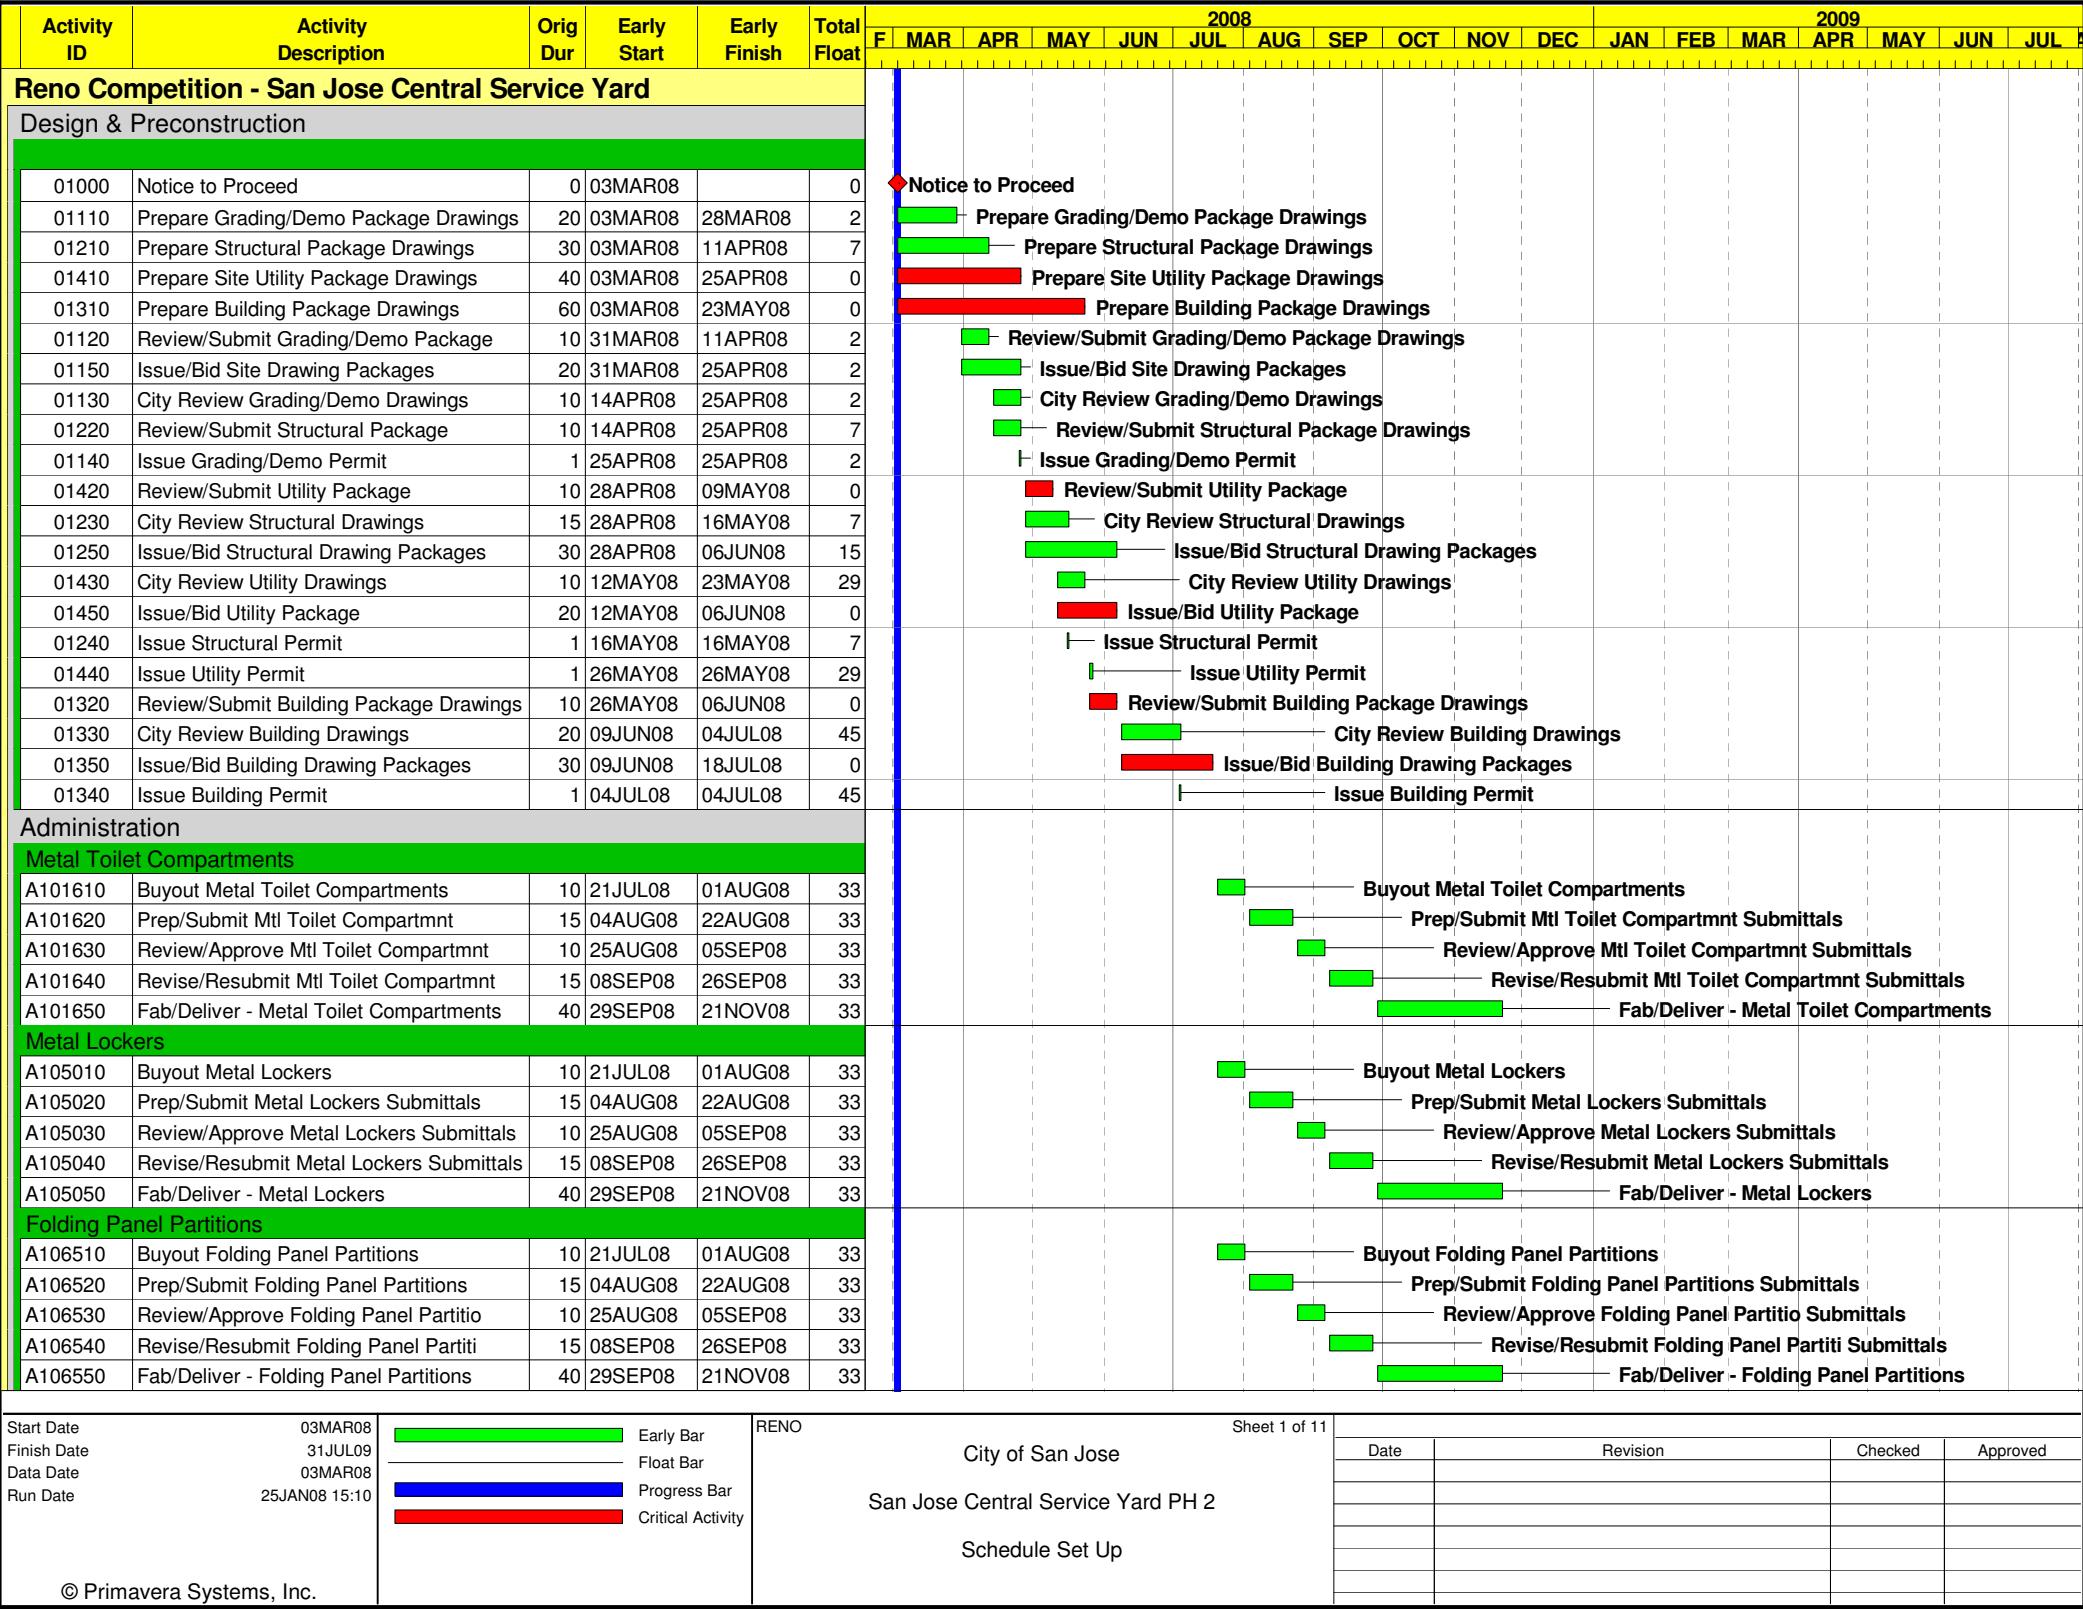

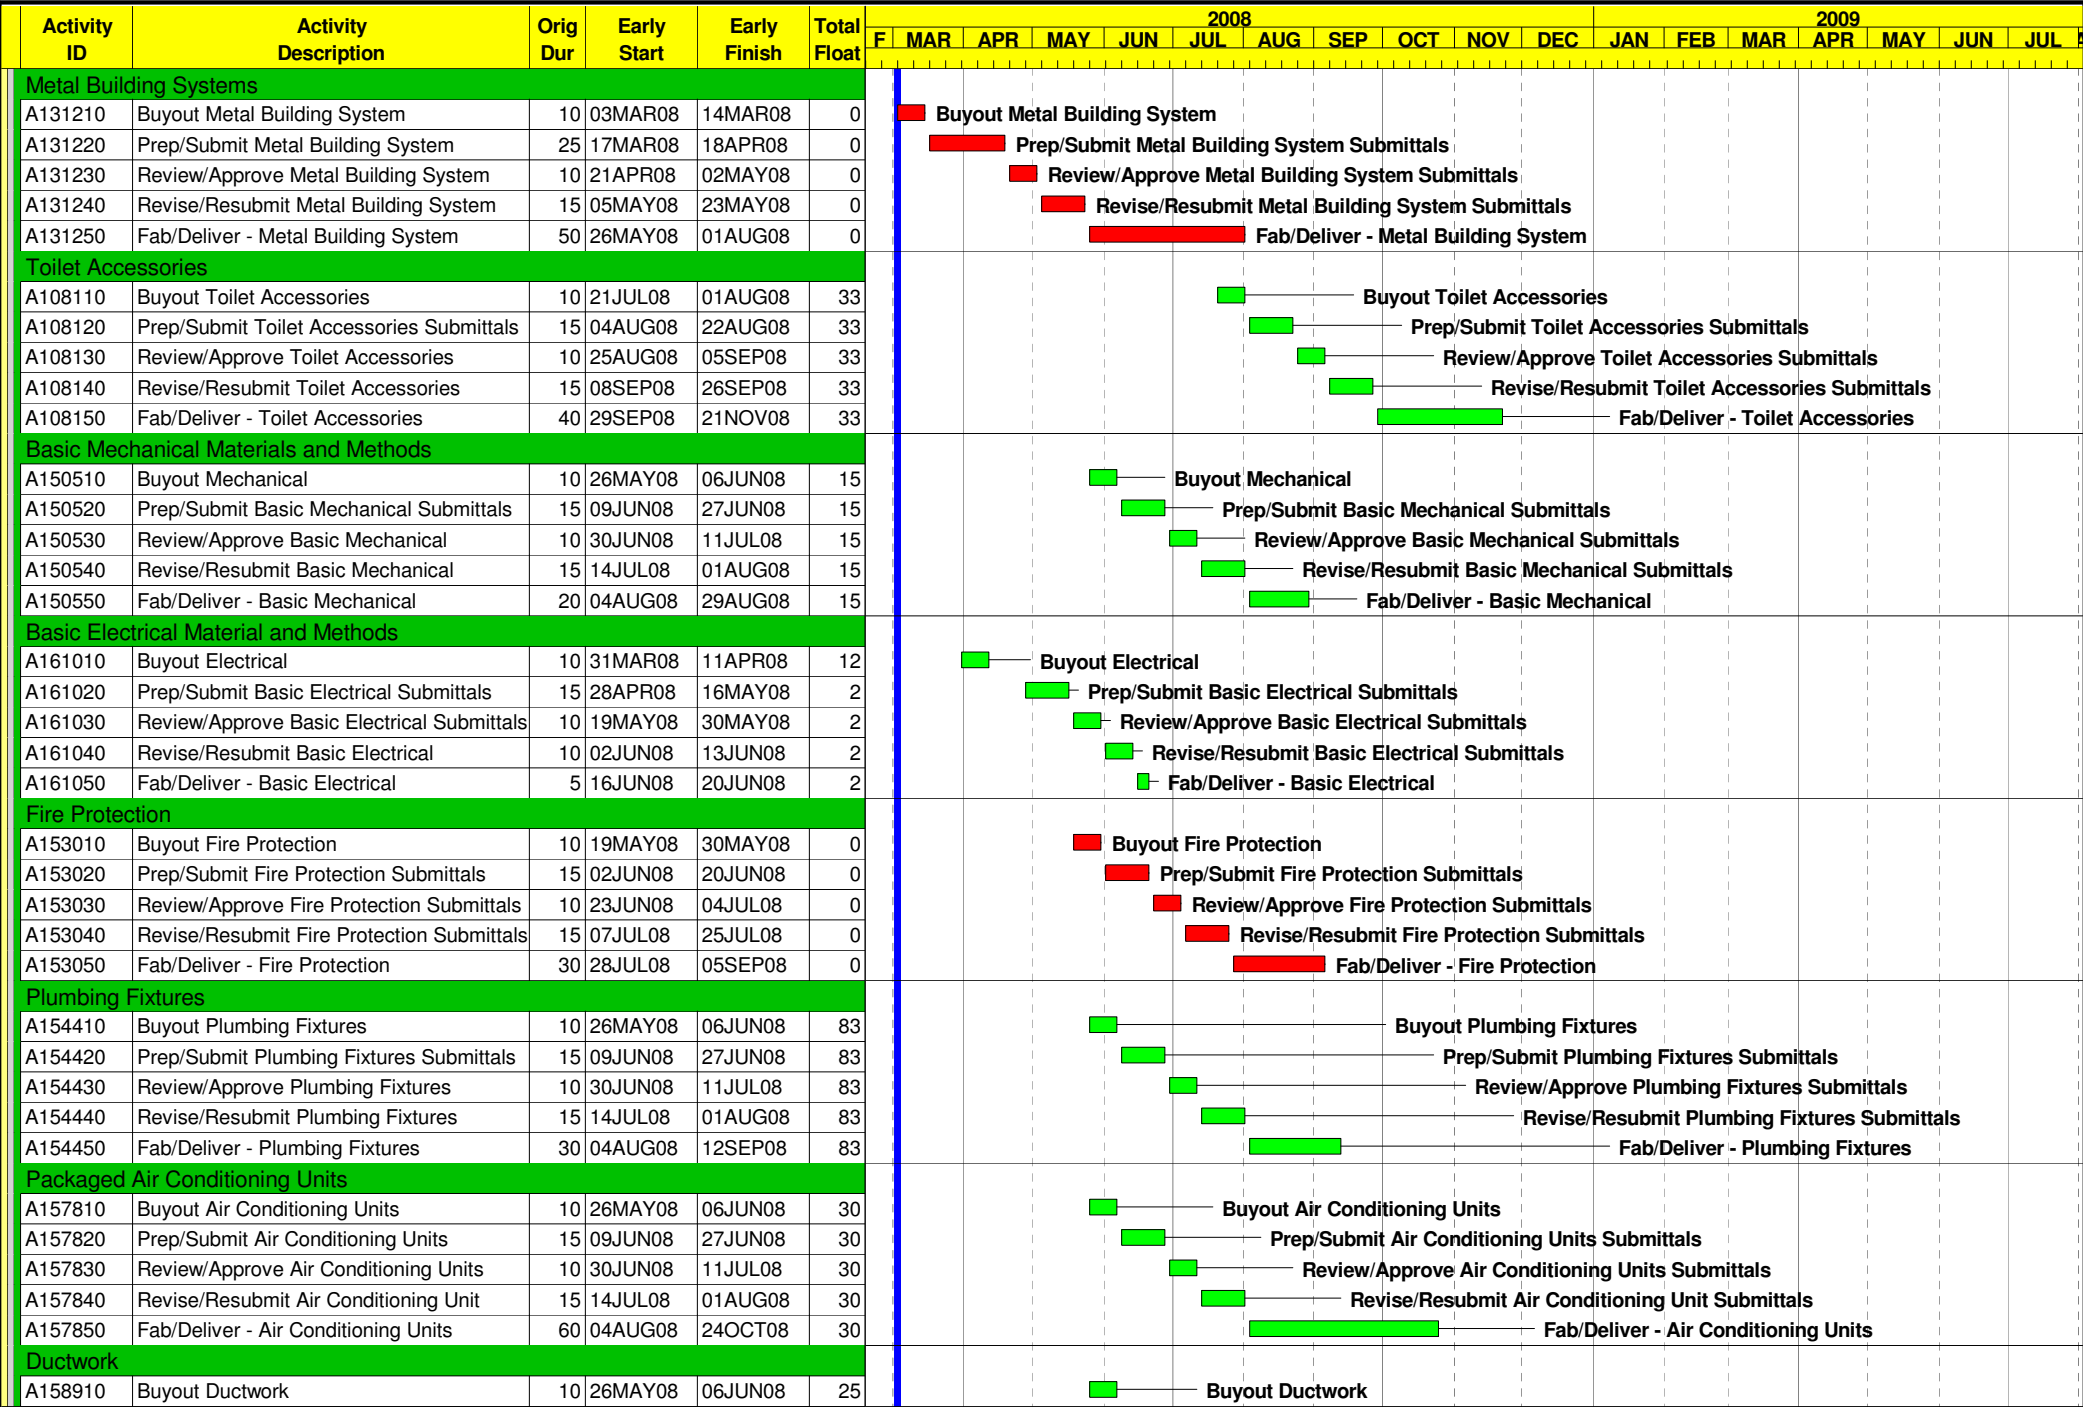

Start Date 03MAR08
Finish Date 31JUL09
Data Date 03MAR08
Run Date 25JAN08 15:10




RENO


City of San Jose
San Jose Central Service Yard PH 2
Schedule Set Up

Sheet 2 of 11

Date	Revision	Checked	Approved

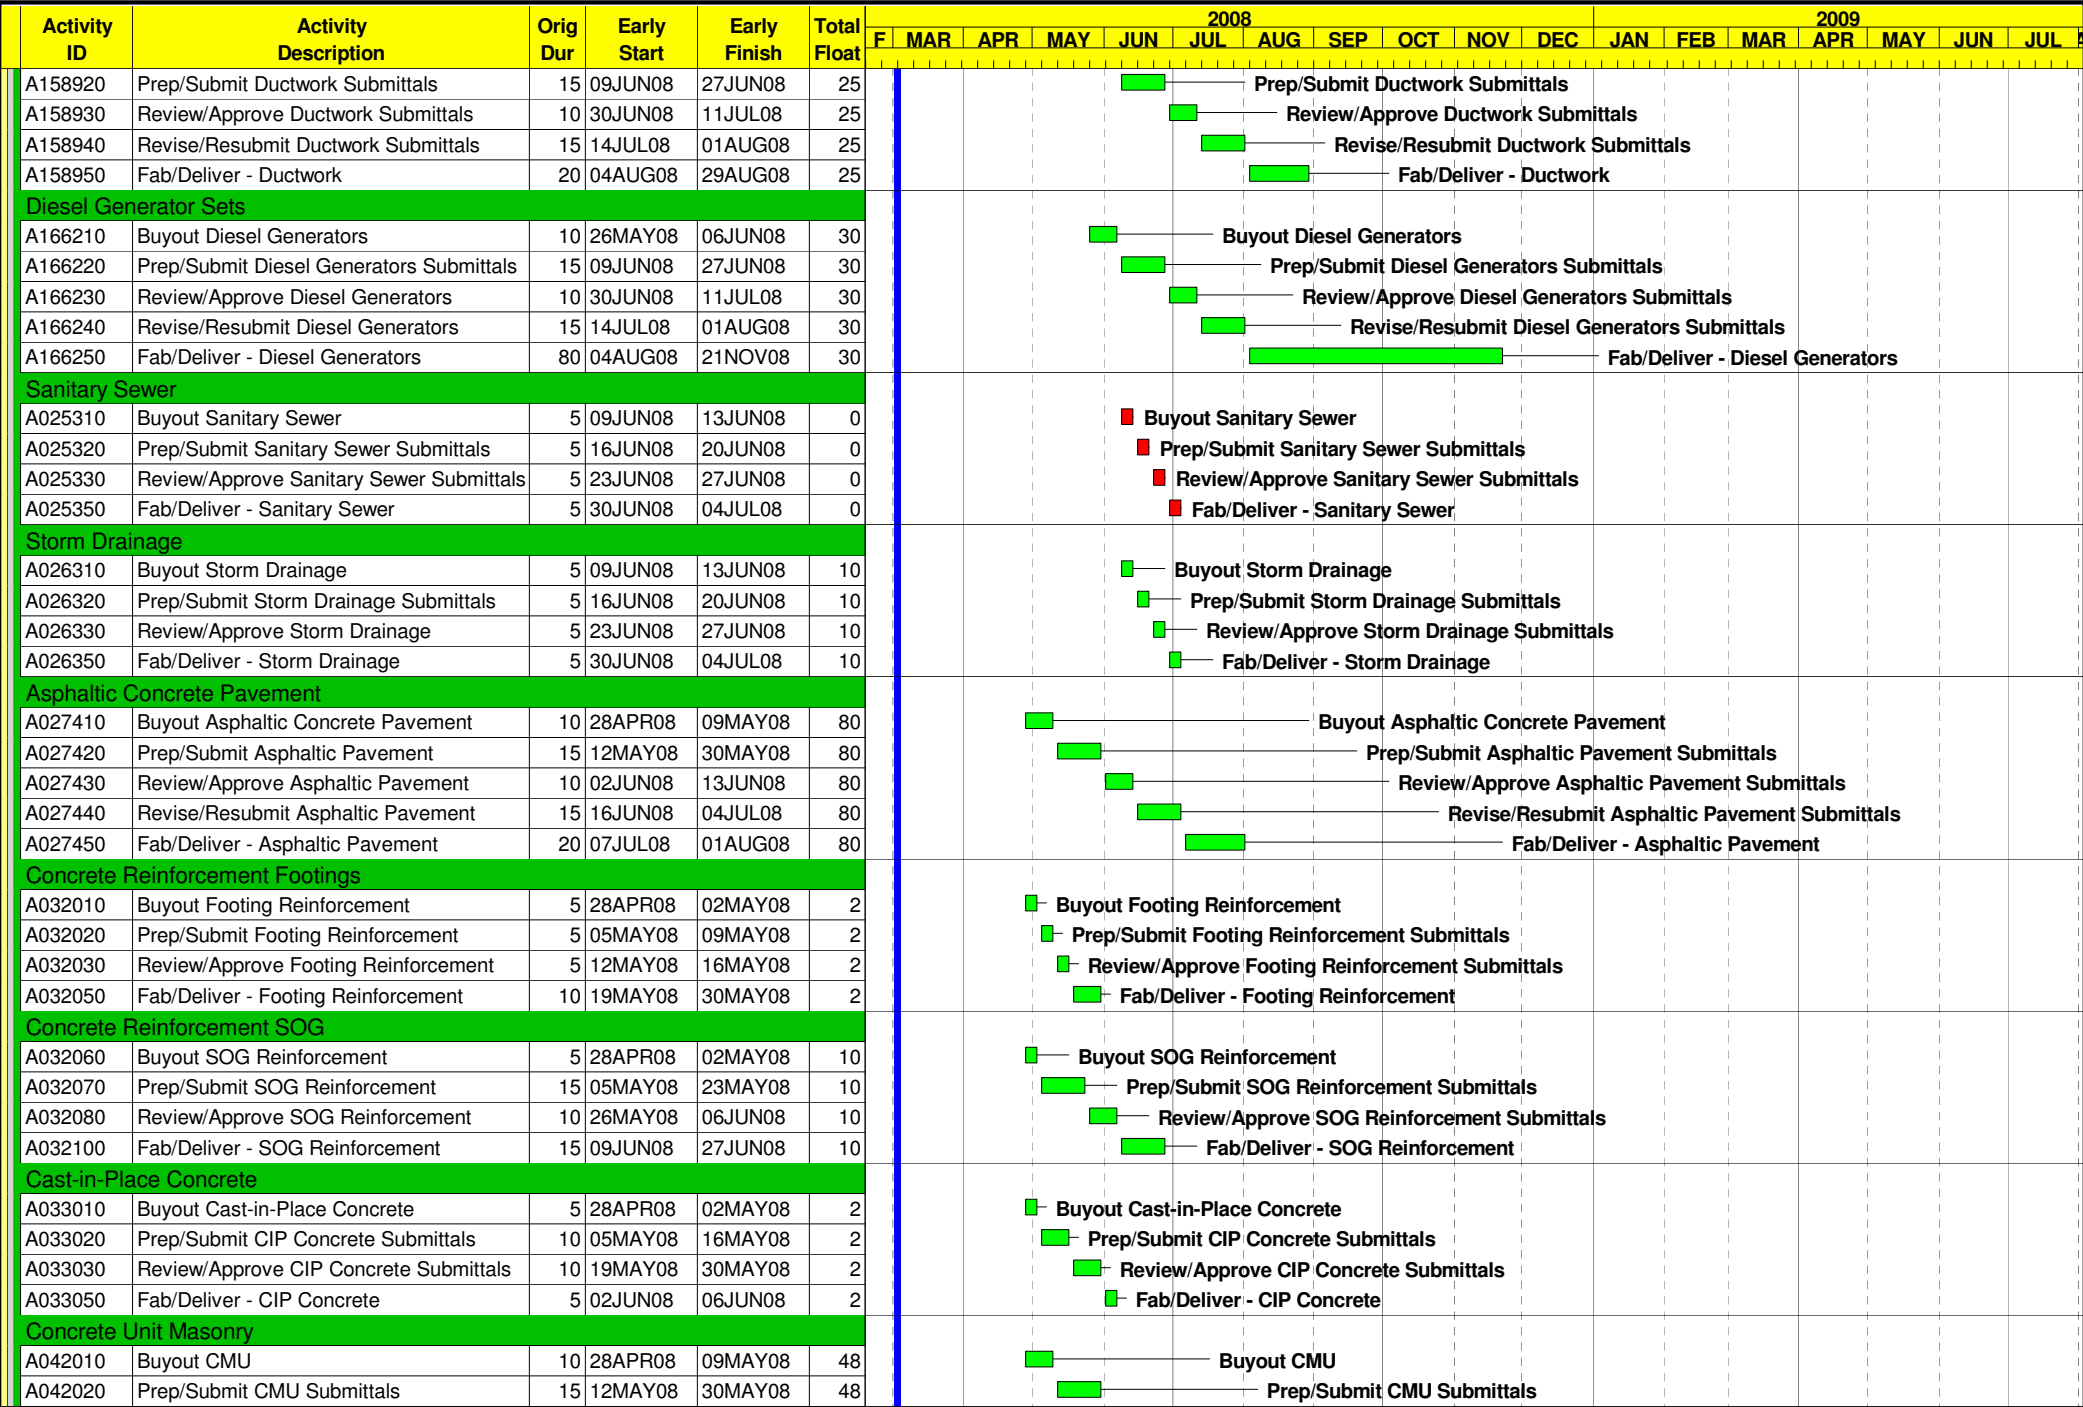

[illegible]

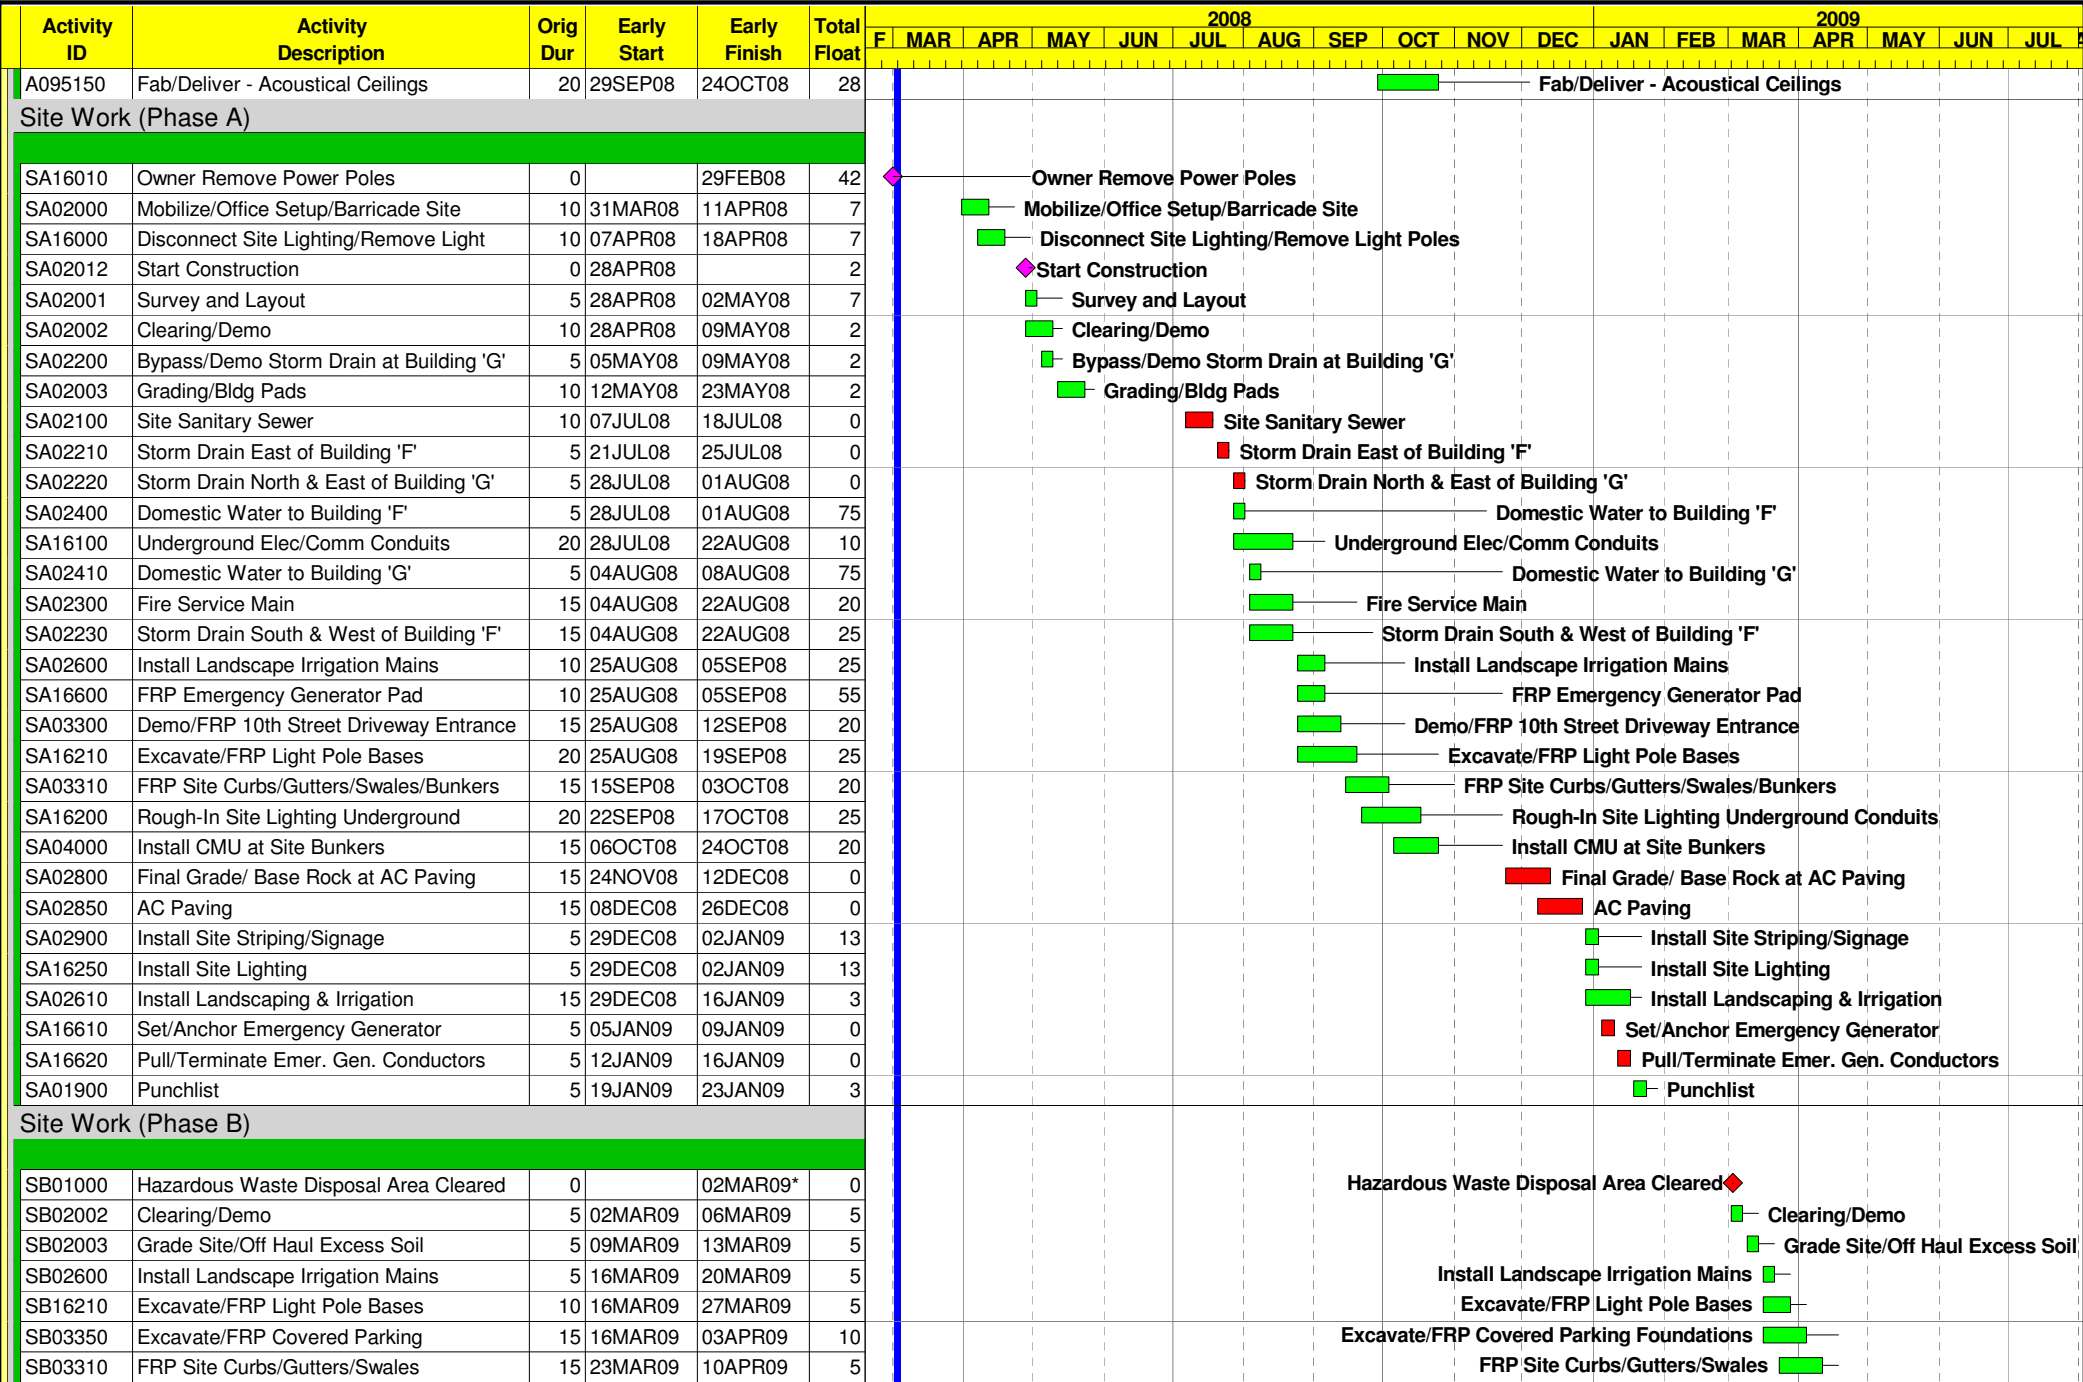

Start Date 03MAR08
Finish Date 31JUL09
Data Date 03MAR08
Run Date 25JAN08 15:10


Early Bar
Float Bar
Progress Bar
Critical Activity

RENO


City of San Jose
San Jose Central Service Yard PH 2
Schedule Set Up

Sheet 5 of 11

Date	Revision	Checked	Approved

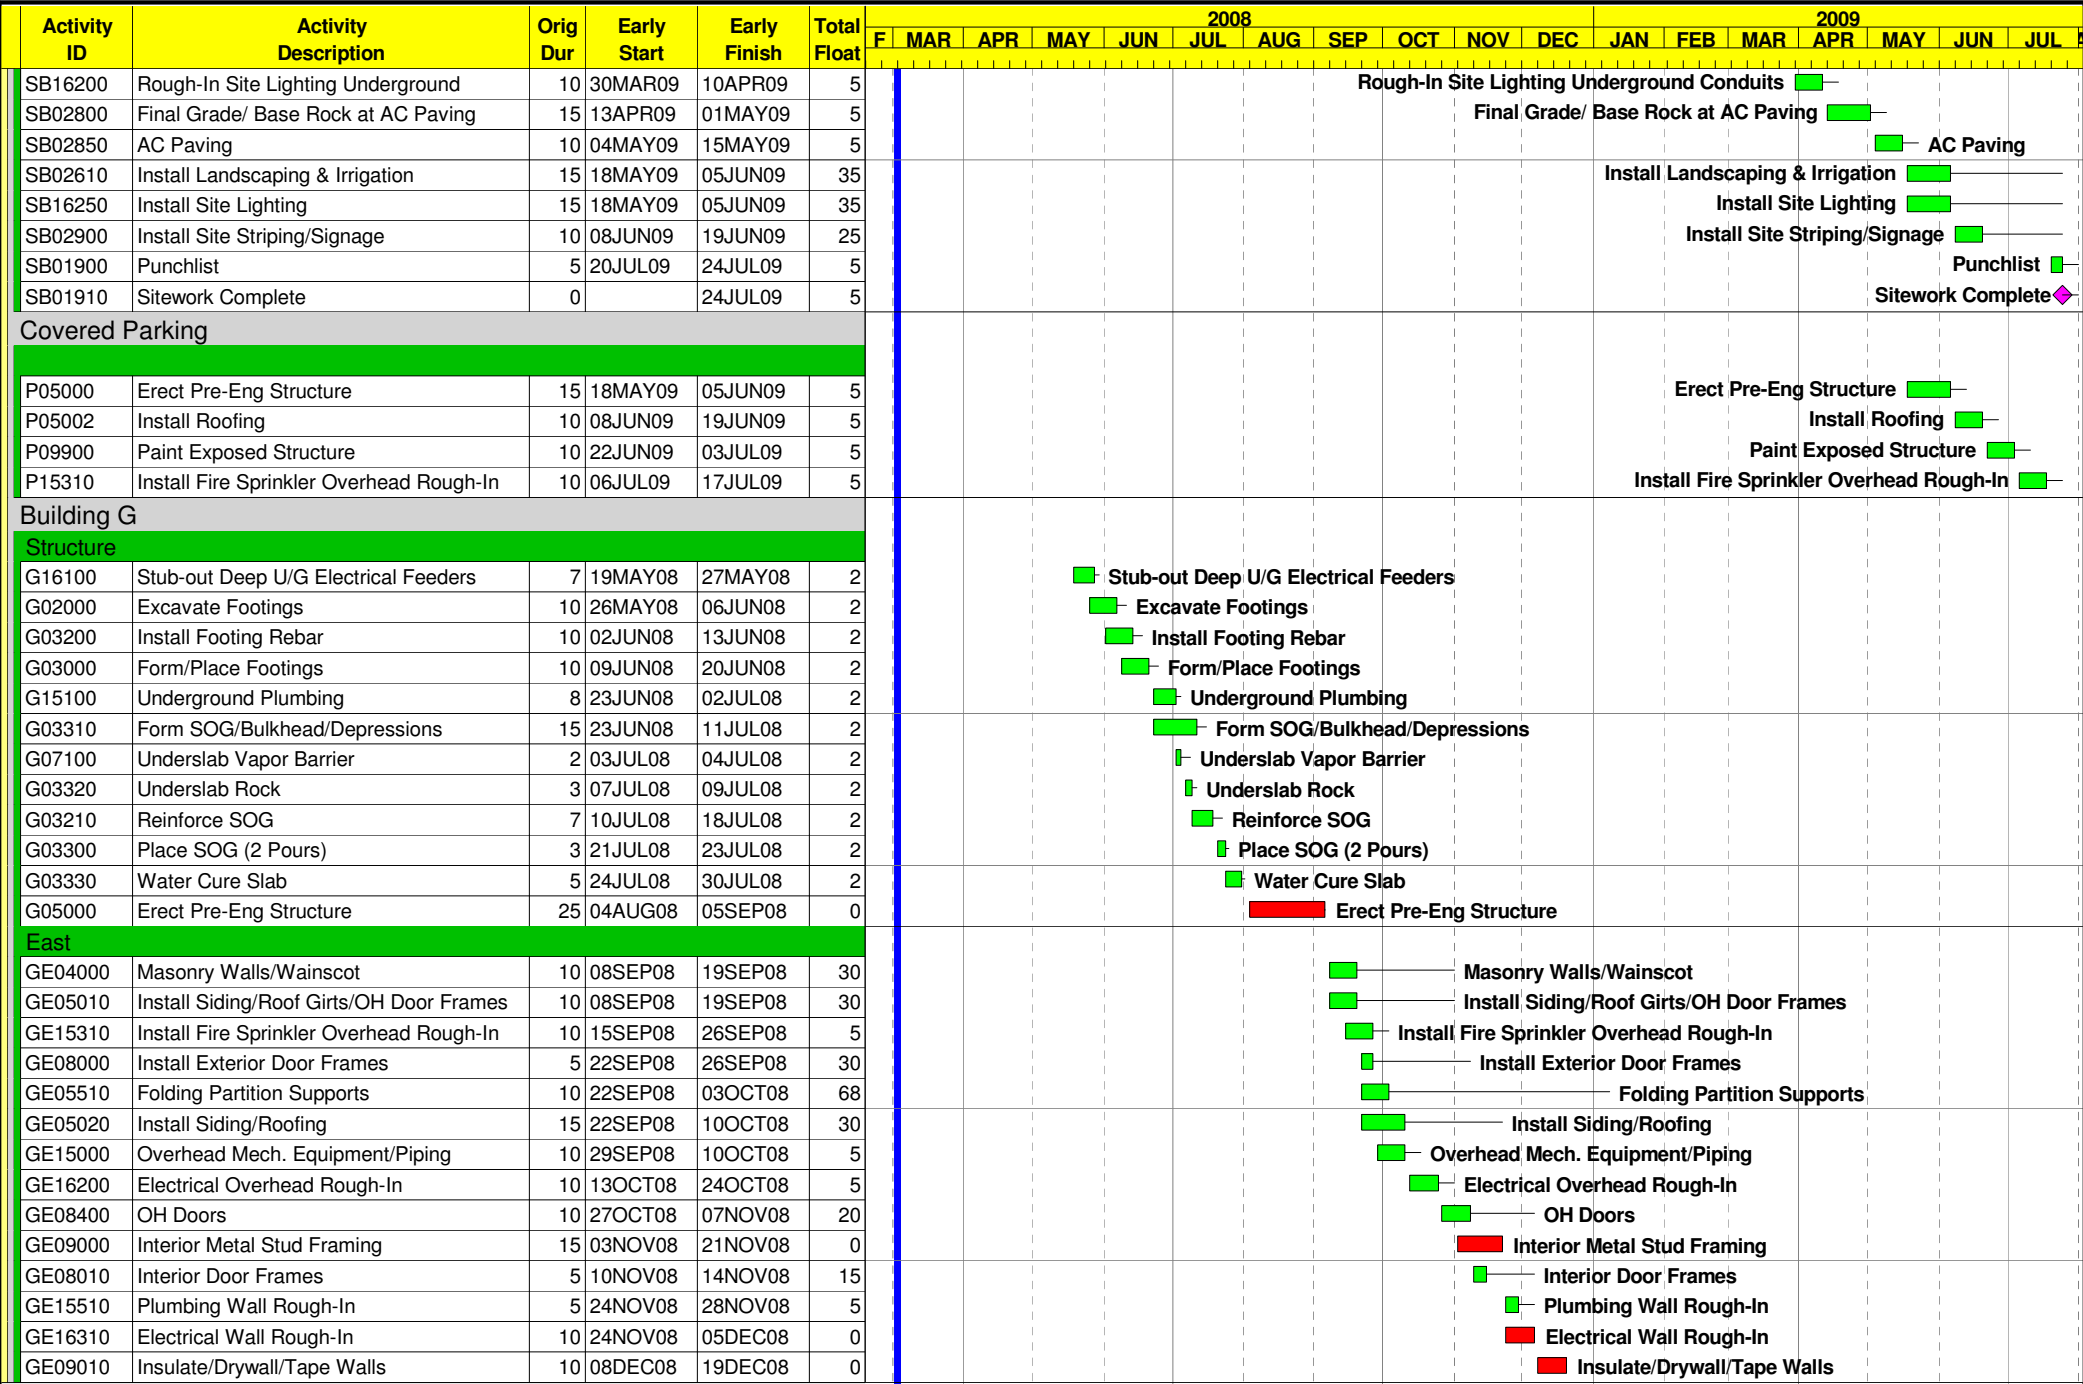

Start Date 03MAR08
Finish Date 31JUL09
Data Date 03MAR08
Run Date 25JAN08 15:10



RENO

Sheet 6 of 11

City of San Jose
San Jose Central Service Yard PH 2
Schedule Set Up

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float	2008												2009																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
						F	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
GE15300	Fire Protection Drops	10	15DEC08	26DEC08	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Start Date

03MAR08

Finish Date

31JUL09

Data Date

03MAR08

Run Date

25JAN08 15:10

Early Bar

Float Bar

Progress Bar

Critical Activity

RENO

City of San Jose

San Jose Central Service Yard PH 2

Schedule Set Up

Sheet 7 of 11

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

[illegible]

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float	2008												2009						
						F	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	
FC05010	Install Siding/Roof Girts/OH Door Frames	15	13OCT08	31OCT08	0																			
FC08000	Install Exterior Door Frames	5	20OCT08	24OCT08	8																			
FC15310	Install Fire Sprinkler Overhead Rough-In	10	20OCT08	31OCT08	3																			
FC15000	Overhead Mech Equipment/Piping	10	03NOV08	14NOV08	3																			
FC05020	Install Siding/Roofing	15	03NOV08	21NOV08	0																			
FC08400	OH Doors	20	03NOV08	28NOV08	23																			
FC16200	Electrical Overhead Rough-In	10	17NOV08	28NOV08	3																			
FC09000	Interior Metal Stud Framing	10	01DEC08	12DEC08	3																			
FC08010	Interior Door Frames	5	08DEC08	12DEC08	13																			
FC15510	Plumbing Wall Rough-In	10	15DEC08	26DEC08	3																			
FC16310	Electrical Wall Rough-In	10	15DEC08	26DEC08	3																			
FC09010	Insulate/Drywall/Tape walls	15	29DEC08	16JAN09	3																			
FC15300	Fire Protection Drops	5	12JAN09	16JAN09	3																			
FC09500	Accoustic Ceiling Grid	5	19JAN09	23JAN09	3																			
FC16020	Elec Trim	10	19JAN09	30JAN09	8																			
FC06000	Case Work	10	19JAN09	30JAN09	23																			
FC09300	Ceramic Tile	15	19JAN09	06FEB09	8																			
FC15010	Mech Trim	5	26JAN09	30JAN09	8																			
FC16010	Elec Lighting	5	02FEB09	06FEB09	3																			
FC09510	Accoustic Ceiling Tile	5	09FEB09	13FEB09	3																			
FC15520	Plumbing Trim	5	09FEB09	13FEB09	8																			
FC09600	Floor Covering	5	16FEB09	20FEB09	3																			
FC15030	Toilet Part/Accessories	5	16FEB09	20FEB09	8																			
FC15320	FP Trim	5	16FEB09	20FEB09	8																			
FC15900	Test and Commission	10	16FEB09	27FEB09	8																			
FC08020	Doors and HDWR	5	23FEB09	27FEB09	3																			
FC10800	Lockers	5	23FEB09	27FEB09	3																			
FC01900	Punchlist	5	02MAR09	06MAR09	3																			
FC01910	Bldg Complete	0		06MAR09	3																			
FC01920	Owner Relocation From Building B	10	09MAR09	20MAR09	3																			
South (Grid 1-7)																								
FS04000	Masonry Walls/Wainscot	10	13OCT08	24OCT08	5																			
FS05010	Install Siding/Roof Girts/OH Door Frames	15	13OCT08	31OCT08	0																			
FS08000	Install Exterior Door Frames	5	20OCT08	24OCT08	8																			
FS15310	Install Fire Sprinkler Overhead Rough-In	10	27OCT08	07NOV08	3																			
FS05020	Install Siding/Roofing	15	03NOV08	21NOV08	0																			
FS08400	OH Doors	20	03NOV08	28NOV08	28																			
FS15000	Overhead Mech Equipment/Piping	15	10NOV08	28NOV08	3																			
FS16200	Electrical Overhead Rough-In	10	01DEC08	12DEC08	3																			
FS09000	Interior Metal Stud Framing	5	15DEC08	19DEC08	3																			
FS08010	Interior Door Frames	5	22DEC08	26DEC08	8																			
FS15510	Plumbing Wall Rough-In	10	22DEC08	02JAN09	3																			
FS16310	Electrical Wall Rough-In	10	22DEC08	02JAN09	3																			
FS09010	Insulate/Drywall/Tape walls	15	05JAN09	23JAN09	3																			

Start Date

03MAR08

Early Bar

Finish Date

31JUL09

Float Bar

Data Date

03MAR08

Progress Bar

Run Date

25JAN08 15:10

Critical Activity

RENO

City of San Jose

San Jose Central Service Yard PH 2

Schedule Set Up

Sheet 9 of 11

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float	2008												2009																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
						F	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
BE16020	Elec Trim	5	22JUN09	26JUN09	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							</
