


Veterans Home of California

Plan. Build. Manage.

Activity ID	Activity Name	OD	Early Start	Early Finish	Total Float
California Veterans Home - Baseline Schedule		677	25-Apr-13	11-Dec-15	0
MILESTONES		677	25-Apr-13	11-Dec-15	0
MILESTONE SUMMARY		677	25-Apr-13	11-Dec-15	0
CONTRACTUAL MILESTONES		677	25-Apr-13	11-Dec-15	0
A1030	Project Award	0	25-Apr-13		0
A1000	Notice to Proceed (NTP)	0	12-Dec-13		0
A1020	Final Completion	0		11-Dec-15	0
PROJECT MILESTONES		258	11-Dec-13	15-Dec-14	0
DESIGN		0	11-Dec-13	11-Dec-13	0
A1200	Complete 35% Construction Documents	0		11-Dec-13	0
CONSTRUCTION		0	15-Dec-14	15-Dec-14	0
A1330	Central Services - Watertight	0		15-Dec-14	0
PRECONSTRUCTION & ADMINISTRATION		165	25-Apr-13	11-Dec-13	0
DESIGN DEVELOPMENT		165	25-Apr-13	11-Dec-13	0
D1000	Develop Conceptual Plans & Programming	5	25-Apr-13	01-May-13	0
D1010	Develop 35% Schematic Design Documents	15	02-May-13	22-May-13	0
D1020	Develop 50% Schematic incl. MEP	20	23-May-13	19-Jun-13	0
D1030	Develop 100% Schematic Design Documents	20	20-Jun-13	17-Jul-13	0
D1040	Develop 35% Design Documents	20	18-Jul-13	14-Aug-13	0
D1050	Develop 50% Design Documents	30	15-Aug-13	25-Sep-13	0
D1060	Develop 100% Design Documents	30	26-Sep-13	06-Nov-13	0
D1070	Develop 35% Construction Documents	20	07-Nov-13	04-Dec-13	0
D1080	Owner Review of 35% CD's	5	05-Dec-13	11-Dec-13	0
D1090	OSHPDA Review of 35% CD's	5	05-Dec-13	11-Dec-13	0
D1100	State Fire Marshall Review of 35% CD's	5	05-Dec-13	11-Dec-13	0
CONSTRUCTION		512	12-Dec-13	11-Dec-15	0
EARLY SITEWORK ACTIVITIES		37	12-Dec-13	03-Feb-14	0
AREA A		4	12-Dec-13	17-Dec-13	0
A1550	Mass Grading - Site (Area A)	4	12-Dec-13	17-Dec-13	0
AREA B		4	18-Dec-13	23-Dec-13	0
A1650	Mass Grading - Site (Area B)	4	18-Dec-13	23-Dec-13	0
AREA C		4	24-Dec-13	27-Dec-13	0
A1750	Mass Grading - Site (Area C)	4	24-Dec-13	27-Dec-13	0
AREA D		25	30-Dec-13	03-Feb-14	0
A1850	Mass Grading - Site (Area D)	4	30-Dec-13	03-Jan-14	0
A1860	Storm Drain Piping - Site (Area D)	3	06-Jan-14	08-Jan-14	0
A1870	Sewer Piping - Site (Area D)	3	09-Jan-14	13-Jan-14	0
A1880	Underground Electrical - Site (Area D)	3	14-Jan-14	16-Jan-14	0
A1890	Fire Water Piping - Site (Area D)	3	17-Jan-14	21-Jan-14	0
A1900	Underground Gas Piping - Site (Area D)	3	22-Jan-14	24-Jan-14	0
A1910	Domestic Water - Site (Area D)	3	27-Jan-14	29-Jan-14	0
A2960	Install U/G Process Piping - Site (Area D)	3	30-Jan-14	03-Feb-14	0
STRUCTURE		66	11-Feb-14	13-May-14	0
CENTRAL SERVICES BUILDING		66	11-Feb-14	13-May-14	0
CS1000	Install U/G Electrical - CS	10	11-Feb-14	24-Feb-14	0
CS1010	Install Drains & FCO's - CS	10	25-Feb-14	10-Mar-14	0

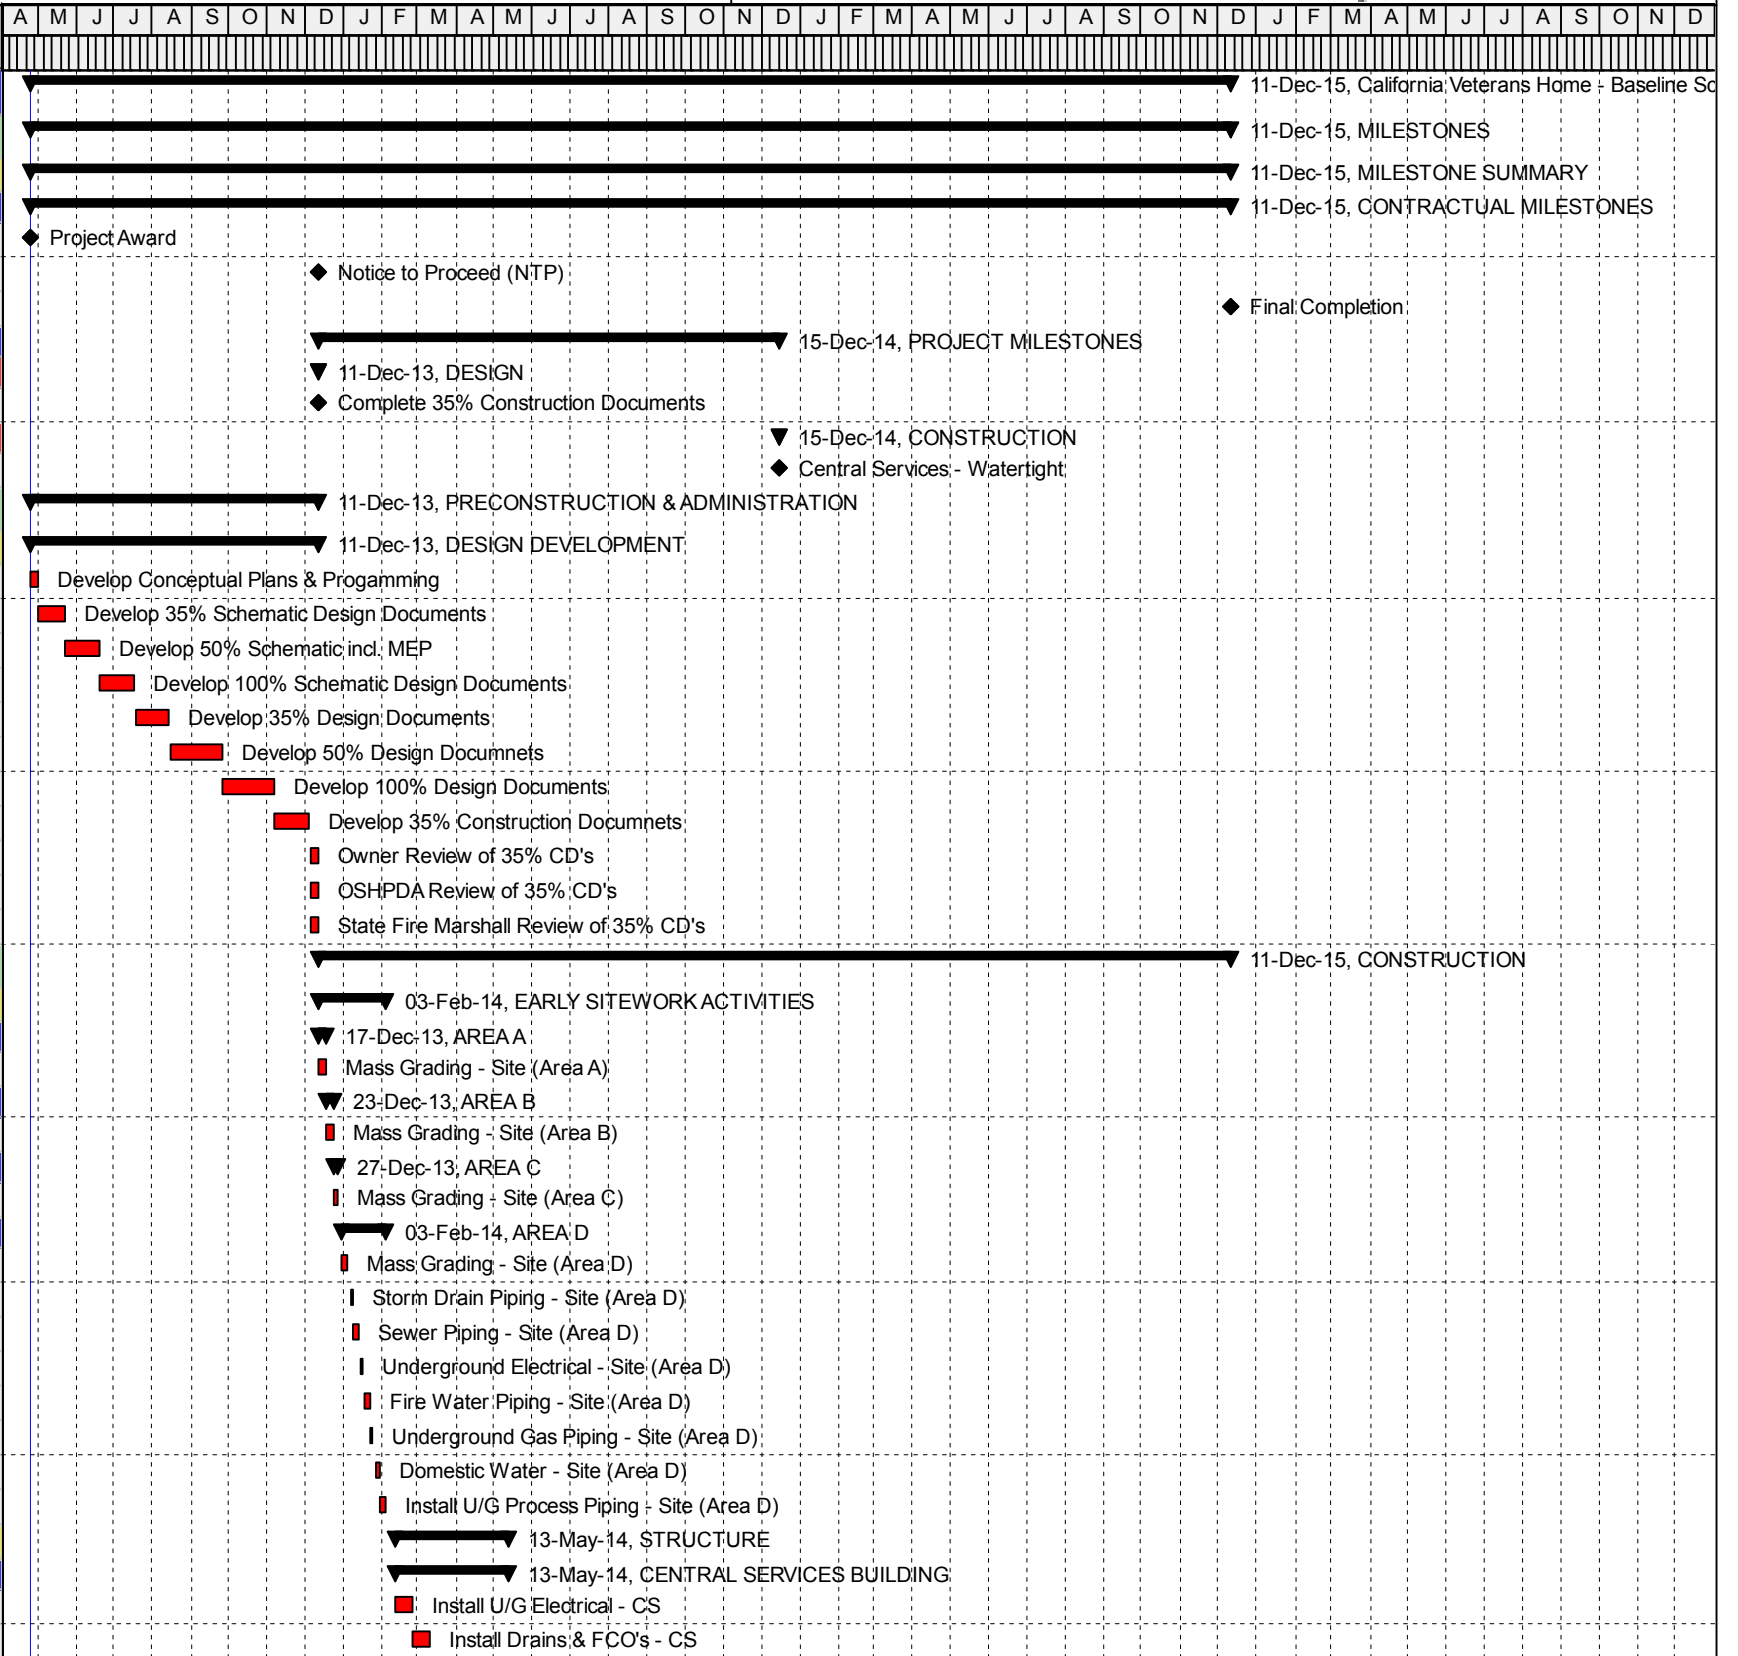

Critical Path Report

 Actual Work
  Critical Remaining Work
  Summary
 Remaining Work
 ◆ ◆ Milestone

Veterans Home of California					
Activity ID		Activity Name	OD	Early Start	
100	100	CS1090	Excavate Foundations - CS	8	11-Mar-19
		CS1100	Place Foundations - CS	8	21-Mar-19
		CS1020	Install Edge Form - CS	5	02-Apr-19
		CS1030	Install Base Course - CS	5	09-Apr-19
		CS1040	Install Vapor Barrier - CS	5	16-Apr-19
		CS1050	Install SOG Reinforcing - CS	10	23-Apr-19
		CS1060	Place SOG - CS	5	07-May-19
	SUPERSTRUCTURE			55	14-May-19
	CENTRAL SERVICES BUILDING			55	14-May-19
		CS2000	Building Control/Layout - CSB	5	14-May-19
		CS2010	Erect Structural Steel - CSB	10	21-May-19
		CS2020	Plumb/Align/Weld/Bolt Structural Steel - CSB	5	05-Jun-19
		CS2030	Install Metal Deck - CSB	5	12-Jun-19
		CS2040	Install Roof Decking - CSB	10	12-Jun-19
		CS2050	Erect Stairs - CSB	5	26-Jun-19
		CS2060	Install MEP Sleeves in Decking - CSB	5	03-Jul-19
		CS2070	Install Deck Reinforcing - CSB	5	11-Jul-19
		CS2080	Place SOD - CSB	5	18-Jul-19
		CS2090	FRP Curbs/Pads @ Mech - CSB	5	25-Jul-19
	EXTERIOR ENCLOSURE			105	01-Aug-19
	CENTRAL SERVICES BUILDING			105	01-Aug-19
		CS3000	Install Exterior Framing - CSB	20	01-Aug-19
		CS3010	Install Exterior Sheathing - CSB	20	15-Aug-19
		CS3050	Install Rooftop Equipment - CSB	5	15-Sep-19
		CS3060	Install Flashing/Wtrprf Plaster - CSB	20	22-Sep-19
		CS3020	Install Exterior Windows - CSB	10	06-Oct-19
		CS3080	Install Roof Sheathing - CSB	10	20-Oct-19
		CS3090	Install Roof Underlayment & Flashing - CSB	10	03-Nov-19
		CS3030	Install Membrane Roofing - CSB	20	17-Nov-19
	CS3100	Install Roof Tiles - CSB	10	16-Dec-19	
MEPF ROUGH-INS			100	31-Dec-19	
CENTRAL SERVICES BUILDING			100	31-Dec-19	
	CS4000	Rough-In OH MEP - CSB	30	31-Dec-19	
	CS4010	Install Plumbing Carriers - CSB	15	12-Feb-20	
	CS4030	MEP Roug-In Ceilings & Soffits - CSB	15	30-Apr-20	
PARTITIONS			70	05-Mar-20	
CENTRAL SERVICES BUILDING			70	05-Mar-20	
	CS5000	Frame Walls - CSB	20	05-Mar-20	
	CS5040	Install Head of Walls - CSB	10	02-Apr-20	
	CS5050	Frame Ceilings & Soffits - CSB	10	16-Apr-20	
	CS5060	Drywall Ceilings & Soffits - CSB	5	21-May-20	
	CS5070	Tape and Finish Walls/Ceilings/Soffits - CSB	10	29-May-20	
INTERIOR FINISHES			100	12-Jun-20	
CENTRAL SERVICES BUILDING			100	12-Jun-20	
	CS6000	Paint Walls & Ceilings - CSB	15	12-Jun-20	
	CS6010	Install Ceiling Grid - CSB	10	26-Jun-20	



Activity ID		Activity Name	OD	Early Start	Early Finish	Total Float																														
		CS1090	Excavate Foundations - CS	8	11-Mar-14	20-Mar-14	0	Excavate Foundations - CS																												
		CS1100	Place Foundations - CS	8	21-Mar-14	01-Apr-14	0	Place Foundations - CS																												
		CS1020	Install Edge Form - CS	5	02-Apr-14	08-Apr-14	0	Install Edge Form - CS																												
		CS1030	Install Base Course - CS	5	09-Apr-14	15-Apr-14	0	Install Base Course - CS																												
		CS1040	Install Vapor Barrier - CS	5	16-Apr-14	22-Apr-14	0	Install Vapor Barrier - CS																												
		CS1050	Install SOG Reinforcing - CS	10	23-Apr-14	06-May-14	0	Install SOG Reinforcing - CS																												
		CS1060	Place SOG - CS	5	07-May-14	13-May-14	0	Place SOG - CS																												
		SUPERSTRUCTURE			55	14-May-14	31-Jul-14	0	31-Jul-14, SUPERSTRUCTURE																											
		CENTRAL SERVICES BUILDING			55	14-May-14	31-Jul-14	0	31-Jul-14, CENTRAL SERVICES BUILDING																											
		CS2000	Building Control/Layout - CSB	5	14-May-14	20-May-14	0	Building Control/Layout - CSB																												
		CS2010	Erect Structural Steel - CSB	10	21-May-14	04-Jun-14	0	Erect Structural Steel - CSB																												
		CS2020	Plumb/Align/Weld/Bolt Structural Steel - CSB	5	05-Jun-14	11-Jun-14	0	Plumb/Align/Weld/Bolt Structural Steel - CSB																												
		CS2030	Install Metal Deck - CSB	5	12-Jun-14	18-Jun-14	0	Install Metal Deck - CSB																												
		CS2040	Install Roof Decking - CSB	10	12-Jun-14	25-Jun-14	0	Install Roof Decking - CSB																												
		CS2050	Erect Stairs - CSB	5	26-Jun-14	02-Jul-14	0	Erect Stairs - CSB																												
		CS2060	Install MEP Sleeves in Decking - CSB	5	03-Jul-14	10-Jul-14	0	Install MEP Sleeves in Decking - CSB																												
		CS2070	Install Deck Reinforcing - CSB	5	11-Jul-14	17-Jul-14	0	Install Deck Reinforcing - CSB																												
		CS2080	Place SOD - CSB	5	18-Jul-14	24-Jul-14	0	Place SOD - CSB																												
		CS2090	FRP Curbs/Pads @ Mech - CSB	5	25-Jul-14	31-Jul-14	0	FRP Curbs/Pads @ Mech - CSB																												
		EXTERIOR ENCLOSURE			105	01-Aug-14	30-Dec-14	0	30-Dec-14, EXTERIOR ENCLOSURE																											
		CENTRAL SERVICES BUILDING			105	01-Aug-14	30-Dec-14	0	30-Dec-14, CENTRAL SERVICES BUILDING																											
		CS3000	Install Exterior Framing - CSB	20	01-Aug-14	28-Aug-14	0	Install Exterior Framing - CSB																												
		CS3010	Install Exterior Sheathing - CSB	20	15-Aug-14	12-Sep-14	0	Install Exterior Sheathing - CSB																												
		CS3050	Install Rooftop Equipment - CSB	5	15-Sep-14	19-Sep-14	0	Install Rooftop Equipment - CSB																												
		CS3060	Install Flashing/Wtrprf Plaster - CSB	20	22-Sep-14	17-Oct-14	0	Install Flashing/Wtrprf Plaster - CSB																												
		CS3020	Install Exterior Windows - CSB	10	06-Oct-14	17-Oct-14	0	Install Exterior Windows - CSB																												
		CS3080	Install Roof Sheathing - CSB	10	20-Oct-14	31-Oct-14	0	Install Roof Sheathing - CSB																												
		CS3090	Install Roof Underlayment & Flashing - CSB	10	03-Nov-14	14-Nov-14	0	Install Roof Underlayment & Flashing - CSB																												
		CS3030	Install Membrane Roofing - CSB	20	17-Nov-14	15-Dec-14	0	Install Membrane Roofing - CSB																												
		CS3100	Install Roof Tiles - CSB	10	16-Dec-14	30-Dec-14	0	Install Roof Tiles - CSB																												
		MEPF ROUGH-INS			100	31-Dec-14	20-May-15	0	20-May-15, MEPF ROUGH-INS																											
		CENTRAL SERVICES BUILDING			100	31-Dec-14	20-May-15	0	20-May-15, CENTRAL SERVICES BUILDING																											
		CS4000	Rough-In OH MEP - CSB	30	31-Dec-14	11-Feb-15	0	Rough-In OH MEP - CSB																												
		CS4010	Install Plumbing Carriers - CSB	15	12-Feb-15	04-Mar-15	0	Install Plumbing Carriers - CSB																												
		CS4030	MEP Roug-In Ceilings & Soffitts - CSB	15	30-Apr-15	20-May-15	0	MEP Roug-In Ceilings & Soffitts - CSB																												
		PARTITIONS			70	05-Mar-15	11-Jun-15	0	11-Jun-15, PARTITIONS																											
		CENTRAL SERVICES BUILDING			70	05-Mar-15	11-Jun-15	0	11-Jun-15, CENTRAL SERVICES BUILDING																											
		CS5000	Frame Walls - CSB	20	05-Mar-15	01-Apr-15	0	Frame Walls - CSB																												
		CS5040	Install Head of Walls - CSB	10	02-Apr-15	15-Apr-15	0	Install Head of Walls - CSB																												
		CS5050	Frame Ceilings & Soffitts - CSB	10	16-Apr-15	29-Apr-15	0	Frame Ceilings & Soffitts - CSB																												
CS5060	Drywall Ceilings & Soffitts - CSB	5	21-May-15	28-May-15	0	Drywall Ceilings & Soffitts - CSB																														
CS5070	Tape and Finish Walls/Ceilings/Soffitts - CSB	10	29-May-15	11-Jun-15	0	Tape and Finish Walls/Ceilings/Soffitts - CSB																														
INTERIOR FINISHES			100	12-Jun-15	30-Oct-15	0	30-Oct-15, INTERIOR FINISHES																													
CENTRAL SERVICES BUILDING			100	12-Jun-15	30-Oct-15	0	30-Oct-15, CENTRAL SERVICES BUILDING																													
CS6000	Paint Walls & Ceilings - CSB	15	12-Jun-15	02-Jul-15	0	Paint Walls & Ceilings - CSB																														
CS6010	Install Ceiling Grid - CSB	10	26-Jun-15	09-Jul-15	0	Install Ceiling Grid - CSB																														

Veterans Home of California

 **HENSEL PHELPS**
Plan. Build. Manage.

 **HENSEL PHELPS**
Plan. Build. Manage.

[illegible]

Critical Path Report

 Actual Work
  Critical Remaining Work
  Summary
 Remaining Work
  Milestone
