



Activity ID		Activity Name		Total Float	Start	Finish	Total Float	2019					Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019			Qtr 1, 2020			Qtr 2, 2020				
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May						
Solano County - CVTC Reno Competition 2019				290	11-Feb-19	10-Apr-20	0																		10-Apr-20, Solano County				
Contract Milestones				290	11-Feb-19	10-Apr-20	0																		10-Apr-20, Cor				
MS-1000		Notice to Proceed		0	11-Feb-19*	11-Feb-19	0	Notice to Proceed																					
MS-1010		Weather Allowance		40	11-Feb-19	09-Apr-19	228	Weather Allowance																					
MS-1020		Substantial Completion		0	10-Mar-20	10-Mar-20	0																		Substantial Completion				
MS-1030		Final Completion		0	10-Apr-20	10-Apr-20	0																		Final Completion				
Interim Milestones				268	11-Feb-19	09-Mar-20	0																		09-Mar-20, Interim Milestones				
IM-1060		Phase 1		268	11-Feb-19	09-Mar-20	0	Phase 1																					
IM-1000		Start Structure		0	15-Jul-19*		0	Start Structure, 15-Jul-19*																					
IM-1030		Energize Main Gear		0	22-Aug-19*		0	Energize Main Gear, 22-Aug-19*																					
IM-1020		Building Dry In		0		10-Oct-19*	0	Building Dry In, 10-Oct-19*																					
IM-1010		End Structure		0		21-Oct-19*	0	End Structure, 21-Oct-19*																					
IM-1040		Start Mechanical Systems		0	13-Dec-19*		0	Start Mechanical Systems, 13-Dec-19*																					
IM-1050		Start Fire Alarm Testing		0	30-Jan-20*		0	Start Fire Alarm Testing, 30-Jan-20*																					
Preconstruction Schedule				152	11-Feb-19	17-Sep-19	6	17-Sep-19, Preconstruction Schedule																					
Buyout				40	11-Feb-19	09-Apr-19	3	09-Apr-19, Buyout																					
BO-1000		Metal Structure		10	11-Feb-19	25-Feb-19	0	Metal Structure																					
BO-1090		Electrical System		10	13-Feb-19	27-Feb-19	0	Electrical System																					
BO-1010		Fire Alarm		10	15-Feb-19	01-Mar-19	0	Fire Alarm																					
BO-1060		Security Electronic Systems		10	19-Feb-19	04-Mar-19	4	Security Electronic Systems																					
BO-1020		Mezzanine Metal Stairs		10	28-Feb-19	13-Mar-19	1	Mezzanine Metal Stairs																					
BO-1030		Fire Suppression		10	05-Mar-19	18-Mar-19	4	Fire Suppression																					
BO-1080		Detention Hardware		10	08-Mar-19	21-Mar-19	5	Detention Hardware																					
BO-1070		Detention Doors and Frames		10	14-Mar-19	27-Mar-19	1	Detention Doors and Frames																					
BO-1040		HVAC Units		10	19-Mar-19	02-Apr-19	2	HVAC Units																					
BO-1050		Security Glazing		10	26-Mar-19	09-Apr-19	3	Security Glazing																					
Submittals				100	11-Feb-19	03-Jul-19	3	03-Jul-19, Submittals																					
Metal Structure				53	11-Feb-19	26-Apr-19	0	26-Apr-19, Metal Structure																					
A1070		Foundation - Shop Drawings - Submit		20	11-Feb-19	11-Mar-19	0	Foundation - Shop Drawings - Submit																					
SM-1000		Structure - Shop Drawings - Submit		30	22-Feb-19	05-Apr-19	0	Structure - Shop Drawings - Submit																					
A1060		Anchor Bolts - Shop Drawings - Submit		25	26-Feb-19	02-Apr-19	3	Anchor Bolts - Shop Drawings - Submit																					
A1100		Foundation - Shop Drawings - R/A		10	12-Mar-19	25-Mar-19	0	Foundation - Shop Drawings - R/A																					
A1110		Anchor Bolt - Shop Drawings - R/A		10	03-Apr-19	16-Apr-19	3	Anchor Bolt - Shop Drawings - R/A																					
A1080		Structure - Shop Drawings - R/A		10	08-Apr-19	19-Apr-19	0	Structure - Shop Drawings - R/A																					
A1090		Structure - Review by AHJ		5	22-Apr-19	26-Apr-19	0	Structure - Review by AHJ																					
Doors, Frames and Hardware				60	28-Mar-19	21-Jun-19	1	21-Jun-19, Doors, Frames and Hardware																					
SM-1010		Detention Doors and Frames - Product Data - Submit		40	28-Mar-19	23-May-19	1	Detention Doors and Frames - Product Data - Submit																					
SM-1110		Detention Hardware - Product Data - Submit		45	28-Mar-19	31-May-19	1	Detention Hardware - Product Data - Submit																					
SM-1090		Detention Doors and Frames - R/A		15	24-May-19	14-Jun-19	1	Detention Doors and Frames - R/A																					
SM-1120		Detention Hardware - R/A		10	03-Jun-19	14-Jun-19	1	Detention Hardware - R/A																					
SM-1100		Doors, Frames and Hardware - Review by AHJ		5	17-Jun-19	21-Jun-19	1	Doors, Frames and Hardware - Review by AHJ																					
Light Fixtures				55	28-Feb-19	16-May-19	0	16-May-19, Light Fixtures																					
SM-1130		Light Fixtures - Product Data - Submit		35	28-Feb-19	18-Apr-19	0	Light Fixtures - Product Data - Submit																					
SM-1020		Light Fixtures - R/A		15	19-Apr-19	09-May-19	0	Light Fixtures - R/A																					
SM-1140		Light Fixtures - Review by AHJ		5	10-May-19	16-May-19	0	Light Fixtures - Review by AHJ																					
Glazing				60	10-Apr-19	03-Jul-19	3	03-Jul-19, Glazing																					
SM-1150		Glazing - Shop Drawings Submit		45	10-Apr-19	12-Jun-19	3	Glazing - Shop Drawings Submit																					
SM-1160		Glazing - R/A		10	13-Jun-19	26-Jun-19	3	Glazing - R/A																					
SM-1030		Glazing - Review by AHJ		5	27-Jun-19	03-Jul-19	3	Glazing - Review by AHJ																					
Mezzanine Metal Stairs				40	14-Mar-19	09-May-19	1	09-May-19, Mezzanine Metal Stairs																					
SM-1040		Mezzanine Metal Stairs - Shop Drawings - Submit		25	14-Mar-19	18-Apr-19	1	Mezzanine Metal Stairs - Shop Drawings - Submit																					
SM-1170		Mezzanine Metal Stairs - R/A		10	19-Apr-19	02-May-19	1	Mezzanine Metal Stairs - R/A																					
SM-1180		Mezzanine Metal Stairs - Review by AHJ		5	03-May-19	09-May-19	1	Mezzanine Metal Stairs - Review by AHJ																					
HVAC Units				50	03-Apr-19	12-Jun-19	2	12-Jun-19, HVAC Units																					
SM-1060		HVAC Units - Product Data - Submit		35	03-Apr-19	21-May-19	2	HVAC Units - Product Data - Submit																					
SM-1210		HVAC Units - Shop Drawing - Submit		35	03-Apr-19	21-May-19	2	HVAC Units - Shop Drawing - Submit																					
SM-1200		HVAC Units - R/A		10	22-May-19	05-Jun-19	2	HVAC Units - R/A																					
SM-1190		HVAC Units - Review by AHJ		5	06-Jun-19	12-Jun-19	2	HVAC Units - Review by AHJ																					
Electrical Systems				47	28-Feb-19	06-May-19	0	06-May-19, Electrical Systems																					
SM-1260		Switchboard - Product Data - Submit		20	28-Feb-19	27-Mar-19	2	Switchboard - Product Data - Submit																					
SM-1280		Panelboards - Product Data - Submit		20	28-Feb-19	27-Mar-19	2	Panelboards - Product Data - Submit																					
SM-1220		Fire Alarm - Shop Drawings - Submit		20	04-Mar-19	29-Mar-19	0	Fire Alarm - Shop Drawings - Submit																					

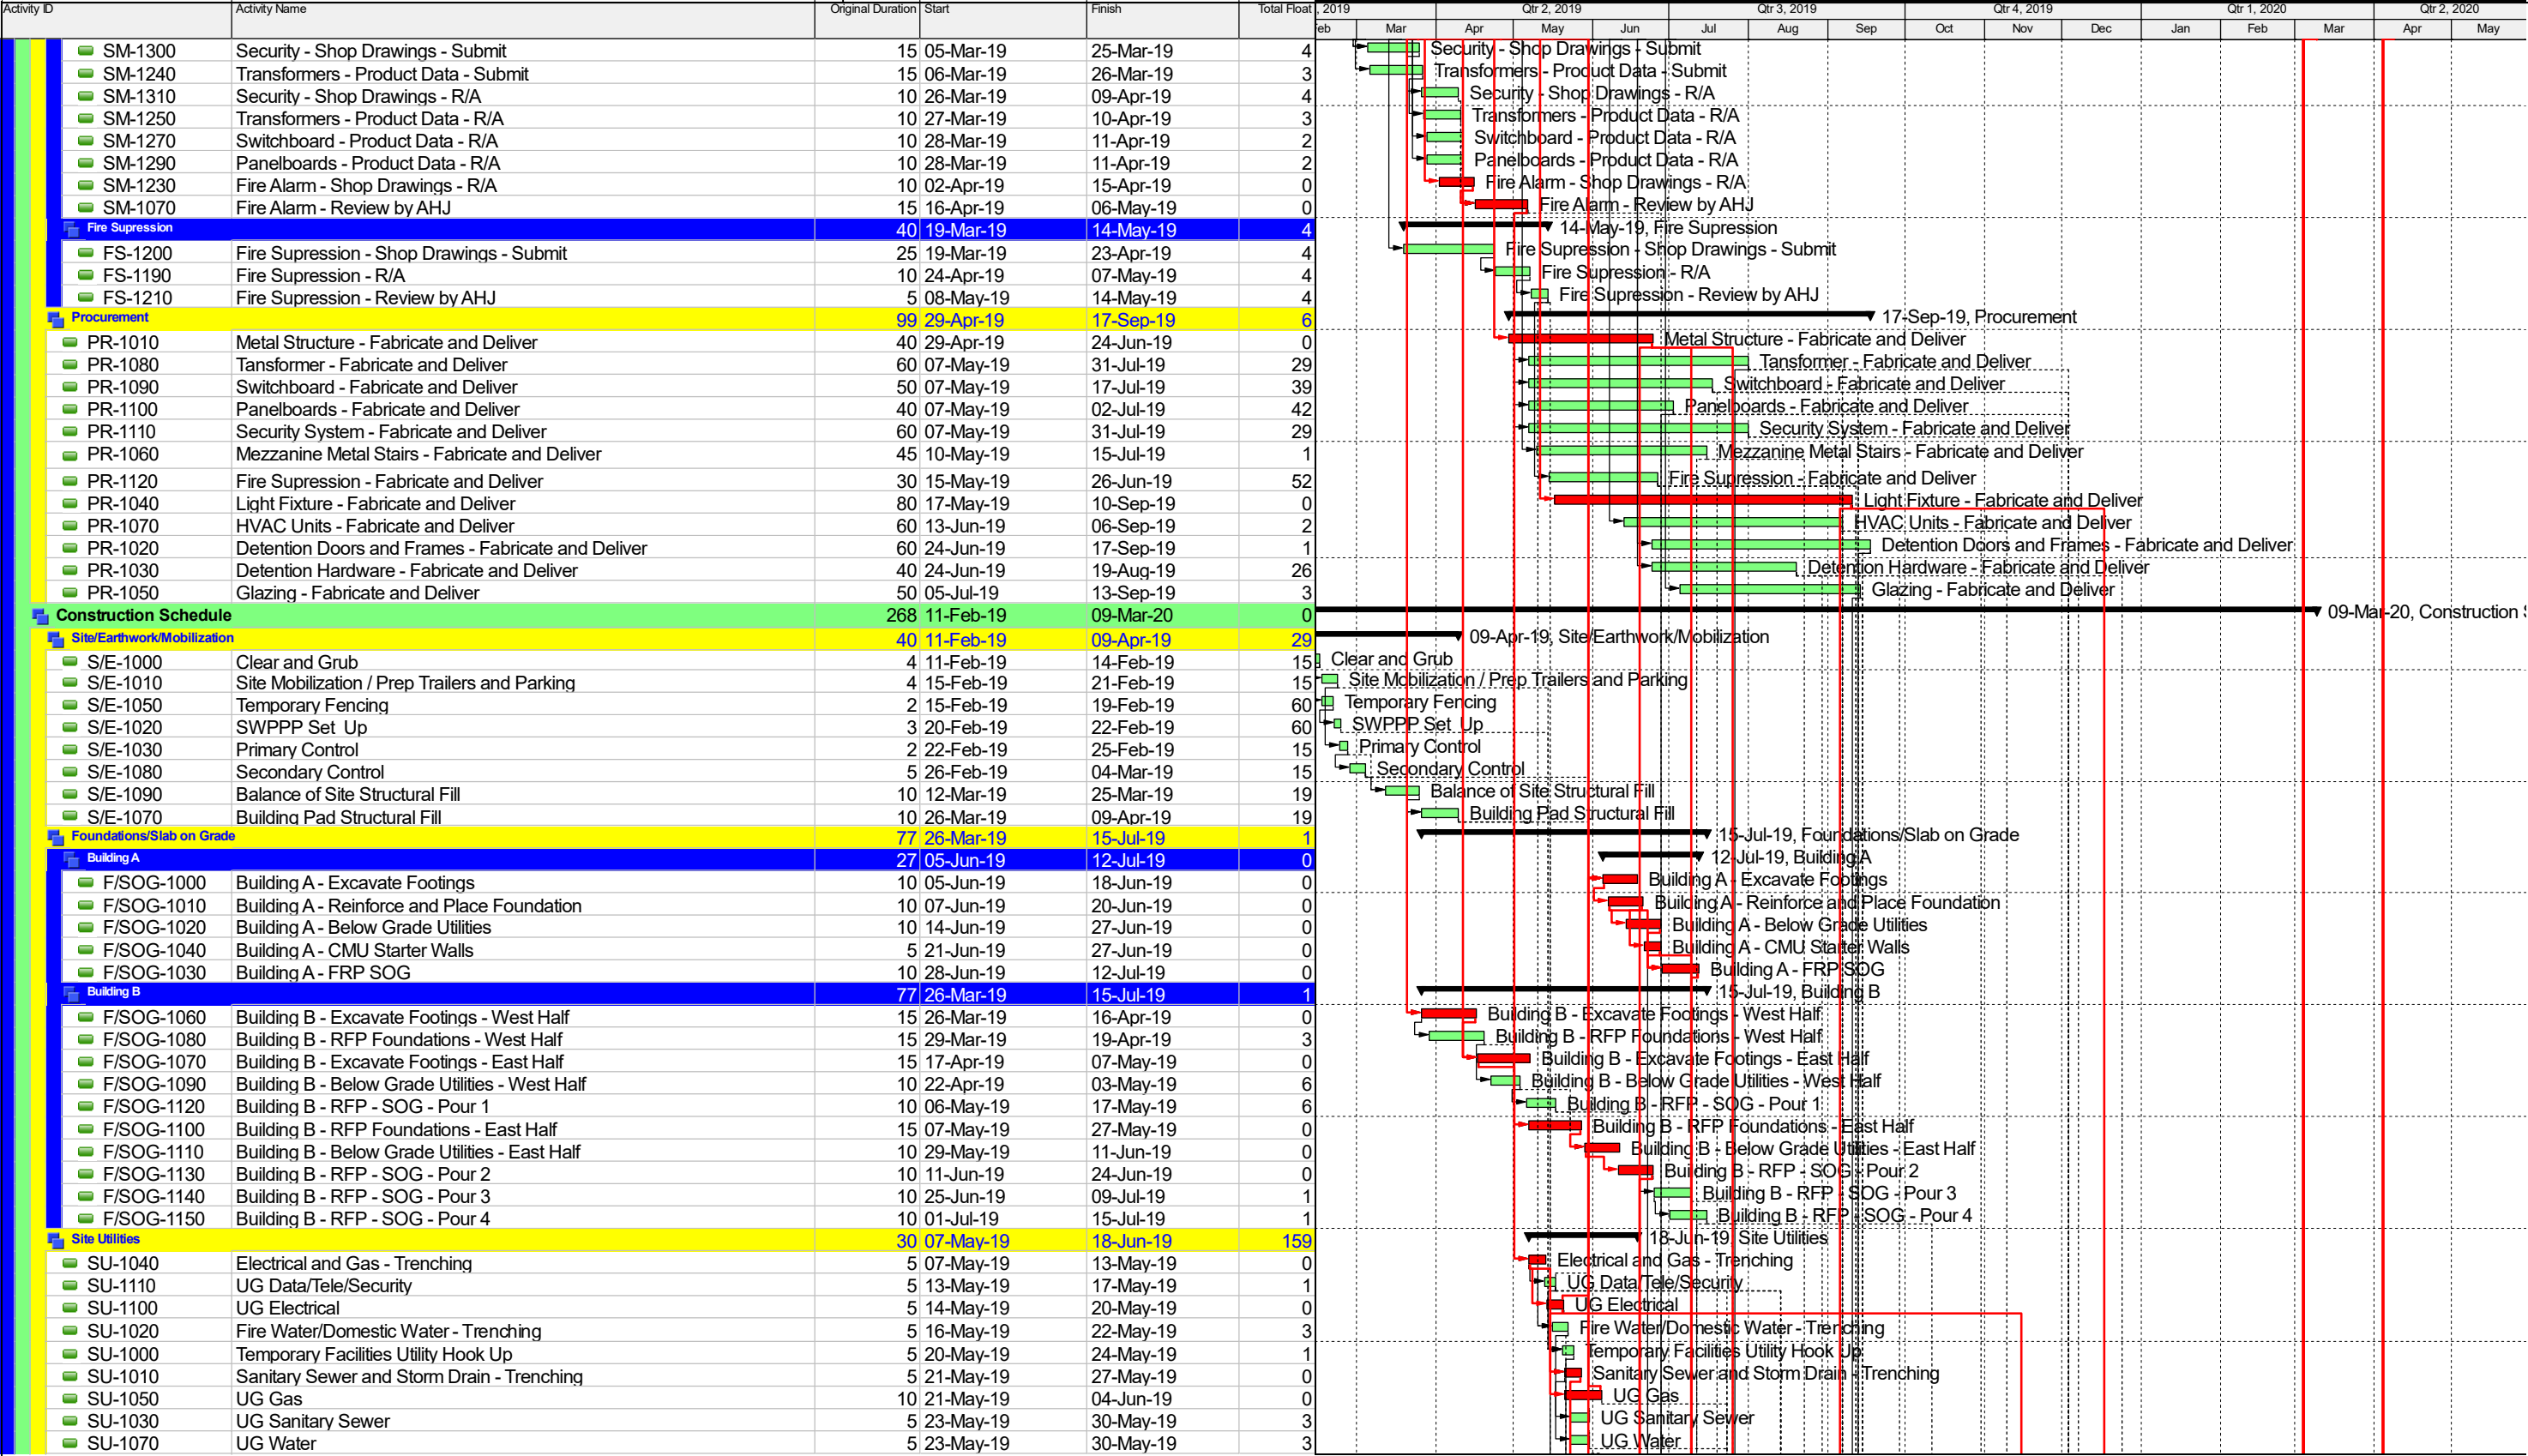

Page 2 of 6

TASK filter: All Activities

© Oracle Corporation

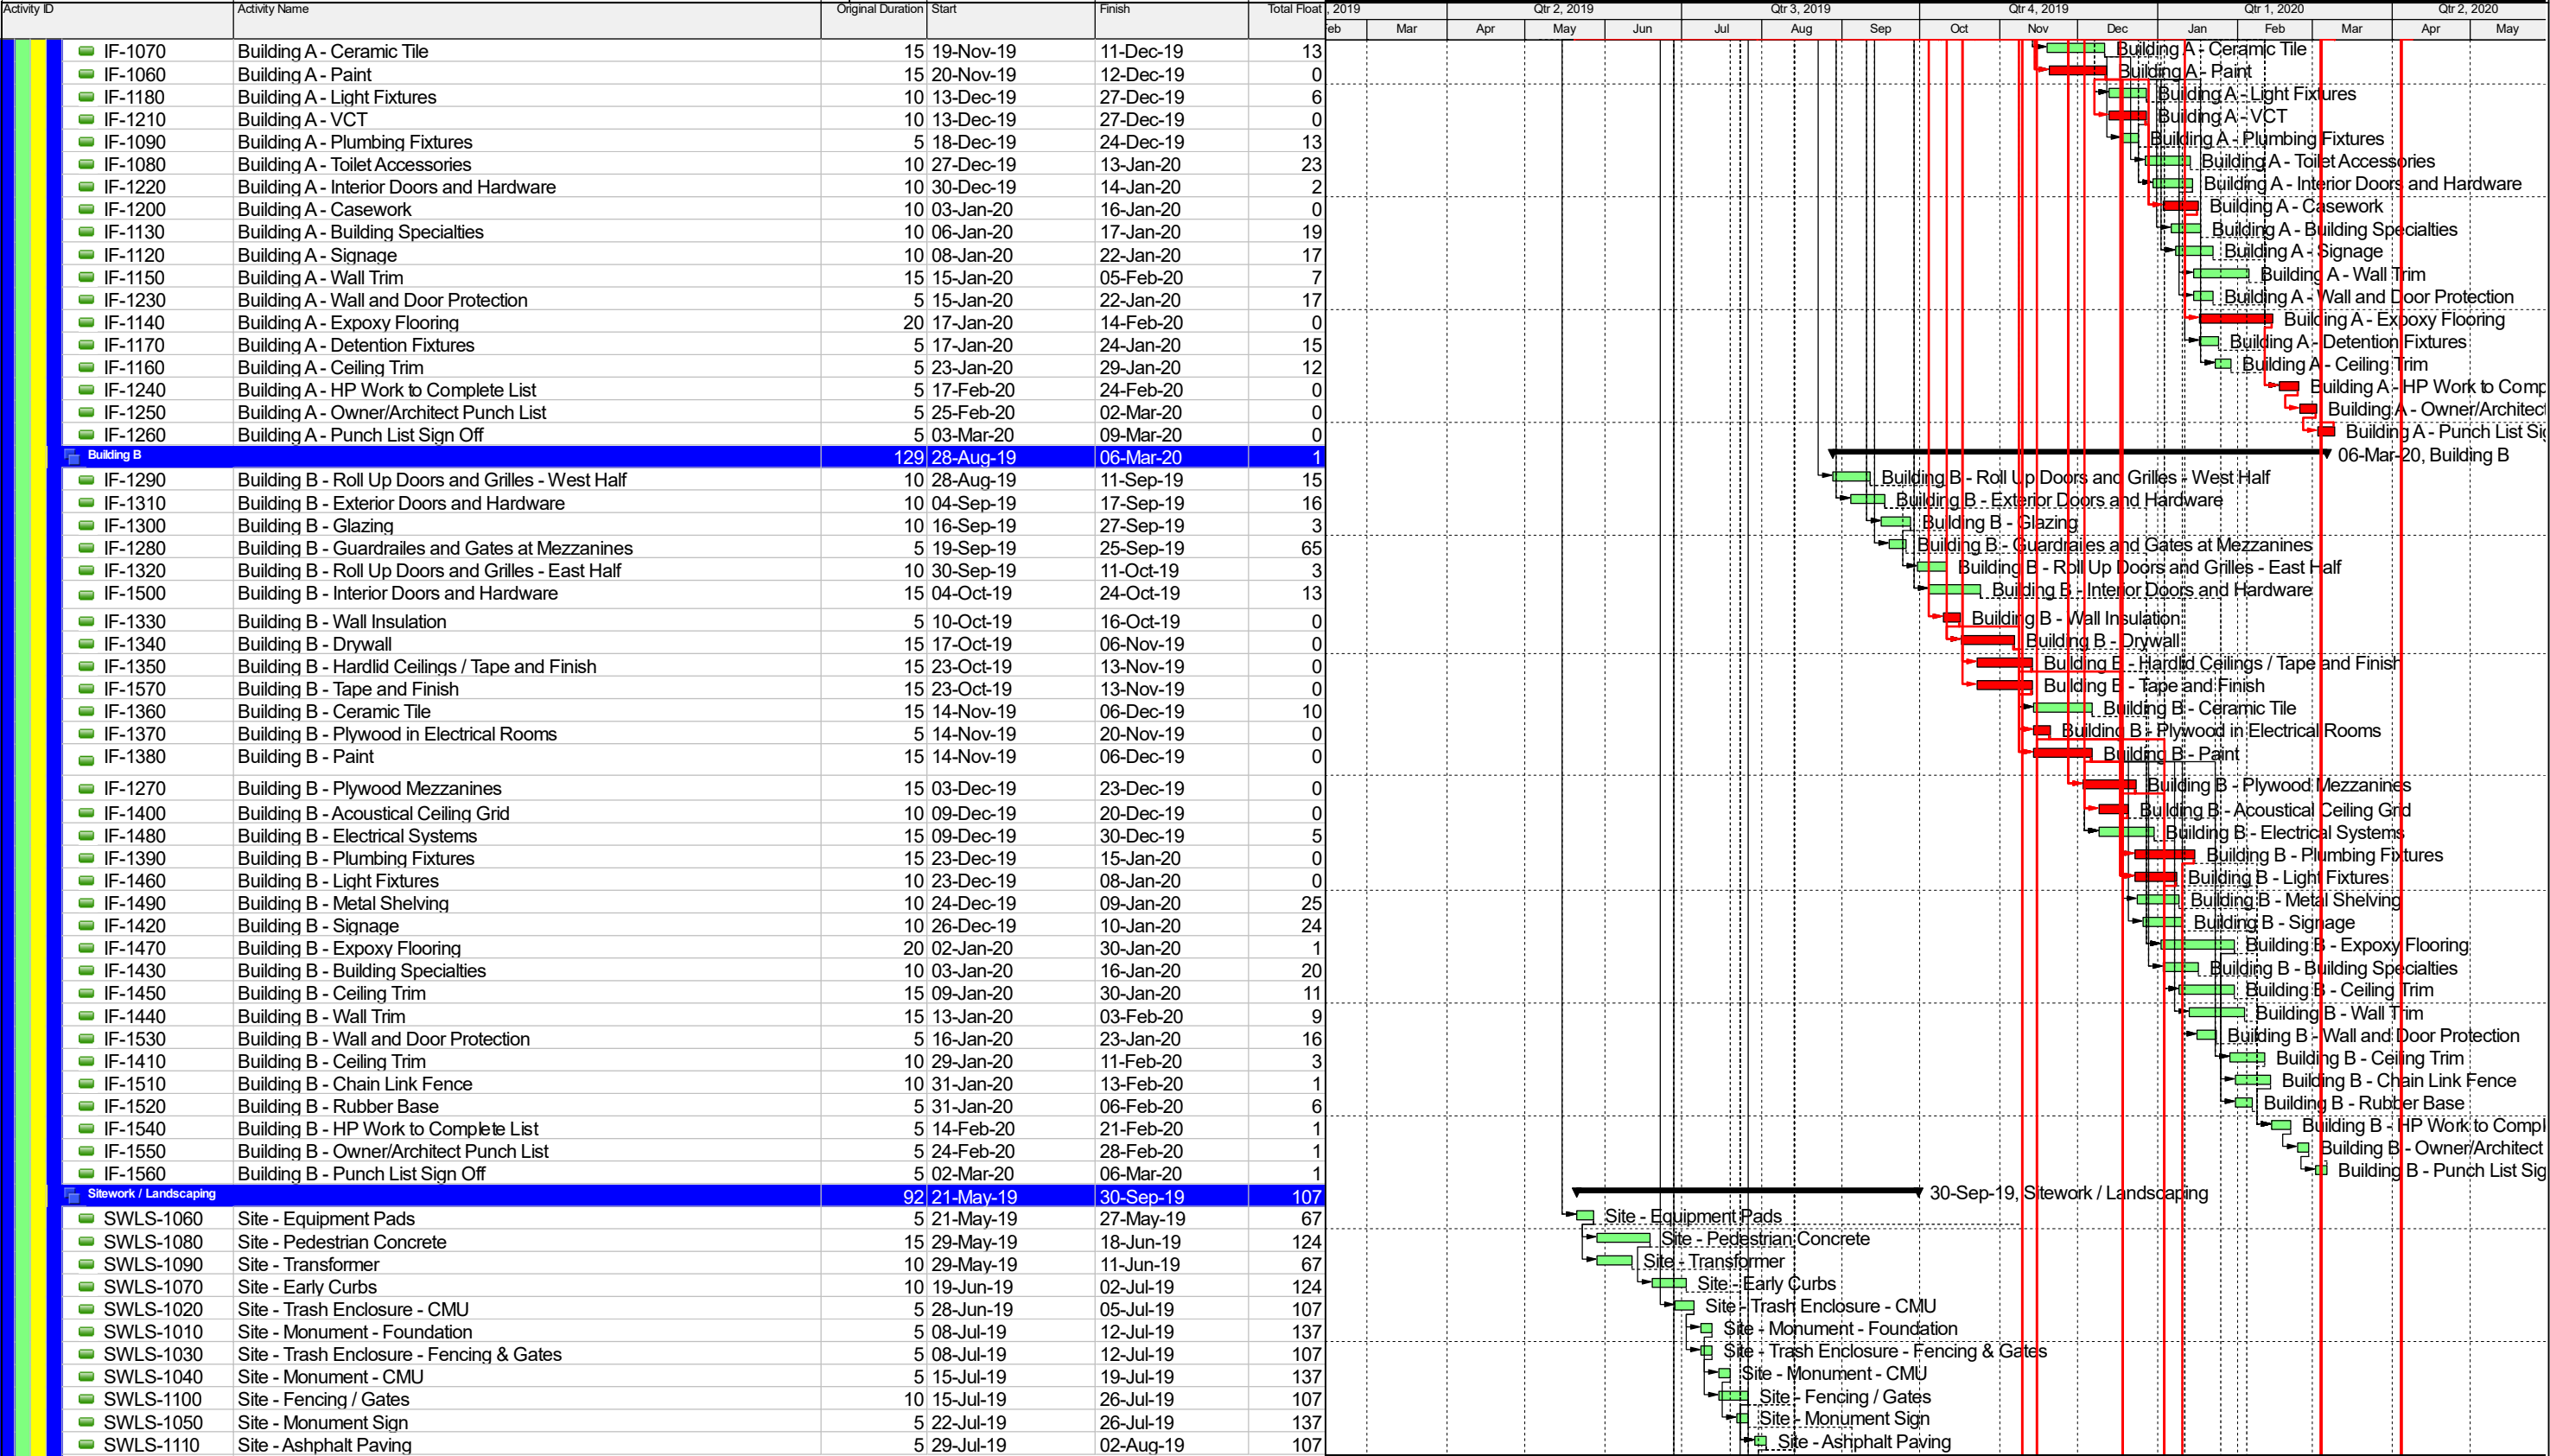

Actual Level of Effort


Actual Work

Remaining Work

Critical Remaining Work

Milestone

summary

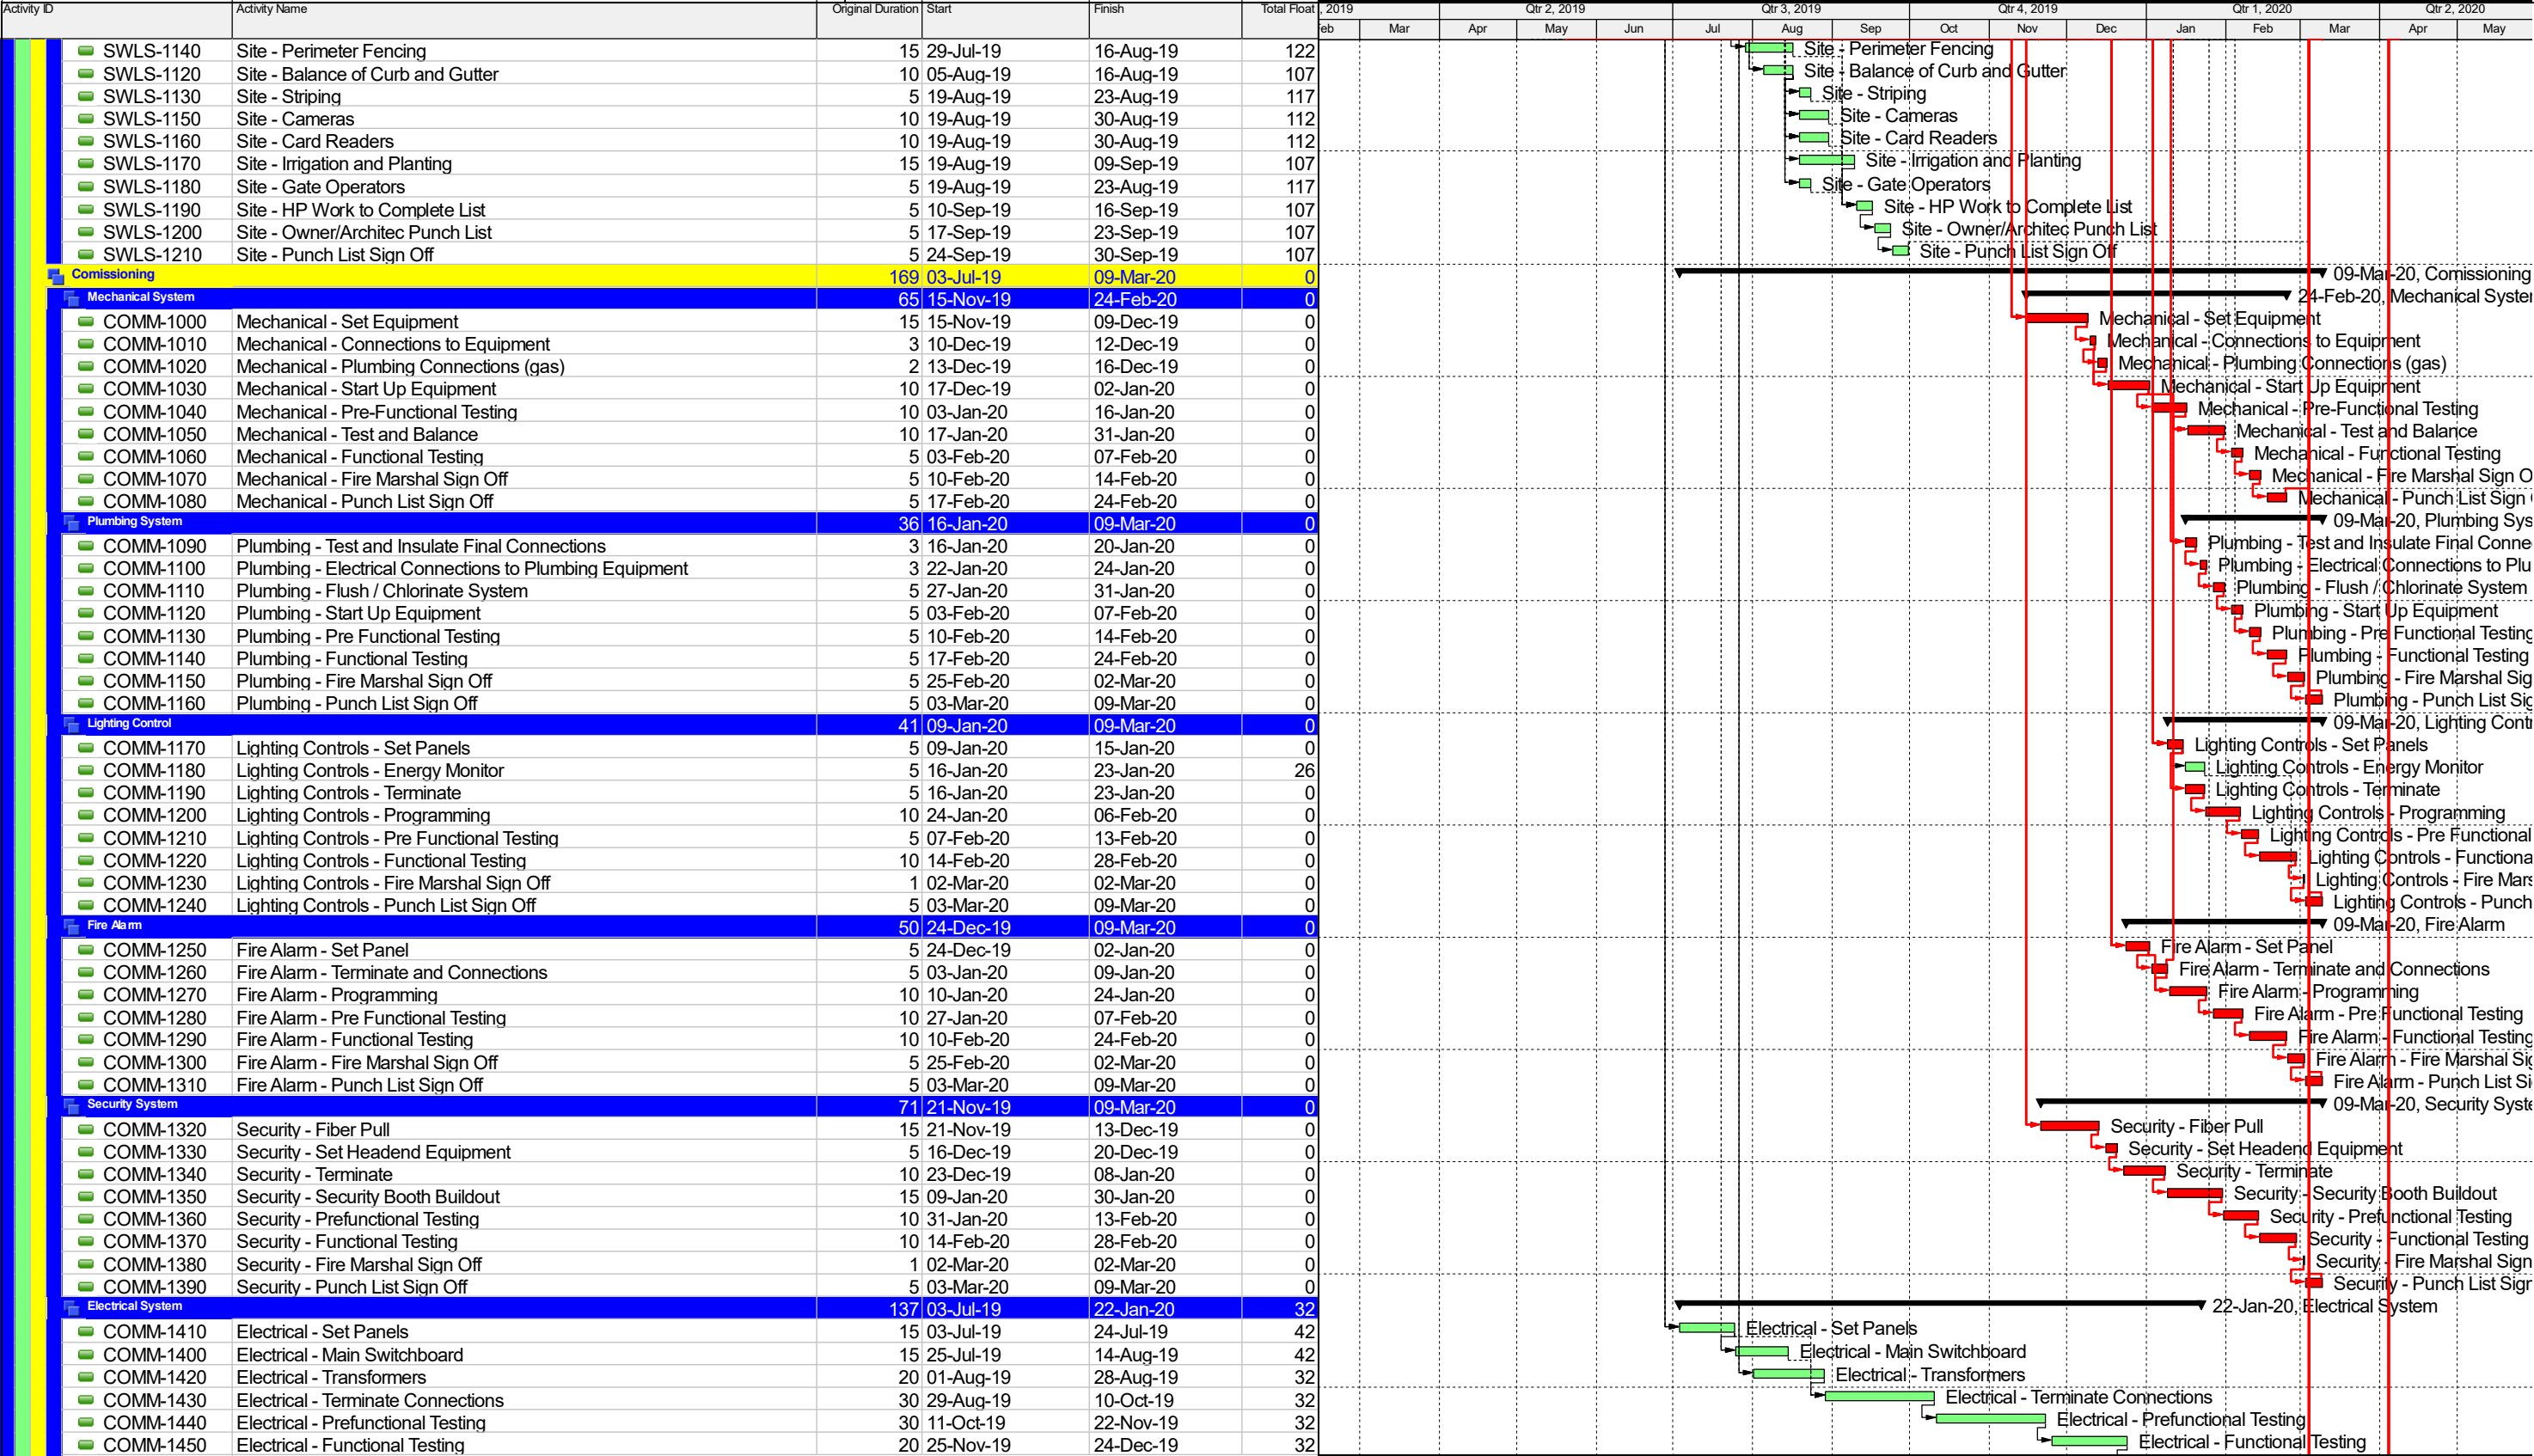

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

summary

