ID	Task Name	Duration	Start	Finish
1	**Construction Start**	0 days	Wed 2/15/12	Wed 2/15/12
2	**Mobilize onsite**	10 days	Fri 2/17/12	Thu 3/1/12
3	**Award Contract to Subcontractors**	2 days	Fri 3/2/12	Mon 3/5/12
4	**Detailed Coordination - BIM**	60 days	Tue 3/6/12	Mon 5/28/12
5	**Underground Excavation**	30 days	Fri 3/2/12	Thu 4/12/12
6	**Basement Construction:**	**95 days**	**Fri 4/13/12**	**Thu 8/23/12**
7	Slab on Grade Basement Level	21 days	Fri 4/13/12	Fri 5/11/12
8	1st Floor - Erect Steel and Deck	7 days	Mon 5/14/12	Tue 5/22/12
9	Pour Concrete	7 days	Wed 5/23/12	Thu 5/31/12
10	Set Equipment	5 days	Fri 6/1/12	Thu 6/7/12
11	MEPS Rough-In	30 days	Fri 6/8/12	Thu 7/19/12
12	Architectural Construction	10 days	Fri 7/20/12	Thu 8/2/12
13	MEPS Finishes	15 days	Fri 8/3/12	Thu 8/23/12
14	**1st Floor Construction:**	**152 days**	**Wed 5/23/12**	**Thu 12/20/12**
15	1st Floor - Erect Steel and Deck	21 days	Wed 5/23/12	Wed 6/20/12
16	Pour Concrete & Cure	21 days	Thu 6/21/12	Thu 7/19/12
17	Equipment Set	5 days	Fri 7/20/12	Thu 7/26/12
18	MEPS Rough-In	45 days	Fri 7/27/12	Thu 9/27/12
19	Architectural Construction	30 days	Fri 9/28/12	Thu 11/8/12
20	MEPS Finishes	30 days	Fri 11/9/12	Thu 12/20/12
21	**2nd Floor Construction:**	**152 days**	**Fri 7/20/12**	**Mon 2/18/13**
22	2nd Floor - Erect Steel and Deck	21 days	Fri 7/20/12	Fri 8/17/12
23	Pour Concrete & Cure	21 days	Mon 8/20/12	Mon 9/17/12
24	Equipment Set	5 days	Tue 9/18/12	Mon 9/24/12
25	MEPS Rough-In	45 days	Tue 9/25/12	Mon 11/26/12
26	Architectural Construction	30 days	Tue 11/27/12	Mon 1/7/13
27	MEPS Finishes	30 days	Tue 1/8/13	Mon 2/18/13
28	**3rd Floor Construction:**	**152 days**	**Tue 9/18/12**	**Wed 4/17/13**
29	3rd Floor - Erect Steel and Deck	21 days	Tue 9/18/12	Tue 10/16/12
30	Pour Concrete & Cure	21 days	Wed 10/17/12	Wed 11/14/12
31	Equipment Set	5 days	Thu 11/15/12	Wed 11/21/12
32	MEPS Rough-In	45 days	Thu 11/22/12	Wed 1/23/13
33	Architectural Construction	30 days	Thu 1/24/13	Wed 3/6/13
34	MEPS Finishes	30 days	Thu 3/7/13	Wed 4/17/13
35	**4th Floor Construction:**	**152 days**	**Thu 11/15/12**	**Fri 6/14/13**
36	4th Floor - Erect Steel and Deck	21 days	Thu 11/15/12	Thu 12/13/12
37	Pour Concrete & Cure	21 days	Fri 12/14/12	Fri 1/11/13
38	Equipment Set	5 days	Mon 1/14/13	Fri 1/18/13
39	MEPS Rough-In	45 days	Mon 1/21/13	Fri 3/22/13
40	Architectural Construction	30 days	Mon 3/25/13	Fri 5/3/13
41	MEPS Finishes	30 days	Mon 5/6/13	Fri 6/14/13
42	**Roof Construction:**	**73 days**	**Fri 12/14/12**	**Tue 3/26/13**
43	MEPS Roof Cans	10 days	Fri 12/14/12	Thu 12/27/12
44	Equipment Pad Layout	2 days	Mon 1/14/13	Tue 1/15/13
45	Crane & Rigging for Roof Top Equipment	5 days	Wed 1/16/13	Tue 1/22/13
46	Equipment Hookup/Tie-in	15 days	Wed 1/23/13	Tue 2/12/13
47	Roofing Finish	30 days	Wed 2/13/13	Tue 3/26/13
48	**Comissioning & Start Up:**	**40 days**	**Mon 6/17/13**	**Fri 8/9/13**
49	Equipment Start Up	10 days	Mon 6/17/13	Fri 6/28/13
50	Testing & Balancing	10 days	Mon 7/1/13	Fri 7/12/13
51	Commissioning	20 days	Mon 7/15/13	Fri 8/9/13
52	**Construction Complete Milestone**	0 days	Fri 8/9/13	Fri 8/9/13

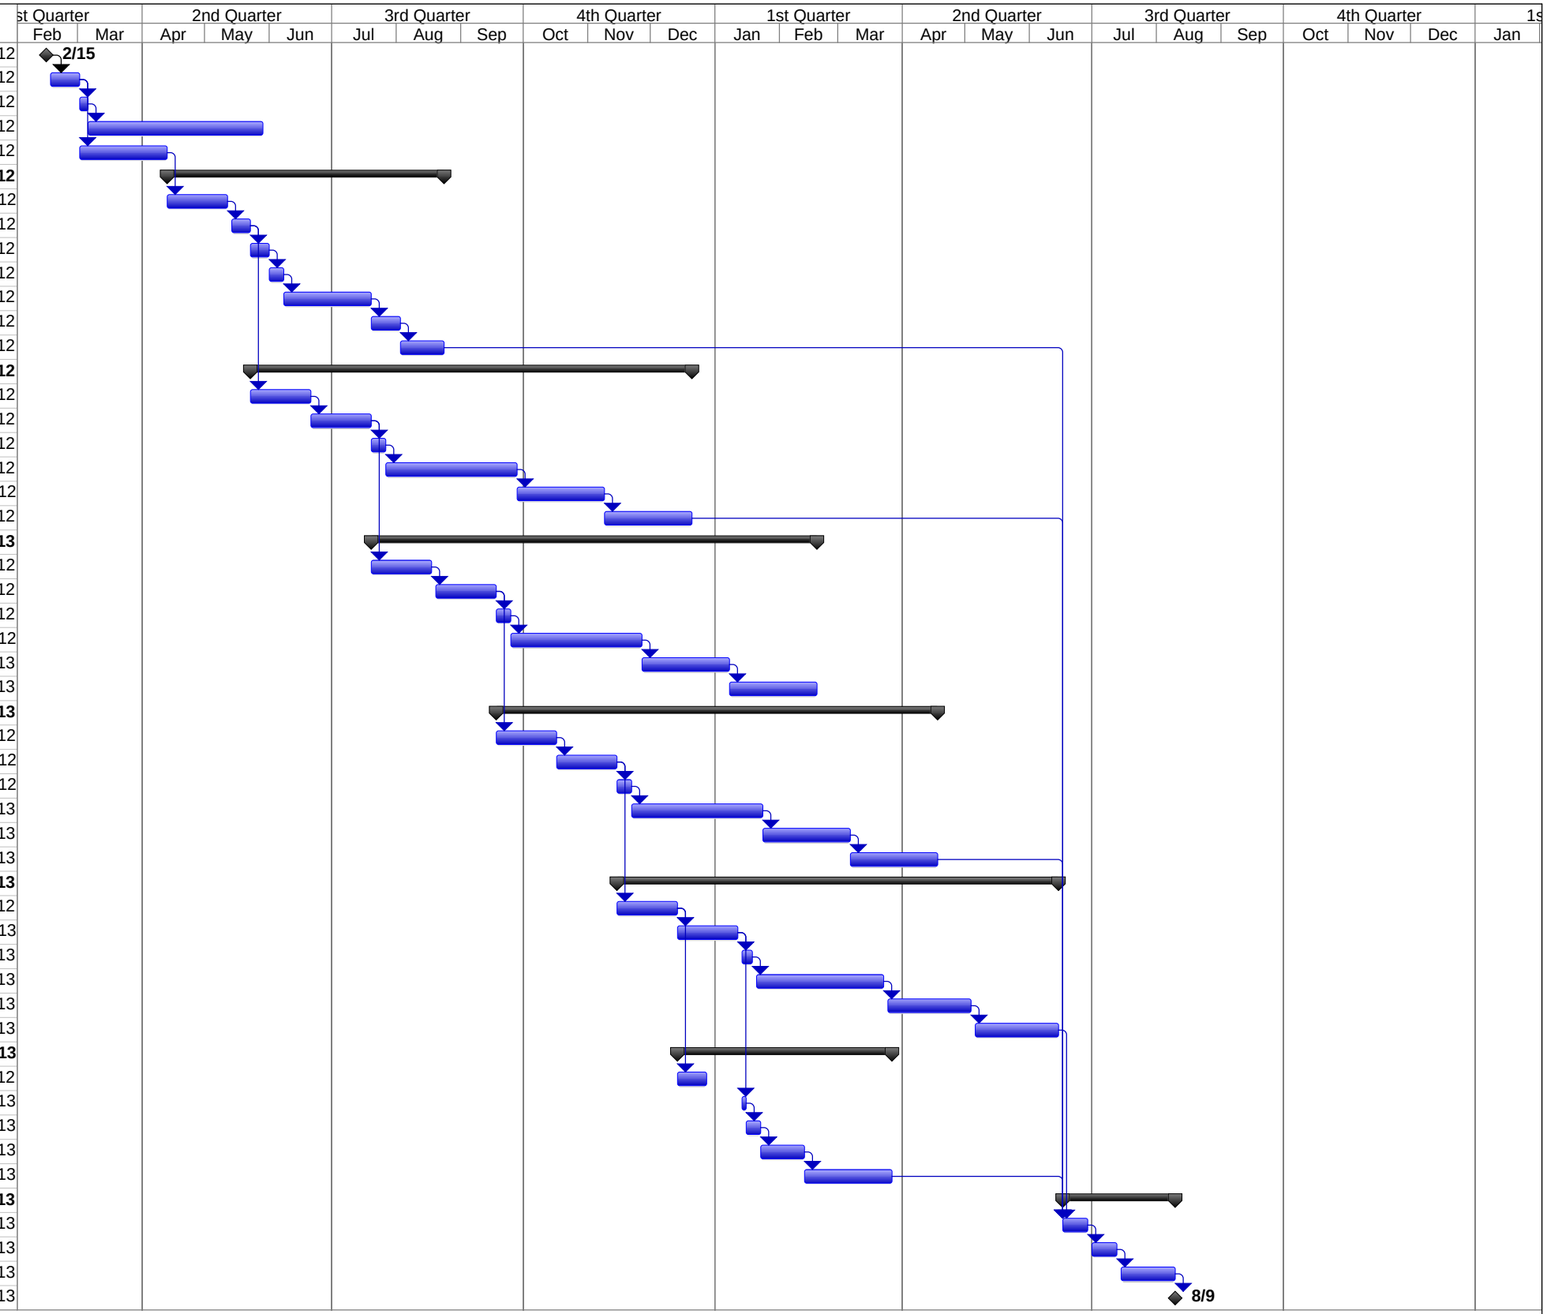

Project: ASC RENO 2012 - Constructio
Date: Wed 1/11/12

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
