


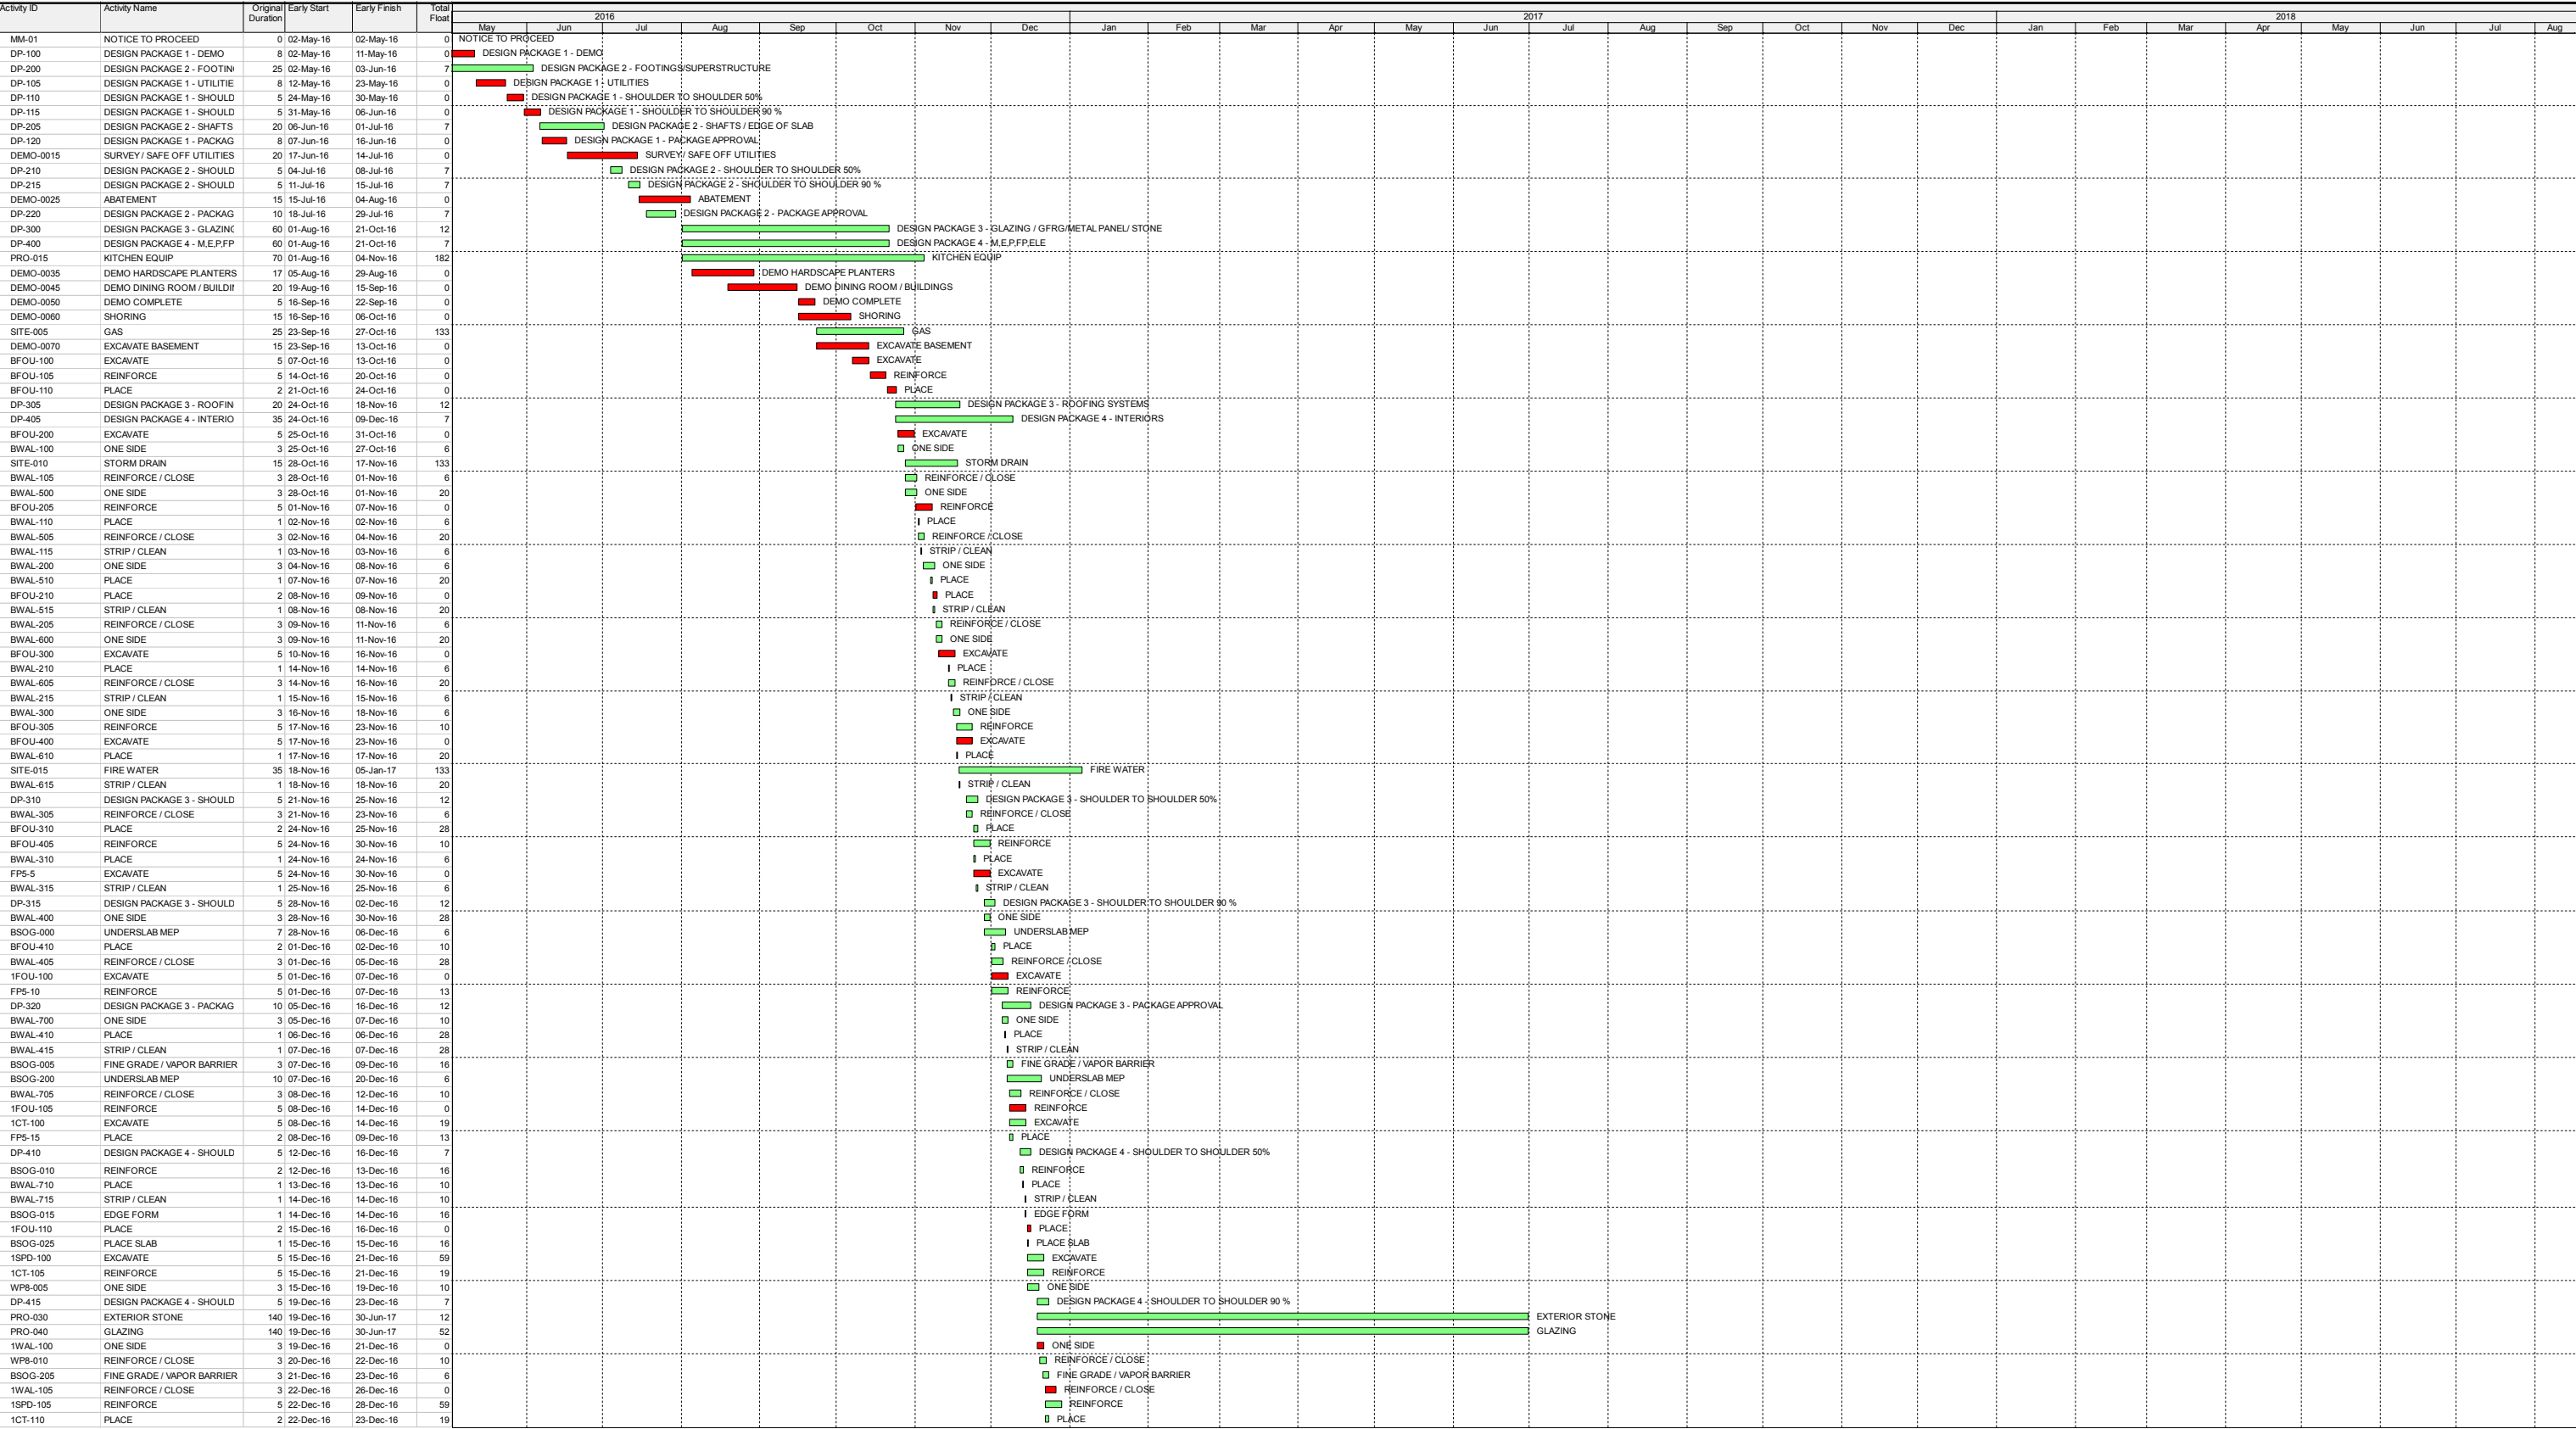

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Start Date: 02-May-16

Finish Date: 01-Aug-18

Data Date: 01-May-16

Run Date: 15-Jan-16

15-Jan-16

TASK filter: All Activities

RENO MCEP


ANSWER SCHEDULE

[illegible]

[illegible]





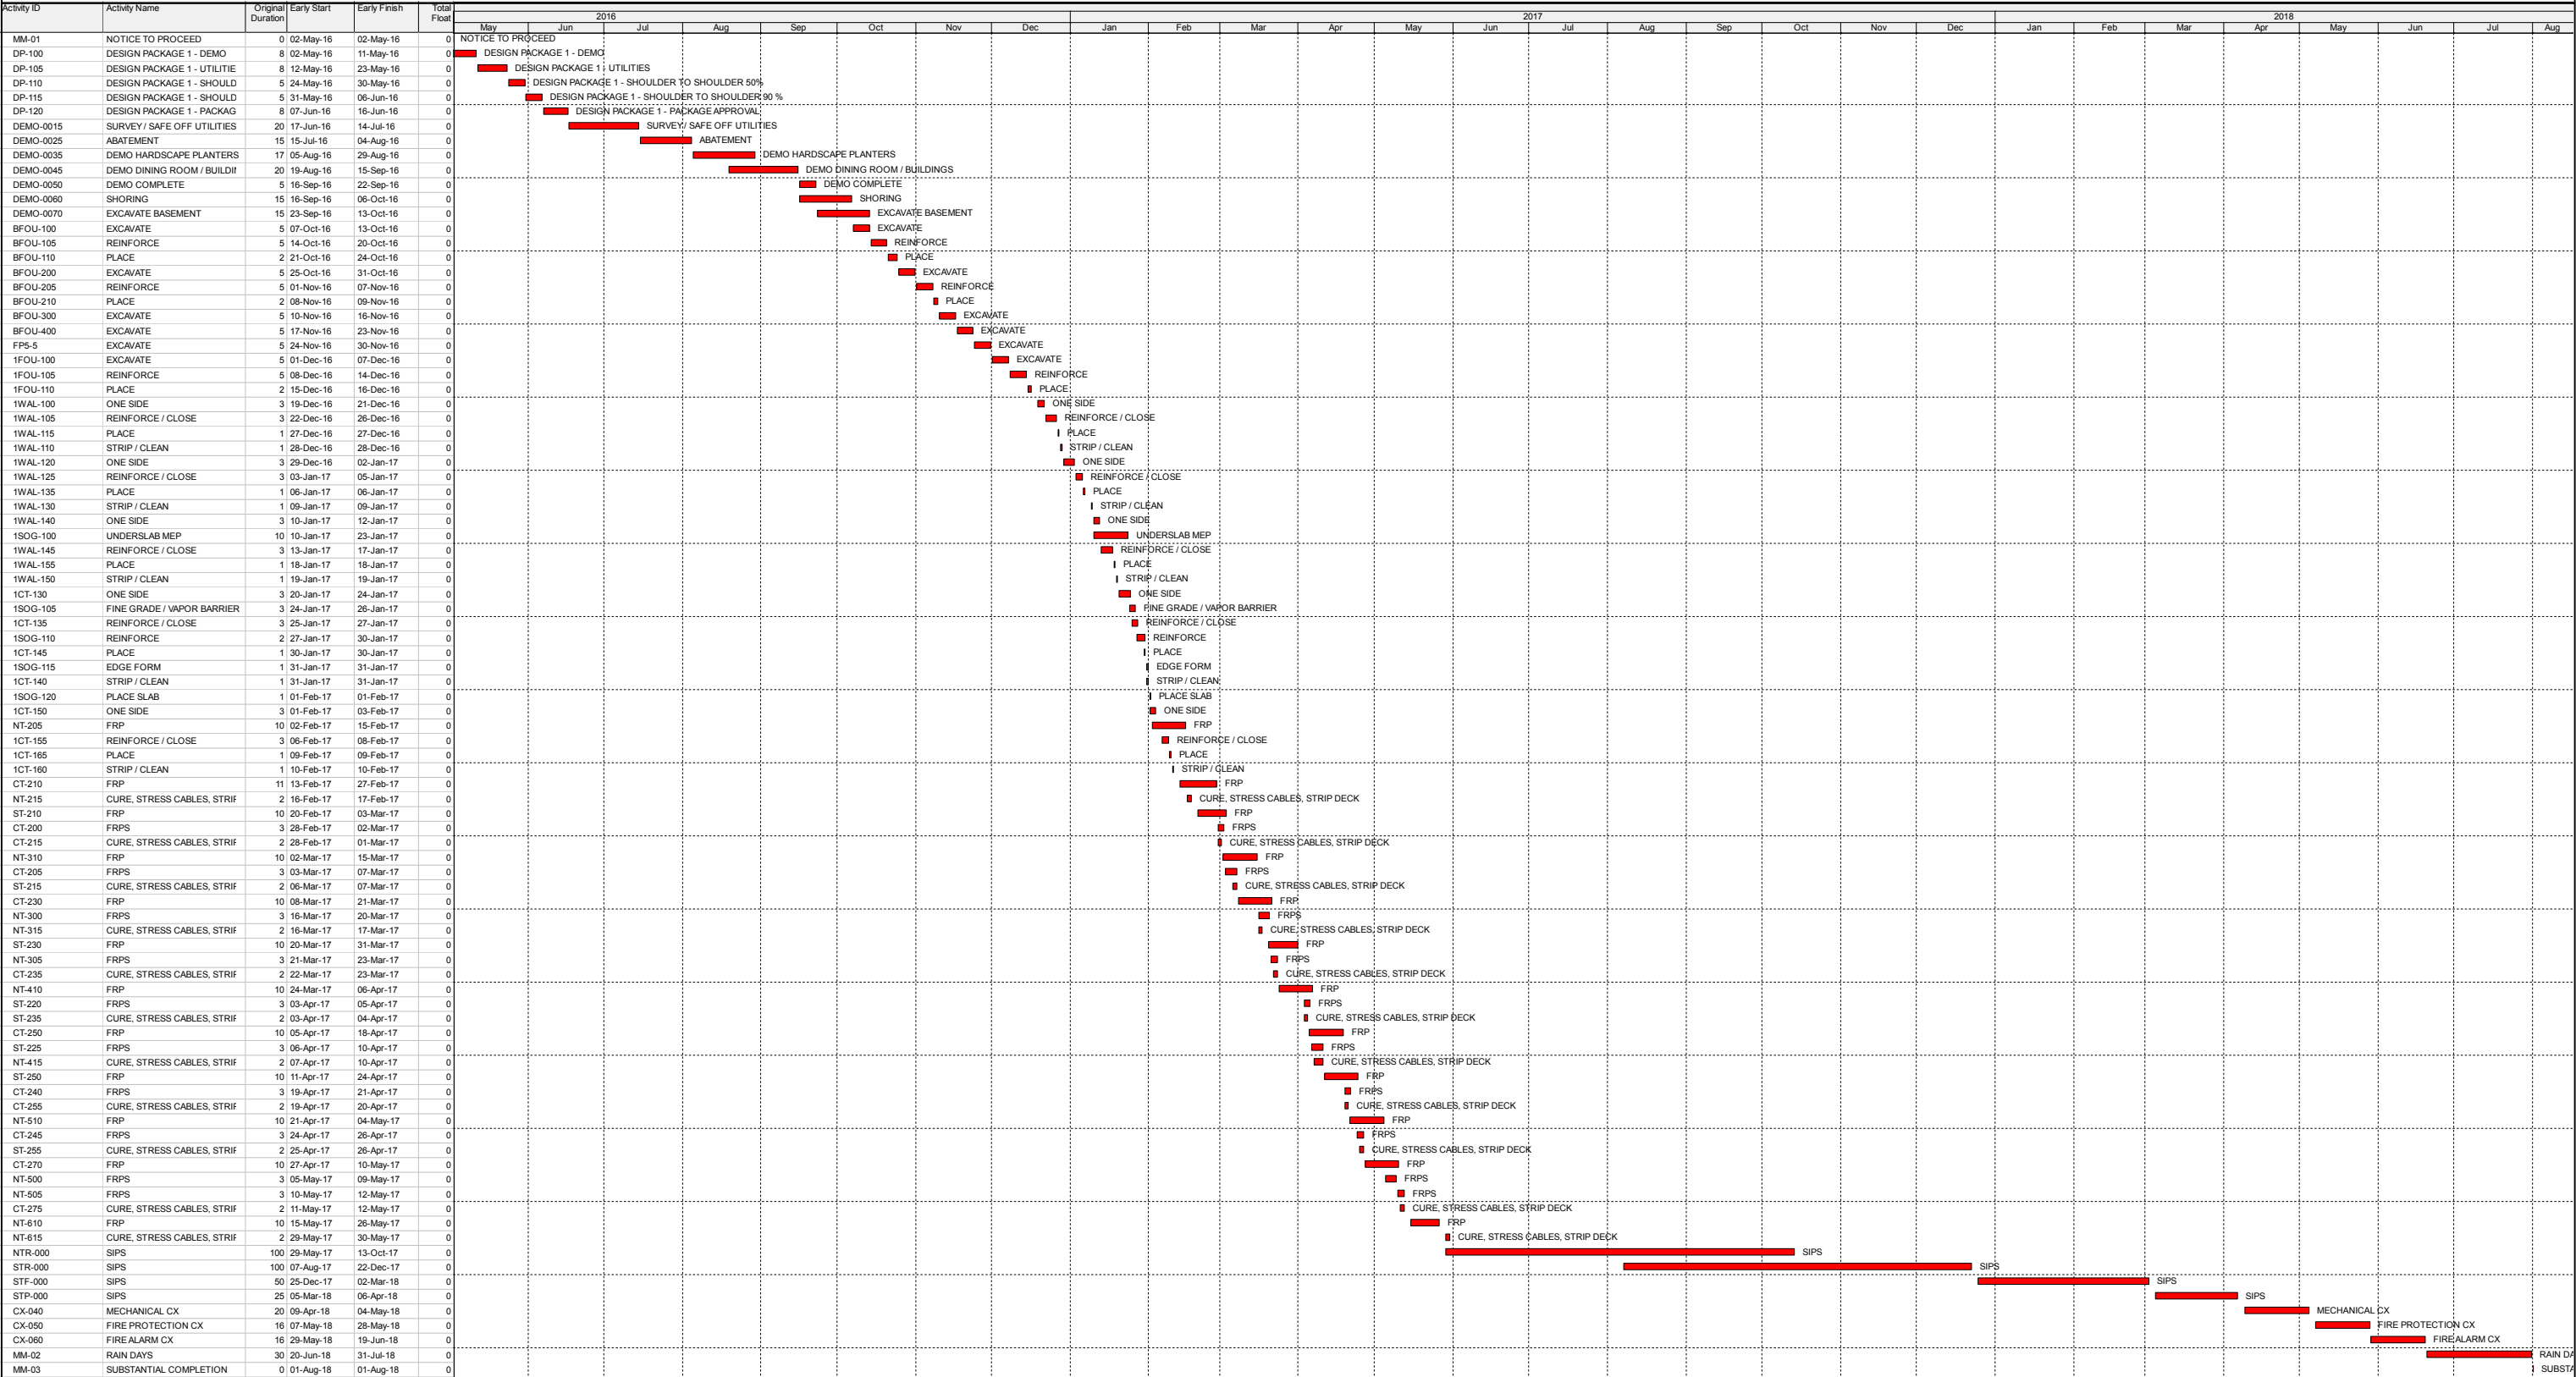

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆

◆ Milestone

Start Date: 02-May-16

Finish Date: 01-Aug-18

Data Date: 01-May-16


Run Date: 15-Jan-16

15-Jan-16

TASK filter: Longest Path.

RENO MCEP

ANSWER SCHEDULE

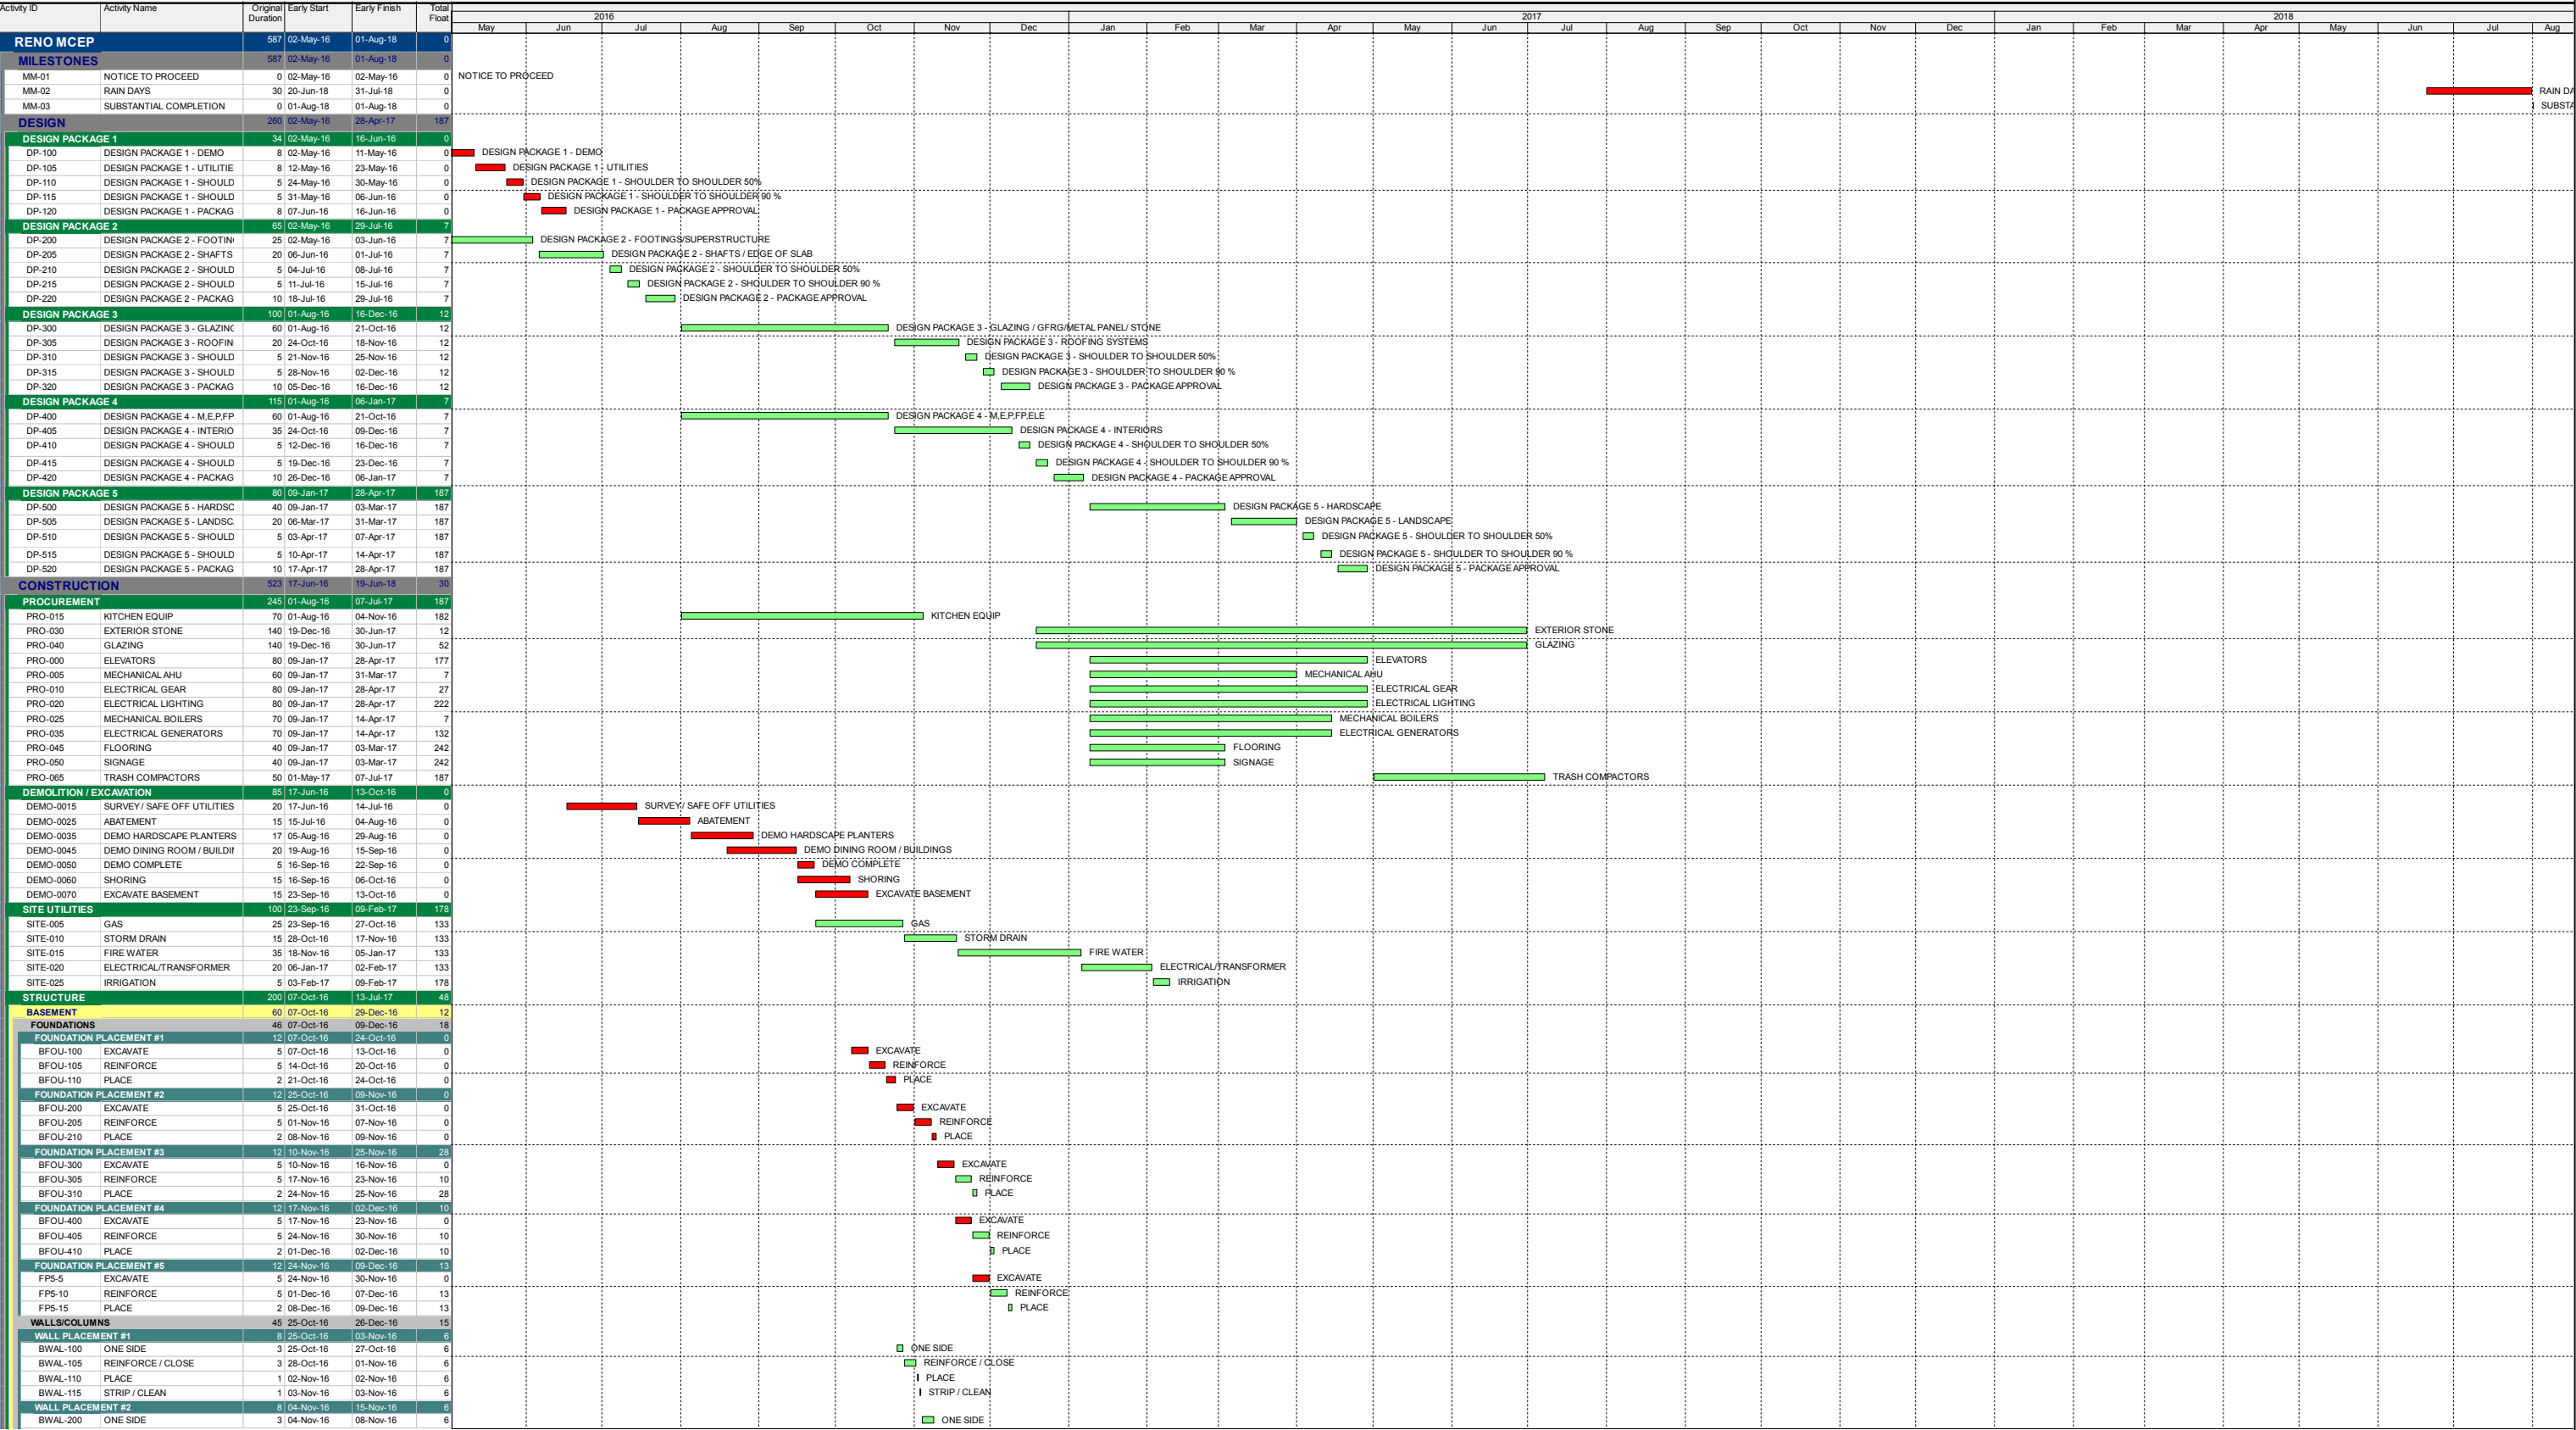

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Start Date: 02-May-16

Finish Date: 01-Aug-18

Data Date: 01-May-16

Run Date: 15-Jan-16

15-Jan-16

TASK filter: All Activities


RENO MCEP

ANSWER SCHEDULE

[illegible]

| Activity ID                             | Activity Name              | Original Duration | Early Start | Early Finish | Total Float | 2016 |     |     |     |     |     |     |     |     |     |     |     | 2017 |     |     |     |     |     |     |     |     |     |     |     | 2018 |     |     |     |  |  |  |  |  |  |  |  |
|-----------------------------------------|----------------------------|-------------------|-------------|--------------|-------------|------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|------|-----|-----|-----|--|--|--|--|--|--|--|--|
|                                         |                            |                   |             |              |             | May  | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May  | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May  | Jun | Jul | Aug |  |  |  |  |  |  |  |  |
| 1CT-195                                 | FINE GRADE / VAPOR BARRIER |                   | 3           | 07-Feb-17    | 09-Feb-17   | 62   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1CT-200                                 | REINFORCE                  |                   | 2           | 10-Feb-17    | 13-Feb-17   | 62   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1CT-205                                 | EDGE FORM                  |                   | 1           | 14-Feb-17    | 14-Feb-17   | 62   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1CT-210                                 | PLACE SLAB                 |                   | 1           | 15-Feb-17    | 15-Feb-17   | 62   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOG #4                                  |                            |                   | 46          | 07-Feb-17    | 11-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| CSOG-5                                  | UNDERSLAB MEP              |                   | 10          | 07-Feb-17    | 20-Feb-17   | 54   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| CSOG-10                                 | FINE GRADE / VAPOR BARRIER |                   | 3           | 21-Feb-17    | 23-Feb-17   | 54   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| CSOG-15                                 | REINFORCE                  |                   | 2           | 24-Feb-17    | 27-Feb-17   | 54   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| CSOG-20                                 | EDGE FORM                  |                   | 1           | 28-Feb-17    | 28-Feb-17   | 54   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| CSOG-25                                 | PLACE SLAB                 |                   | 1           | 11-Apr-17    | 11-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOD                                     |                            |                   | 19          | 30-Dec-16    | 25-Jan-17   | 12   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOD #1                                  |                            |                   | 19          | 30-Dec-16    | 25-Jan-17   | 12   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SOD-210                                | FRP                        |                   | 13          | 30-Dec-16    | 17-Jan-17   | 12   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SOD-215                                | CURE / STRESS / STRIP      |                   | 6           | 18-Jan-17    | 25-Jan-17   | 12   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOUTH PODIUM                            |                            |                   | 93          | 15-Dec-16    | 24-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| FOUNDATIONS                             |                            |                   | 48          | 15-Dec-16    | 20-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| FOUNDATION PLACEMENT #3 (EAST MAT)      |                            |                   | 12          | 15-Dec-16    | 30-Dec-16   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-100                                | EXCAVATE                   |                   | 5           | 15-Dec-16    | 21-Dec-16   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-105                                | REINFORCE                  |                   | 5           | 22-Dec-16    | 28-Dec-16   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-110                                | PLACE                      |                   | 2           | 29-Dec-16    | 30-Dec-16   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| FOUNDATION PLACEMENT #4 (CENTER SPOT)   |                            |                   | 12          | 02-Jan-17    | 17-Jan-17   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-115                                | EXCAVATE                   |                   | 5           | 02-Jan-17    | 06-Jan-17   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-120                                | REINFORCE                  |                   | 5           | 09-Jan-17    | 13-Jan-17   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-125                                | PLACE                      |                   | 2           | 16-Jan-17    | 17-Jan-17   | 59   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| FOUNDATION PLACEMENT #5 (WEST MAT)      |                            |                   | 12          | 18-Jan-17    | 02-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-130                                | EXCAVATE                   |                   | 5           | 18-Jan-17    | 24-Jan-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-135                                | REINFORCE                  |                   | 5           | 25-Jan-17    | 31-Jan-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-140                                | PLACE                      |                   | 2           | 01-Feb-17    | 02-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| FOUNDATION PLACEMENT #7 (PAVILION)      |                            |                   | 12          | 03-Feb-17    | 20-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-145                                | EXCAVATE                   |                   | 5           | 03-Feb-17    | 09-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-150                                | REINFORCE                  |                   | 5           | 10-Feb-17    | 16-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-155                                | PLACE                      |                   | 2           | 17-Feb-17    | 20-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WALLS/COLUMNS                           |                            |                   | 26          | 21-Feb-17    | 28-Mar-17   | 120  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WALL PLACEMENT #1 (EAST SHEAR WALL & I  |                            |                   | 8           | 23-Feb-17    | 06-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-160                                | ONE SIDE                   |                   | 3           | 23-Feb-17    | 27-Feb-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-165                                | REINFORCE / CLOSE          |                   | 3           | 28-Feb-17    | 02-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-175                                | PLACE                      |                   | 1           | 03-Mar-17    | 03-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-170                                | STRIP / CLEAN              |                   | 1           | 06-Mar-17    | 06-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WALL PLACEMENT #2 (COLUMNS)             |                            |                   | 8           | 07-Mar-17    | 16-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-180                                | ONE SIDE                   |                   | 3           | 07-Mar-17    | 09-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-185                                | REINFORCE / CLOSE          |                   | 3           | 10-Mar-17    | 14-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-195                                | PLACE                      |                   | 1           | 15-Mar-17    | 15-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-190                                | STRIP / CLEAN              |                   | 1           | 16-Mar-17    | 16-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WALL PLACEMENT #3 (WEST SHEAR WALLS & I |                            |                   | 8           | 17-Mar-17    | 28-Mar-17   | 103  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-200                                | ONE SIDE                   |                   | 3           | 17-Mar-17    | 21-Mar-17   | 103  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-205                                | REINFORCE / CLOSE          |                   | 3           | 22-Mar-17    | 24-Mar-17   | 103  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-215                                | PLACE                      |                   | 1           | 27-Mar-17    | 27-Mar-17   | 103  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-210                                | STRIP / CLEAN              |                   | 1           | 28-Mar-17    | 28-Mar-17   | 103  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WALL PLACEMENT #4 (PAVILION BLDG)       |                            |                   | 8           | 21-Feb-17    | 02-Mar-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SP-400                                 | ONE SIDE                   |                   | 3           | 21-Feb-17    | 23-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SP-405                                 | REINFORCE / CLOSE          |                   | 3           | 24-Feb-17    | 28-Feb-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SP-415                                 | PLACE                      |                   | 1           | 01-Mar-17    | 01-Mar-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SP-410                                 | STRIP / CLEAN              |                   | 1           | 02-Mar-17    | 02-Mar-17   | 138  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOG                                     |                            |                   | 27          | 17-Mar-17    | 24-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOG #3                                  |                            |                   | 17          | 17-Mar-17    | 10-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-300                                | UNDERSLAB MEP              |                   | 10          | 17-Mar-17    | 30-Mar-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-305                                | FINE GRADE / VAPOR BARRIER |                   | 3           | 31-Mar-17    | 04-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-310                                | REINFORCE                  |                   | 2           | 05-Apr-17    | 06-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-315                                | EDGE FORM                  |                   | 1           | 07-Apr-17    | 07-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-320                                | PLACE SLAB                 |                   | 1           | 10-Apr-17    | 10-Apr-17   | 25   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOG #5                                  |                            |                   | 17          | 31-Mar-17    | 24-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-325                                | UNDERSLAB MEP              |                   | 10          | 31-Mar-17    | 13-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-330                                | FINE GRADE / VAPOR BARRIER |                   | 3           | 14-Apr-17    | 18-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-335                                | REINFORCE                  |                   | 2           | 19-Apr-17    | 20-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-340                                | EDGE FORM                  |                   | 1           | 21-Apr-17    | 21-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| 1SPD-345                                | PLACE SLAB                 |                   | 1           | 24-Apr-17    | 24-Apr-17   | 101  |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| NORTH TOWER                             |                            |                   | 104         | 02-Feb-17    | 27-Jun-17   | 16   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| L2                                      |                            |                   | 16          | 02-Feb-17    | 23-Feb-17   | 4    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| SOD                                     |                            |                   | 12          | 02-Feb-17    | 17-Feb-17   | 0    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| NT-205                                  | FRP                        |                   | 10          | 02-Feb-17    | 15-Feb-17   | 0    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| NT-215                                  | CURE, STRESS CABLES, STRIP |                   | 2           | 16-Feb-17    | 17-Feb-17   | 0    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WALLS / COLUMNS                         |                            |                   | 6           | 16-Feb-17    | 23-Feb-17   | 4    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| EAST WALLS / COLUMNS                    |                            |                   | 3           | 16-Feb-17    | 20-Feb-17   | 4    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| NT-000                                  | FRPS                       |                   | 3           | 16-Feb-17    | 20-Feb-17   | 4    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| WEST WALLS/ COLUMNS                     |                            |                   | 3           | 21-Feb-17    | 23-Feb-17   | 4    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| NT-200                                  | FRPS                       |                   | 3           | 21-Feb-17    | 23-Feb-17   | 4    |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |
| L3                                      |                            |                   | 16          | 02-Mar-17    | 23-Mar-17   | 0    |     |     |     |     |     |     |     |     |     |     |     | </   |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |



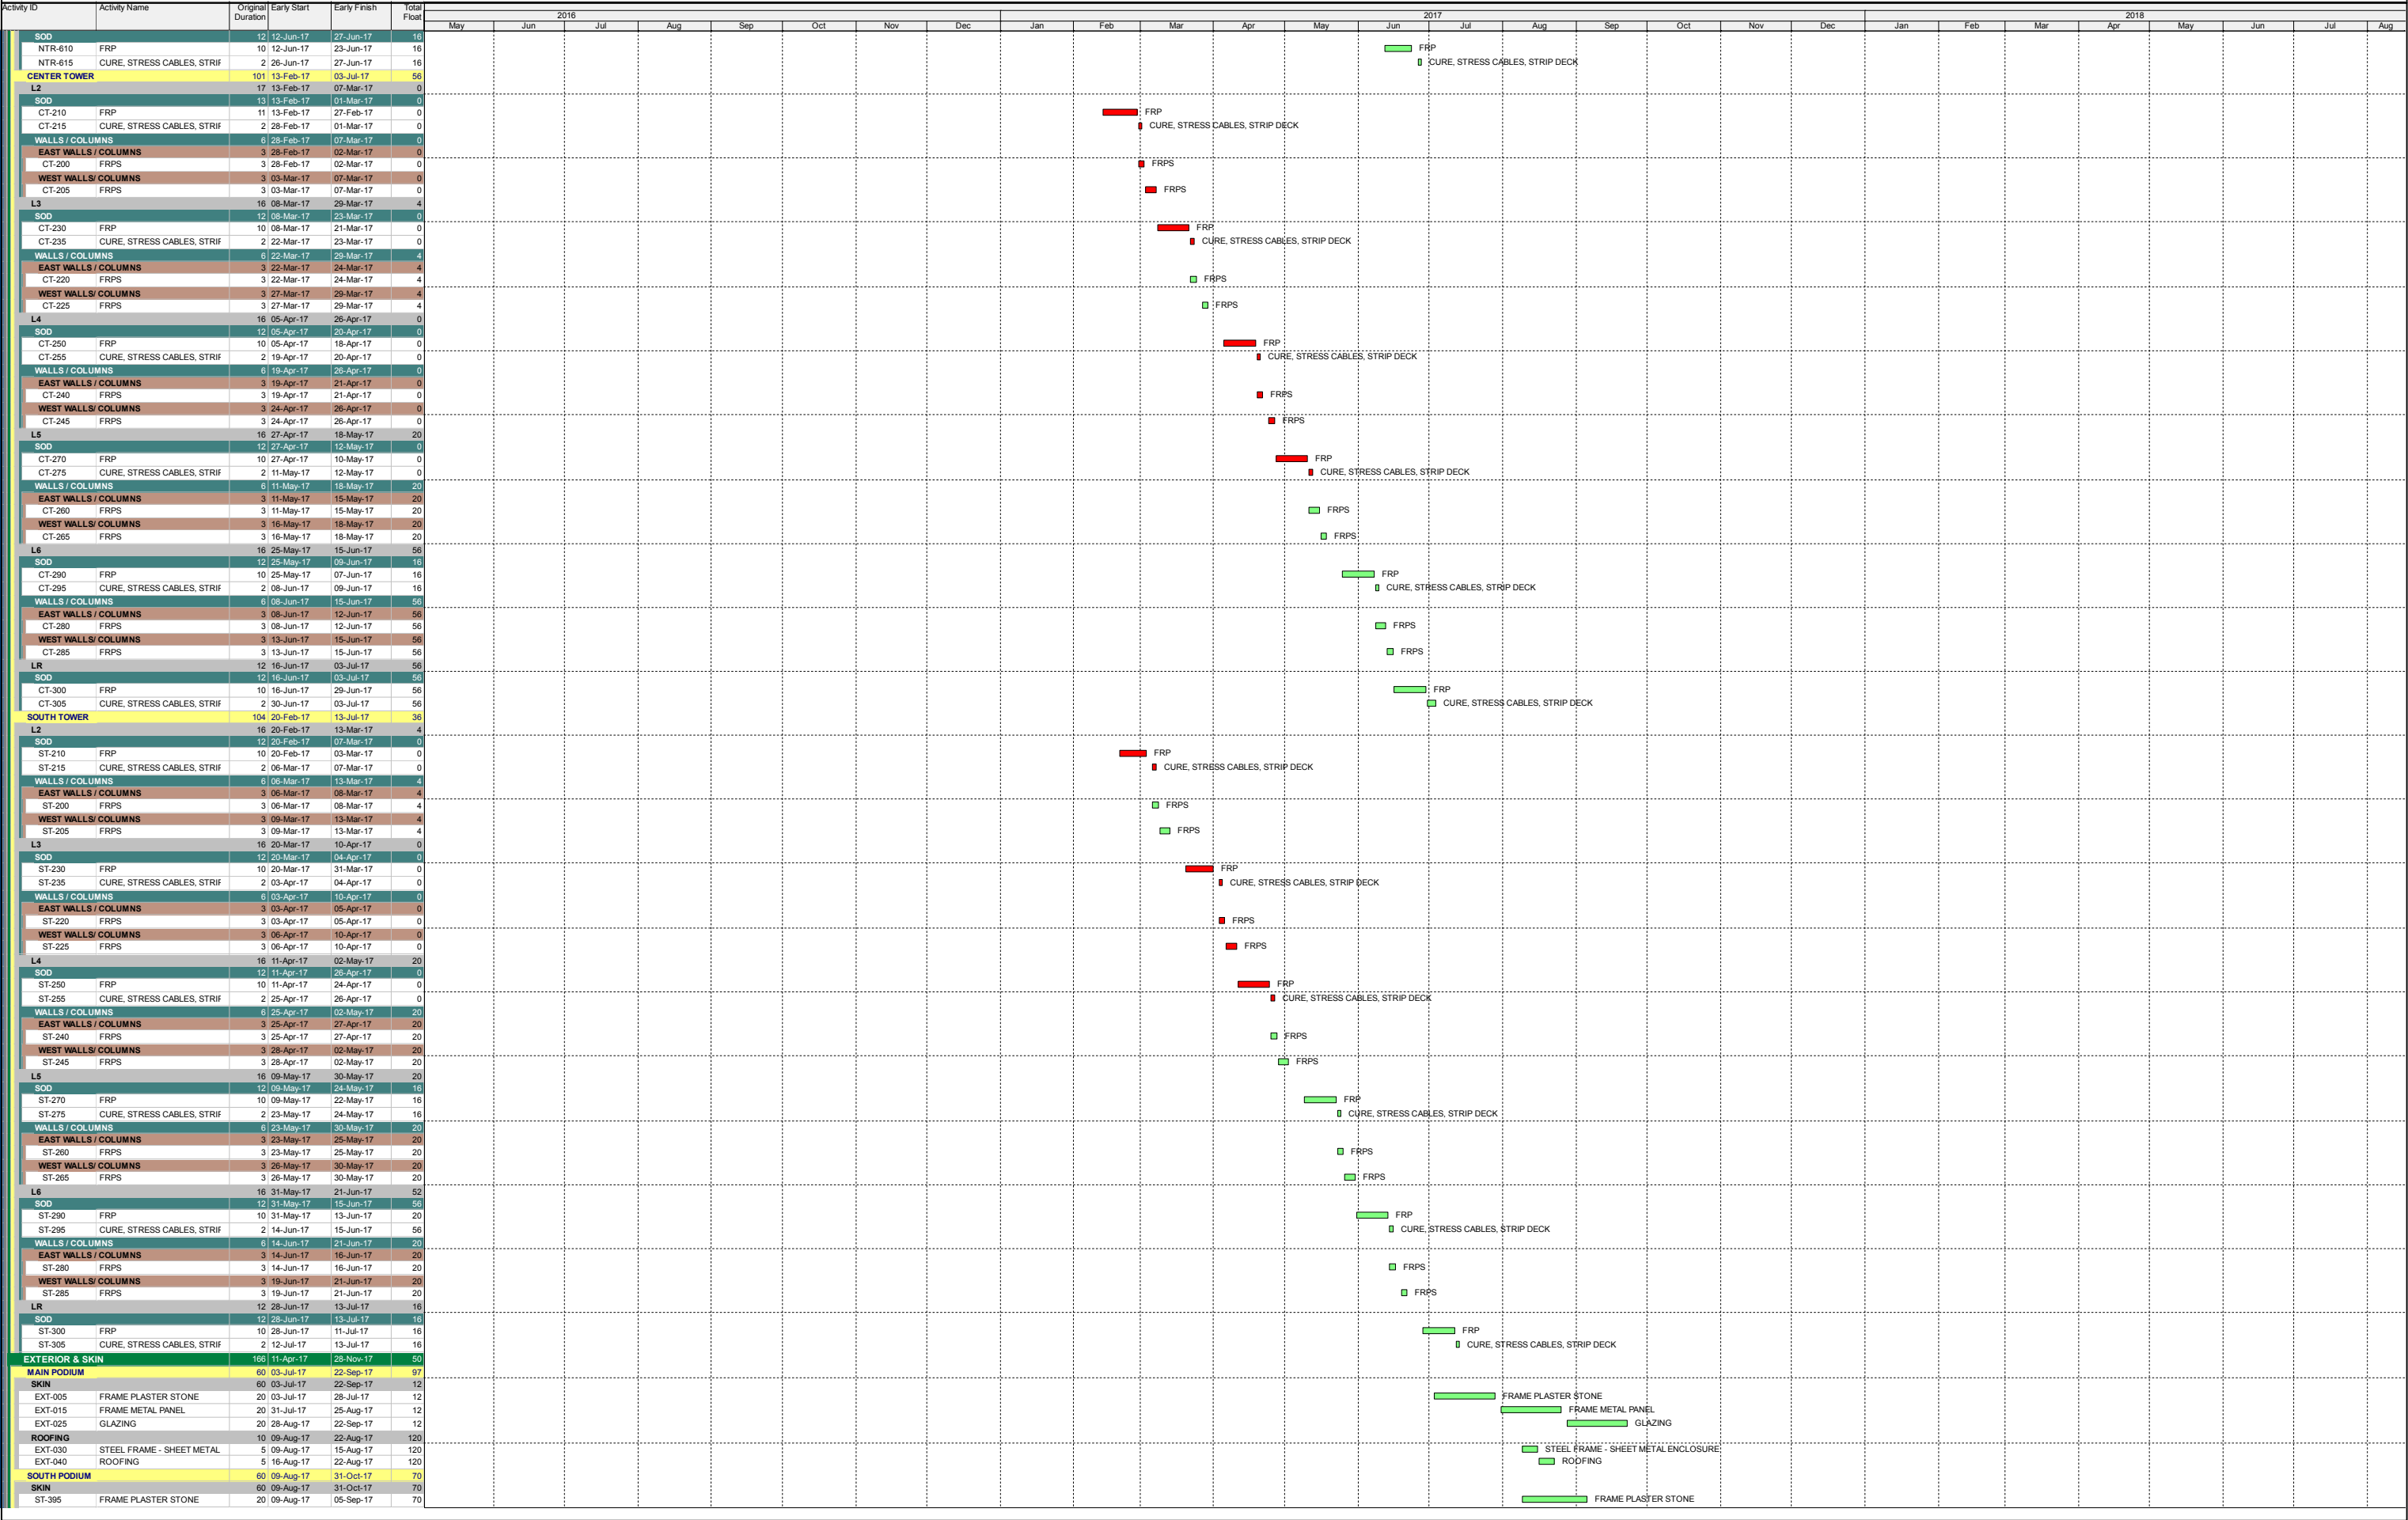

| Activity ID         | Activity Name               | Original Duration | Early Start | Early Finish | Total Float |
|---------------------|-----------------------------|-------------------|-------------|--------------|-------------|
| ST-400              | FRAME METAL PANEL           | 20                | 06-Sep-17   | 03-Oct-17    | 70          |
| ST-405              | GLAZING                     | 20                | 04-Oct-17   | 31-Oct-17    | 70          |
| NORTH TOWER         |                             |                   |             |              |             |
| SKIN                |                             | 100               | 11-Apr-17   | 15-Sep-17    | 102         |
| NSKIN-000           | WINDOW WALL                 | 20                | 11-Apr-17   | 08-May-17    | 51          |
| NSKIN-010           | FRAME - METAL PANEL         | 20                | 09-May-17   | 05-Jun-17    | 116         |
| NSKIN-020           | GFRC                        | 20                | 06-Jun-17   | 03-Jul-17    | 116         |
| NSKIN-030           | STUDY ROOM / GREAT ROOM     | 40                | 04-Jul-17   | 28-Aug-17    | 116         |
| ROOFING             |                             | 60                | 26-Jun-17   | 15-Sep-17    | 102         |
| ST-310              | STEEL FRAME - SHEET METAL   | 20                | 26-Jun-17   | 21-Jul-17    | 97          |
| ST-315              | ROOFING                     | 20                | 24-Jul-17   | 18-Aug-17    | 97          |
| ST-320              | EQUIPMENT - WINDOW WASH     | 20                | 21-Aug-17   | 15-Sep-17    | 102         |
| CENTER TOWER        |                             |                   |             |              |             |
| SKIN                |                             | 100               | 30-Jun-17   | 16-Nov-17    | 58          |
| ST-355              | WINDOW WALL                 | 20                | 30-Jun-17   | 27-Jul-17    | 58          |
| ST-360              | FRAME - METAL PANEL         | 20                | 28-Jul-17   | 24-Aug-17    | 58          |
| ST-365              | GFRC                        | 20                | 25-Aug-17   | 21-Sep-17    | 58          |
| ST-370              | STUDY ROOM / GREAT ROOM     | 40                | 22-Sep-17   | 16-Nov-17    | 58          |
| ROOFING             |                             | 60                | 30-Jun-17   | 21-Sep-17    | 98          |
| ST-325              | STEEL FRAME - SHEET METAL   | 20                | 30-Jun-17   | 27-Jul-17    | 98          |
| ST-330              | ROOFING                     | 20                | 28-Jul-17   | 24-Aug-17    | 98          |
| ST-335              | EQUIPMENT - WINDOW WASH     | 20                | 25-Aug-17   | 21-Sep-17    | 98          |
| SOUTH TOWER         |                             |                   |             |              |             |
| SKIN                |                             | 100               | 12-Jul-17   | 28-Nov-17    | 50          |
| ST-375              | WINDOW WALL                 | 20                | 12-Jul-17   | 08-Aug-17    | 18          |
| ST-380              | FRAME - METAL PANEL         | 20                | 09-Aug-17   | 05-Sep-17    | 18          |
| ST-385              | GFRC                        | 20                | 06-Sep-17   | 03-Oct-17    | 18          |
| ST-390              | STUDY ROOM / GREAT ROOM     | 40                | 04-Oct-17   | 28-Nov-17    | 18          |
| ROOFING             |                             | 60                | 12-Jul-17   | 03-Oct-17    | 90          |
| ST-340              | STEEL FRAME - SHEET METAL   | 20                | 12-Jul-17   | 08-Aug-17    | 78          |
| ST-345              | ROOFING                     | 20                | 09-Aug-17   | 05-Sep-17    | 78          |
| ST-350              | EQUIPMENT - WINDOW WASH     | 20                | 06-Sep-17   | 03-Oct-17    | 90          |
| SITE WORK           |                             |                   |             |              |             |
| SITE100             | UNDERGROUND MEP             | 40                | 17-Apr-17   | 09-Jun-17    | 132         |
| SITE105             | CURB & GUTTER               | 20                | 12-Jun-17   | 07-Jul-17    | 132         |
| SITE110             | SHADE STRUCTURE / SCREEN    | 35                | 10-Jul-17   | 25-Aug-17    | 132         |
| SITE115             | HARDSCAPE                   | 20                | 28-Aug-17   | 22-Sep-17    | 132         |
| SITE120             | IRRIGATION / LANDSCAPE / PA | 40                | 25-Sep-17   | 17-Nov-17    | 132         |
| ROUGH INS           |                             |                   |             |              |             |
| BASEMENT            |                             | 125               | 03-Apr-17   | 22-Sep-17    | 7           |
| BR-000              | BASEMENT LAYOUT             | 5                 | 03-Apr-17   | 07-Apr-17    | 7           |
| BR-010              | BASEMENT RISERS             | 5                 | 10-Apr-17   | 14-Apr-17    | 7           |
| BR-020              | BASEMENT WALL FRAME         | 5                 | 17-Apr-17   | 21-Apr-17    | 7           |
| BR-030              | BASEMENT OH SPRINKLER PIP   | 5                 | 24-Apr-17   | 28-Apr-17    | 7           |
| BR-040              | BASEMENT OH WASTE/VENT/D    | 20                | 01-May-17   | 26-May-17    | 7           |
| BR-050              | BASEMENT OH ELECTRICAL      | 20                | 29-May-17   | 23-Jun-17    | 7           |
| BR-060              | BASEMENT OH SOFFIT / CEILI  | 5                 | 26-Jun-17   | 30-Jun-17    | 7           |
| BR-070              | BASEMENT MECH / PLUMBING    | 20                | 03-Jul-17   | 28-Jul-17    | 7           |
| BR-080              | BASEMENT ELECT ROUGH IN -   | 20                | 31-Jul-17   | 25-Aug-17    | 7           |
| BR-090              | BASEMENT MEP ROUGH IN - C   | 20                | 28-Aug-17   | 22-Sep-17    | 7           |
| MAIN PODIUM         |                             |                   |             |              |             |
| PR-10               | MP LAYOUT                   | 5                 | 12-Apr-17   | 16-Apr-17    | 25          |
| PR-100              | MP MEP ROUGH IN - CEILINGS  | 20                | 19-Apr-17   | 16-May-17    | 25          |
| PR-20               | MP RISERS                   | 20                | 17-May-17   | 13-Jun-17    | 25          |
| PR-30               | MP WALL FRAME               | 5                 | 14-Jun-17   | 20-Jun-17    | 25          |
| PR-40               | MP OH SPRINKLER PIPE        | 5                 | 21-Jun-17   | 27-Jun-17    | 25          |
| PR-50               | MP OH WASTE/VENT/DUCT       | 20                | 28-Jun-17   | 25-Jul-17    | 25          |
| PR-60               | MP OH ELECTRICAL            | 10                | 26-Jul-17   | 08-Aug-17    | 25          |
| PR-70               | MP OH SOFFIT / CEILING FRA  | 5                 | 09-Aug-17   | 15-Aug-17    | 25          |
| PR-80               | MP MECH / PLUMBING ROUGH    | 5                 | 16-Aug-17   | 22-Aug-17    | 25          |
| PR-90               | MP ELECT ROUGH IN - WALL    | 10                | 23-Aug-17   | 05-Sep-17    | 25          |
| SOUTH PODIUM        |                             |                   |             |              |             |
| SPR-10              | SP LAYOUT                   | 5                 | 25-Apr-17   | 14-Aug-17    | 101         |
| SPR-100             | SP MEP ROUGH IN - CEILINGS  | 20                | 02-May-17   | 29-May-17    | 101         |
| SPR-20              | SP RISERS                   | 5                 | 30-May-17   | 05-Jun-17    | 101         |
| SPR-30              | SP WALL FRAME               | 5                 | 06-Jun-17   | 12-Jun-17    | 101         |
| SPR-40              | SP OH SPRINKLER PIPE        | 5                 | 13-Jun-17   | 19-Jun-17    | 101         |
| SPR-50              | SP OH WASTE/VENT/DUCT       | 20                | 20-Jun-17   | 17-Jul-17    | 101         |
| SPR-60              | SP OH ELECTRICAL            | 5                 | 18-Jul-17   | 24-Jul-17    | 101         |
| SPR-70              | SP OH SOFFIT / CEILING FRA  | 5                 | 25-Jul-17   | 31-Jul-17    | 101         |
| SPR-80              | SP MECH / PLUMBING ROUGH    | 5                 | 01-Aug-17   | 07-Aug-17    | 101         |
| SPR-90              | SP ELECT ROUGH IN - WALL    | 5                 | 08-Aug-17   | 14-Aug-17    | 101         |
| NORTH TOWER         |                             |                   |             |              |             |
| NTR-000             | SIPS                        | 100               | 29-May-17   | 13-Oct-17    | 0           |
| CENTER TOWER        |                             |                   |             |              |             |
| CTR-000             | SIPS                        | 100               | 04-Jul-17   | 20-Nov-17    | 56          |
| SOUTH TOWER         |                             |                   |             |              |             |
| STR-000             | SIPS                        | 100               | 07-Aug-17   | 22-Dec-17    | 0           |
| ELEVATOR            |                             |                   |             |              |             |
| NORTH TOWER         |                             | 90                | 21-Aug-17   | 22-Dec-17    | 97          |
| ELEV-000            | INSTALL ELEVATORS           | 90                | 21-Aug-17   | 22-Dec-17    | 97          |
| CENTER TOWER        |                             | 90                | 18-Sep-17   | 19-Jan-18    | 97          |
| ELEV-010            | INSTALL ELEVATORS           | 90                | 18-Sep-17   | 19-Jan-18    | 97          |
| SOUTH TOWER         |                             | 90                | 16-Oct-17   | 16-Feb-18    | 97          |
| ELEV-015            | INSTALL ELEVATORS           | 90                | 16-Oct-17   | 16-Feb-18    | 97          |
| SERVICE ELEVATOR    |                             | 40                | 13-Nov-17   | 05-Jan-18    | 127         |
| ELEV-020            | INSTALL ELEVATORS           | 40                | 13-Nov-17   | 05-Jan-18    | 127         |
| FINISHES            |                             |                   |             |              |             |
| BASEMENT            |                             | 50                | 25-Sep-17   | 01-Dec-17    | 82          |
| BF-005              | BASEMENT HANG GYP WALLS     | 5                 | 25-Sep-17   | 29-Sep-17    | 7           |
| BF-010              | BASEMENT TAPE AND FINISH I  | 5                 | 02-Oct-17   | 06-Oct-17    | 82          |
| BF-20               | BASEMENT TAPE AND FINISH F  | 5                 | 09-Oct-17   | 13-Oct-17    | 82          |
| BF-30               | BASEMENT CERAMIC TILE       | 5                 | 16-Oct-17   | 20-Oct-17    | 82          |
| BF-40               | BASEMENT PRIME AND PAINT    | 5                 | 23-Oct-17   | 27-Oct-17    | 82          |
| BF-50               | BASEMENT CASEWORK/MILLW     | 5                 | 30-Oct-17   | 03-Nov-17    | 82          |
| BF-60               | BASEMENT T-GRID             | 5                 | 06-Nov-17   | 10-Nov-17    | 82          |
| BF-70               | BASEMENT MEP TRIM/FINISH    | 5                 | 13-Nov-17   | 17-Nov-17    | 82          |
| BF-80               | BASEMENT FLOORING           | 5                 | 20-Nov-17   | 24-Nov-17    | 82          |
| BF-90               | BASEMENT DOORS HARDWAR      | 5                 | 27-Nov-17   | 01-Dec-17    | 82          |
| MAIN PODIUM/KITCHEN |                             |                   |             |              |             |
| PF-10               | MP HANG GYP WALLS/CEILING   | 10                | 02-Oct-17   | 13-Oct-17    | 7           |
| PF-15               | MP TAPE AND FINISH INITIAL  | 10                | 16-Oct-17   | 27-Oct-17    | 7           |
| PF-20               | MP TAPE AND FINISH FINAL    | 10                | 30-Oct-17   | 10-Nov-17    | 7           |
| PF-25               | MP CERAMIC TILE             | 10                | 30-Oct-17   | 10-Nov-17    | 87          |
| PF-30               | MP PRIME AND PAINT          | 10                | 13-Nov-17   | 24-Nov-17    | 87          |
| PF-21               | MP KITCHEN EQUIP LAYOUT     | 10                | 13-Nov-17   | 24-Nov-17    | 7           |
| PF-35               | MP CASEWORK/MILLWORK        | 10                | 27-Nov-17   | 08-Dec-17    | 87          |
| PF-40               | MP T-GRID                   | 10                | 27-Nov-17   | 08-Dec-17    | 87          |
| PF-45               | MP MEP TRIM/FINISH          | 10                | 27-Nov-17   | 08-Dec-17    | 87          |
| PF-50               | MP FLOORING                 | 10                | 27-Nov-17   | 08-Dec-17    | 87          |
| PF-22               | MP KITCHEN HOODS            | 10                | 27-Nov-17   | 08-Dec-17    | 7           |

| Activity ID         | Activity Name              | Original Duration | Early Start | Early Finish | Total Float | 2016 |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     | 2017 |     |     |     |  |  |  |  |  |  |  |  | 2018 |  |  |  |  |  |  |  |  |  |  |  |
|---------------------|----------------------------|-------------------|-------------|--------------|-------------|------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|------|-----|-----|-----|--|--|--|--|--|--|--|--|------|--|--|--|--|--|--|--|--|--|--|--|
|                     |                            |                   |             |              |             | May  | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May  | Jun | Jul | Aug |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| PF-23               | MP KITCHEN BUILT IN FRIDGE | 15                | 11-Dec-17   | 29-Dec-17    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| PF-24               | MP KITCHEN STAINLESS COUP  | 15                | 01-Jan-18   | 19-Jan-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| PF-26               | MP KITCHEN EQUIP INSTALL   | 20                | 22-Jan-18   | 16-Feb-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| PF-27               | MP KITCHEN PLATFORMS       | 20                | 19-Feb-18   | 16-Mar-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| PF-55               | MP DOORS HARDWARE          | 10                | 19-Mar-18   | 30-Mar-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SOUTH PODIUM        |                            | 130               | 16-Oct-17   | 13-Apr-18    | 12          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-10               | MP HANG GYP WALLS/CEILING  | 10                | 16-Oct-17   | 27-Oct-17    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-15               | MP TAPE AND FINISH INITIAL | 10                | 30-Oct-17   | 10-Nov-17    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-20               | MP TAPE AND FINISH FINAL   | 10                | 13-Nov-17   | 24-Nov-17    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-25               | MP CERAMIC TILE            | 10                | 27-Nov-17   | 08-Dec-17    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-30               | MP PRIME AND PAINT         | 10                | 11-Dec-17   | 22-Dec-17    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-35               | MP CASEWORK/MILLWORK       | 15                | 25-Dec-17   | 12-Jan-18    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-50               | MP FLOORING                | 20                | 01-Jan-18   | 26-Jan-18    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-45               | MP MEP TRIM/FINISH         | 15                | 08-Jan-18   | 26-Jan-18    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-40               | MP T-GRID                  | 10                | 15-Jan-18   | 26-Jan-18    | 57          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SF-55               | MP DOORS HARDWARE          | 10                | 02-Apr-18   | 13-Apr-18    | 12          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| NORTH TOWER         |                            | 50                | 17-Nov-17   | 25-Jan-18    | 58          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| NTF-000             | SIPS                       | 50                | 17-Nov-17   | 25-Jan-18    | 58          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| CENTER TOWER        |                            | 50                | 21-Nov-17   | 29-Jan-18    | 56          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| CTF-000             | SIPS                       | 50                | 21-Nov-17   | 29-Jan-18    | 56          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SOUTH TOWER         |                            | 50                | 25-Dec-17   | 02-Mar-18    | 0           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| STF-000             | SIPS                       | 50                | 25-Dec-17   | 02-Mar-18    | 0           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| PUNCHLIST           |                            | 115               | 04-Dec-17   | 11-May-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| BASEMENT            |                            | 20                | 04-Dec-17   | 29-Dec-17    | 102         |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| BP-005              | OWNER ARCH PUNCHLIST       | 20                | 04-Dec-17   | 29-Dec-17    | 102         |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| MAIN PODIUM/KITCHEN |                            | 30                | 02-Apr-18   | 11-May-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| MPP-5               | OWNER ARCH PUNCHLIST       | 30                | 02-Apr-18   | 11-May-18    | 7           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SOUTH PODIUM        |                            | 15                | 16-Apr-18   | 04-May-18    | 12          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SPP-5               | OWNER ARCH PUNCHLIST       | 15                | 16-Apr-18   | 04-May-18    | 12          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| NORTH TOWER         |                            | 25                | 26-Jan-18   | 01-Mar-18    | 58          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| NTP-000             | SIPS                       | 25                | 26-Jan-18   | 01-Mar-18    | 58          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| CENTER TOWER        |                            | 25                | 30-Jan-18   | 05-Mar-18    | 56          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| CTP-000             | SIPS                       | 25                | 30-Jan-18   | 05-Mar-18    | 56          |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |
| SOUTH TOWER         |                            | 25                | 05-Mar-18   | 06-Apr-18    | 0           |      |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |  |  |  |  |  |  |  |  |      |  |  |  |  |  |  |  |  |  |  |  |

| Activity ID                          | Activity Name | Original Duration | Early Start | Early Finish | Total Float |
|--------------------------------------|---------------|-------------------|-------------|--------------|-------------|
| <b>RENO MCEP</b>                     |               | 587               | 02-May-16   | 01-Aug-18    | 0           |
| <b>MILESTONES</b>                    |               | 587               | 02-May-16   | 01-Aug-18    | 0           |
| <b>DESIGN</b>                        |               | 260               | 02-May-16   | 28-Apr-17    | 187         |
| DESIGN PACKAGE 1                     |               | 34                | 02-May-16   | 16-Jun-16    | 0           |
| DESIGN PACKAGE 2                     |               | 65                | 02-May-16   | 29-Jul-16    | 7           |
| DESIGN PACKAGE 3                     |               | 100               | 01-Aug-16   | 16-Dec-16    | 12          |
| DESIGN PACKAGE 4                     |               | 115               | 01-Aug-16   | 06-Jan-17    | 7           |
| DESIGN PACKAGE 5                     |               | 80                | 09-Jan-17   | 28-Apr-17    | 187         |
| <b>CONSTRUCTION</b>                  |               | 523               | 17-Jun-16   | 19-Jun-18    | 30          |
| PROCUREMENT                          |               | 245               | 01-Aug-16   | 07-Jul-17    | 187         |
| DEMOLITION / EXCAVATION              |               | 85                | 17-Jun-16   | 13-Oct-16    | 0           |
| SITE UTILITIES                       |               | 100               | 23-Sep-16   | 09-Feb-17    | 178         |
| STRUCTURE                            |               | 200               | 07-Oct-16   | 13-Jul-17    | 48          |
| <b>BASEMENT</b>                      |               | 60                | 07-Oct-16   | 29-Dec-16    | 12          |
| FOUNDATIONS                          |               | 46                | 07-Oct-16   | 09-Dec-16    | 18          |
| FOUNDATION PLACEMENT #1              |               | 12                | 07-Oct-16   | 24-Oct-16    | 0           |
| FOUNDATION PLACEMENT #2              |               | 12                | 25-Oct-16   | 09-Nov-16    | 0           |
| FOUNDATION PLACEMENT #3              |               | 12                | 10-Nov-16   | 25-Nov-16    | 28          |
| FOUNDATION PLACEMENT #4              |               | 12                | 17-Nov-16   | 02-Dec-16    | 10          |
| FOUNDATION PLACEMENT #5              |               | 12                | 24-Nov-16   | 09-Dec-16    | 13          |
| WALLS/COLUMNS                        |               | 45                | 25-Oct-16   | 26-Dec-16    | 15          |
| WALL PLACEMENT #1                    |               | 8                 | 25-Oct-16   | 03-Nov-16    | 6           |
| WALL PLACEMENT #2                    |               | 8                 | 04-Nov-16   | 15-Nov-16    | 6           |
| WALL PLACEMENT #3                    |               | 8                 | 16-Nov-16   | 25-Nov-16    | 6           |
| WALL PLACEMENT #4                    |               | 8                 | 28-Nov-16   | 07-Dec-16    | 28          |
| WALL PLACEMENT #5                    |               | 8                 | 28-Oct-16   | 08-Nov-16    | 20          |
| WALL PLACEMENT #6                    |               | 8                 | 09-Nov-16   | 18-Nov-16    | 20          |
| WALL PLACEMENT #7                    |               | 8                 | 05-Dec-16   | 14-Dec-16    | 10          |
| WALL PLACEMENT #8                    |               | 8                 | 15-Dec-16   | 26-Dec-16    | 10          |
| SOG                                  |               | 24                | 28-Nov-16   | 29-Dec-16    | 6           |
| SOG #1                               |               | 14                | 28-Nov-16   | 15-Dec-16    | 16          |
| SOG #2                               |               | 17                | 07-Dec-16   | 29-Dec-16    | 6           |
| <b>MAIN PODIUM</b>                   |               | 94                | 01-Dec-16   | 11-Apr-17    | 25          |
| NORTH TOWER                          |               | 45                | 01-Dec-16   | 01-Feb-17    | 0           |
| FOUNDATIONS                          |               | 12                | 01-Dec-16   | 16-Dec-16    | 0           |
| FOUNDATION PLACEMENT #1              |               | 12                | 01-Dec-16   | 16-Dec-16    | 0           |
| WALLS/COLUMNS                        |               | 24                | 19-Dec-16   | 19-Jan-17    | 0           |
| WALL PLACEMENT #1 (EAST SHEAR WALLS/ |               | 8                 | 19-Dec-16   | 28-Dec-16    | 0           |
| WALL PLACEMENT #2 (COLUMNS)          |               | 8                 | 29-Dec-16   | 09-Jan-17    | 0           |
| WALL PLACEMENT #3 (WEST SHEAR WALLS) |               | 8                 | 10-Jan-17   | 19-Jan-17    | 0           |
| SOG                                  |               | 17                | 10-Jan-17   | 01-Feb-17    | 0           |
| SOG #1                               |               | 17                | 10-Jan-17   | 01-Feb-17    | 0           |
| SOD                                  |               | 18                | 30-Dec-16   | 24-Jan-17    | 6           |
| SOD #1                               |               | 14                | 30-Dec-16   | 18-Jan-17    | 6           |
| SOD #2 FOOD PREP ROOF                |               | 18                | 30-Dec-16   | 24-Jan-17    | 6           |
| CENTER TOWER                         |               | 89                | 08-Dec-16   | 11-Apr-17    | 25          |
| FOUNDATIONS                          |               | 24                | 08-Dec-16   | 10-Jan-17    | 48          |
| FOUNDATION PLACEMENT #2              |               | 12                | 08-Dec-16   | 23-Dec-16    | 19          |
| FOUNDATION PLACEMENT #6              |               | 12                | 26-Dec-16   | 10-Jan-17    | 48          |
| WALLS/COLUMNS                        |               | 24                | 20-Jan-17   | 22-Feb-17    | 25          |

Start Date:  
02-May-16Finish Date:  
01-Aug-18Data Date:  
01-May-16

15-Jan-16

TASK filter: All Activities

RENO MCEP  
ANSWER SCHEDULE



| Activity ID | Activity Name                           | Original Duration | Early Start      | Early Finish     | Total Float |
|-------------|-----------------------------------------|-------------------|------------------|------------------|-------------|
|             | WALL PLACEMENT #1 (EAST SHEAR WALLS/    | 8                 | 20-Jan-17        | 31-Jan-17        | 0           |
|             | WALL PLACEMENT #2 (COLUMNS)             | 8                 | 01-Feb-17        | 10-Feb-17        | 0           |
|             | WALL PLACEMENT #3 (WEST SHEAR WALLS)    | 8                 | 13-Feb-17        | 22-Feb-17        | 25          |
|             | SOG                                     | 56                | 24-Jan-17        | 11-Apr-17        | 25          |
|             | SOG #2                                  | 17                | 24-Jan-17        | 15-Feb-17        | 62          |
|             | SOG #4                                  | 46                | 07-Feb-17        | 11-Apr-17        | 25          |
|             | SOD                                     | 19                | 30-Dec-16        | 25-Jan-17        | 12          |
|             | SOD #1                                  | 19                | 30-Dec-16        | 25-Jan-17        | 12          |
|             | <b>SOUTH PODIUM</b>                     | <b>93</b>         | <b>15-Dec-16</b> | <b>24-Apr-17</b> | <b>101</b>  |
|             | FOUNDATIONS                             | 48                | 15-Dec-16        | 20-Feb-17        | 138         |
|             | FOUNDATION PLACEMENT #3 (EAST MAT)      | 12                | 15-Dec-16        | 30-Dec-16        | 59          |
|             | FOUNDATION PLACEMENT #4 (CENTER SPOT    | 12                | 02-Jan-17        | 17-Jan-17        | 59          |
|             | FOUNDATION PLACEMENT #5 (WEST MAT)      | 12                | 18-Jan-17        | 02-Feb-17        | 138         |
|             | FOUNDATION PLACEMENT #7 (PAVILION)      | 12                | 03-Feb-17        | 20-Feb-17        | 138         |
|             | WALLS/COLUMNS                           | 26                | 21-Feb-17        | 28-Mar-17        | 120         |
|             | WALL PLACEMENT #1 (EAST SHEAR WALL & I  | 8                 | 23-Feb-17        | 06-Mar-17        | 25          |
|             | WALL PLACEMENT #2 (COLUMNS)             | 8                 | 07-Mar-17        | 16-Mar-17        | 25          |
|             | WALL PLACEMENT #3 (WEST SHEAR WALLS & I | 8                 | 17-Mar-17        | 28-Mar-17        | 103         |
|             | WALL PLACEMENT #4 (PAVILION BLDG)       | 8                 | 21-Feb-17        | 02-Mar-17        | 138         |
|             | SOG                                     | 27                | 17-Mar-17        | 24-Apr-17        | 101         |
|             | SOG #3                                  | 17                | 17-Mar-17        | 10-Apr-17        | 25          |
|             | SOG #5                                  | 17                | 31-Mar-17        | 24-Apr-17        | 101         |
|             | <b>NORTH TOWER</b>                      | <b>104</b>        | <b>02-Feb-17</b> | <b>27-Jun-17</b> | <b>16</b>   |
|             | L2                                      | 16                | 02-Feb-17        | 23-Feb-17        | 4           |
|             | SOD                                     | 12                | 02-Feb-17        | 17-Feb-17        | 0           |
|             | WALLS / COLUMNS                         | 6                 | 16-Feb-17        | 23-Feb-17        | 4           |
|             | EAST WALLS / COLUMNS                    | 3                 | 16-Feb-17        | 20-Feb-17        | 4           |
|             | WEST WALLS/ COLUMNS                     | 3                 | 21-Feb-17        | 23-Feb-17        | 4           |
|             | L3                                      | 16                | 02-Mar-17        | 23-Mar-17        | 0           |
|             | SOD                                     | 12                | 02-Mar-17        | 17-Mar-17        | 0           |
|             | WALLS / COLUMNS                         | 6                 | 16-Mar-17        | 23-Mar-17        | 0           |
|             | EAST WALLS / COLUMNS                    | 3                 | 16-Mar-17        | 20-Mar-17        | 0           |
|             | WEST WALLS/ COLUMNS                     | 3                 | 21-Mar-17        | 23-Mar-17        | 0           |
|             | L4                                      | 16                | 24-Mar-17        | 14-Apr-17        | 4           |
|             | SOD                                     | 12                | 24-Mar-17        | 10-Apr-17        | 0           |
|             | WALLS / COLUMNS                         | 6                 | 07-Apr-17        | 14-Apr-17        | 4           |
|             | EAST WALLS / COLUMNS                    | 3                 | 07-Apr-17        | 11-Apr-17        | 4           |
|             | WEST WALLS/ COLUMNS                     | 3                 | 12-Apr-17        | 14-Apr-17        | 4           |
|             | L5                                      | 16                | 21-Apr-17        | 12-May-17        | 12          |
|             | SOD                                     | 12                | 21-Apr-17        | 08-May-17        | 16          |
|             | WALLS / COLUMNS                         | 6                 | 05-May-17        | 12-May-17        | 0           |
|             | EAST WALLS / COLUMNS                    | 3                 | 05-May-17        | 09-May-17        | 0           |
|             | WEST WALLS/ COLUMNS                     | 3                 | 10-May-17        | 12-May-17        | 0           |
|             | L6                                      | 16                | 15-May-17        | 05-Jun-17        | 20          |
|             | SOD                                     | 12                | 15-May-17        | 30-May-17        | 0           |
|             | WALLS / COLUMNS                         | 6                 | 29-May-17        | 05-Jun-17        | 20          |
|             | EAST WALLS / COLUMNS                    | 3                 | 29-May-17        | 31-May-17        | 20          |
|             | WEST WALLS/ COLUMNS                     | 3                 | 01-Jun-17        | 05-Jun-17        | 20          |
|             | LR                                      | 12                | 12-Jun-17        | 27-Jun-17        | 16          |
|             | SOD                                     | 12                | 12-Jun-17        | 27-Jun-17        | 16          |
|             | <b>CENTER TOWER</b>                     | <b>101</b>        | <b>13-Feb-17</b> | <b>03-Jul-17</b> | <b>56</b>   |
|             | L2                                      | 17                | 13-Feb-17        | 07-Mar-17        | 0           |
|             | SOD                                     | 13                | 13-Feb-17        | 01-Mar-17        | 0           |
|             | WALLS / COLUMNS                         | 6                 | 28-Feb-17        | 07-Mar-17        | 0           |
|             | EAST WALLS / COLUMNS                    | 3                 | 28-Feb-17        | 02-Mar-17        | 0           |
|             | WEST WALLS/ COLUMNS                     | 3                 | 03-Mar-17        | 07-Mar-17        | 0           |
|             | L3                                      | 16                | 08-Mar-17        | 29-Mar-17        | 4           |
|             | SOD                                     | 12                | 08-Mar-17        | 23-Mar-17        | 0           |
|             | WALLS / COLUMNS                         | 6                 | 22-Mar-17        | 29-Mar-17        | 4           |
|             | EAST WALLS / COLUMNS                    | 3                 | 22-Mar-17        | 24-Mar-17        | 4           |

| Activity ID | Activity Name               | Original Duration | Early Start | Early Finish | Total Float |
|-------------|-----------------------------|-------------------|-------------|--------------|-------------|
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 27-Mar-17   | 29-Mar-17    | 4           |
| L4          |                             | 16                | 05-Apr-17   | 26-Apr-17    | 0           |
|             | <b>SOD</b>                  | 12                | 05-Apr-17   | 20-Apr-17    | 0           |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 19-Apr-17   | 26-Apr-17    | 0           |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 19-Apr-17   | 21-Apr-17    | 0           |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 24-Apr-17   | 26-Apr-17    | 0           |
| L5          |                             | 16                | 27-Apr-17   | 18-May-17    | 20          |
|             | <b>SOD</b>                  | 12                | 27-Apr-17   | 12-May-17    | 0           |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 11-May-17   | 18-May-17    | 20          |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 11-May-17   | 15-May-17    | 20          |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 16-May-17   | 18-May-17    | 20          |
| L6          |                             | 16                | 25-May-17   | 15-Jun-17    | 56          |
|             | <b>SOD</b>                  | 12                | 25-May-17   | 09-Jun-17    | 16          |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 08-Jun-17   | 15-Jun-17    | 56          |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 08-Jun-17   | 12-Jun-17    | 56          |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 13-Jun-17   | 15-Jun-17    | 56          |
| LR          |                             | 12                | 16-Jun-17   | 03-Jul-17    | 56          |
|             | <b>SOD</b>                  | 12                | 16-Jun-17   | 03-Jul-17    | 56          |
|             | <b>SOUTH TOWER</b>          | 104               | 20-Feb-17   | 13-Jul-17    | 36          |
| L2          |                             | 16                | 20-Feb-17   | 13-Mar-17    | 4           |
|             | <b>SOD</b>                  | 12                | 20-Feb-17   | 07-Mar-17    | 0           |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 06-Mar-17   | 13-Mar-17    | 4           |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 06-Mar-17   | 08-Mar-17    | 4           |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 09-Mar-17   | 13-Mar-17    | 4           |
| L3          |                             | 16                | 20-Mar-17   | 10-Apr-17    | 0           |
|             | <b>SOD</b>                  | 12                | 20-Mar-17   | 04-Apr-17    | 0           |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 03-Apr-17   | 10-Apr-17    | 0           |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 03-Apr-17   | 05-Apr-17    | 0           |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 06-Apr-17   | 10-Apr-17    | 0           |
| L4          |                             | 16                | 11-Apr-17   | 02-May-17    | 20          |
|             | <b>SOD</b>                  | 12                | 11-Apr-17   | 26-Apr-17    | 0           |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 25-Apr-17   | 02-May-17    | 20          |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 25-Apr-17   | 27-Apr-17    | 20          |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 28-Apr-17   | 02-May-17    | 20          |
| L5          |                             | 16                | 09-May-17   | 30-May-17    | 20          |
|             | <b>SOD</b>                  | 12                | 09-May-17   | 24-May-17    | 16          |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 23-May-17   | 30-May-17    | 20          |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 23-May-17   | 25-May-17    | 20          |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 26-May-17   | 30-May-17    | 20          |
| L6          |                             | 16                | 31-May-17   | 21-Jun-17    | 52          |
|             | <b>SOD</b>                  | 12                | 31-May-17   | 15-Jun-17    | 56          |
|             | <b>WALLS / COLUMNS</b>      | 6                 | 14-Jun-17   | 21-Jun-17    | 20          |
|             | <b>EAST WALLS / COLUMNS</b> | 3                 | 14-Jun-17   | 16-Jun-17    | 20          |
|             | <b>WEST WALLS/ COLUMNS</b>  | 3                 | 19-Jun-17   | 21-Jun-17    | 20          |
| LR          |                             | 12                | 28-Jun-17   | 13-Jul-17    | 16          |
|             | <b>SOD</b>                  | 12                | 28-Jun-17   | 13-Jul-17    | 16          |
|             | <b>EXTERIOR &amp; SKIN</b>  | 166               | 11-Apr-17   | 28-Nov-17    | 50          |
|             | <b>MAIN PODIUM</b>          | 60                | 03-Jul-17   | 22-Sep-17    | 97          |
|             | <b>SKIN</b>                 | 60                | 03-Jul-17   | 22-Sep-17    | 12          |
|             | <b>ROOFING</b>              | 10                | 09-Aug-17   | 22-Aug-17    | 120         |
|             | <b>SOUTH PODIUM</b>         | 60                | 09-Aug-17   | 31-Oct-17    | 70          |
|             | <b>SKIN</b>                 | 60                | 09-Aug-17   | 31-Oct-17    | 70          |
|             | <b>NORTH TOWER</b>          | 114               | 11-Apr-17   | 15-Sep-17    | 102         |
|             | <b>SKIN</b>                 | 100               | 11-Apr-17   | 28-Aug-17    | 116         |
|             | <b>ROOFING</b>              | 60                | 26-Jun-17   | 15-Sep-17    | 102         |
|             | <b>CENTER TOWER</b>         | 100               | 30-Jun-17   | 16-Nov-17    | 58          |
|             | <b>SKIN</b>                 | 100               | 30-Jun-17   | 16-Nov-17    | 58          |
|             | <b>ROOFING</b>              | 60                | 30-Jun-17   | 21-Sep-17    | 98          |
|             | <b>SOUTH TOWER</b>          | 100               | 12-Jul-17   | 28-Nov-17    | 50          |

| Activity ID | Activity Name              | Original Duration | Early Start | Early Finish | Total Float |
|-------------|----------------------------|-------------------|-------------|--------------|-------------|
|             | <b>SKIN</b>                | 100               | 12-Jul-17   | 28-Nov-17    | 18          |
|             | <b>ROOFING</b>             | 60                | 12-Jul-17   | 03-Oct-17    | 90          |
|             | <b>SITE WORK</b>           | 155               | 17-Apr-17   | 17-Nov-17    | 132         |
|             | <b>ROUGH INS</b>           | 190               | 03-Apr-17   | 22-Dec-17    | 32          |
|             | <b>BASEMENT</b>            | 125               | 03-Apr-17   | 22-Sep-17    | 7           |
|             | <b>MAIN PODIUM</b>         | 105               | 12-Apr-17   | 05-Sep-17    | 25          |
|             | <b>SOUTH PODIUM</b>        | 80                | 25-Apr-17   | 14-Aug-17    | 101         |
|             | <b>NORTH TOWER</b>         | 100               | 29-May-17   | 13-Oct-17    | 0           |
|             | <b>CENTER TOWER</b>        | 100               | 04-Jul-17   | 20-Nov-17    | 56          |
|             | <b>SOUTH TOWER</b>         | 100               | 07-Aug-17   | 22-Dec-17    | 0           |
|             | <b>ELEVATOR</b>            | 130               | 21-Aug-17   | 16-Feb-18    | 97          |
|             | <b>NORTH TOWER</b>         | 90                | 21-Aug-17   | 22-Dec-17    | 97          |
|             | <b>CENTER TOWER</b>        | 90                | 18-Sep-17   | 19-Jan-18    | 97          |
|             | <b>SOUTH TOWER</b>         | 90                | 16-Oct-17   | 16-Feb-18    | 97          |
|             | <b>SERVICE ELEVATOR</b>    | 40                | 13-Nov-17   | 05-Jan-18    | 127         |
|             | <b>FINISHES</b>            | 145               | 25-Sep-17   | 13-Apr-18    | 12          |
|             | <b>BASEMENT</b>            | 50                | 25-Sep-17   | 01-Dec-17    | 82          |
|             | <b>MAIN PODIUM/KITCHEN</b> | 130               | 02-Oct-17   | 30-Mar-18    | 7           |
|             | <b>SOUTH PODIUM</b>        | 130               | 16-Oct-17   | 13-Apr-18    | 12          |
|             | <b>NORTH TOWER</b>         | 50                | 17-Nov-17   | 25-Jan-18    | 58          |
|             | <b>CENTER TOWER</b>        | 50                | 21-Nov-17   | 29-Jan-18    | 56          |
|             | <b>SOUTH TOWER</b>         | 50                | 25-Dec-17   | 02-Mar-18    | 0           |
|             | <b>PUNCHLIST</b>           | 115               | 04-Dec-17   | 11-May-18    | 7           |
|             | <b>BASEMENT</b>            | 20                | 04-Dec-17   | 29-Dec-17    | 102         |
|             | <b>MAIN PODIUM/KITCHEN</b> | 30                | 02-Apr-18   | 11-May-18    | 7           |
|             | <b>SOUTH PODIUM</b>        | 15                | 16-Apr-18   | 04-May-18    | 12          |
|             | <b>NORTH TOWER</b>         | 25                | 26-Jan-18   | 01-Mar-18    | 58          |
|             | <b>CENTER TOWER</b>        | 25                | 30-Jan-18   | 05-Mar-18    | 56          |
|             | <b>SOUTH TOWER</b>         | 25                | 05-Mar-18   | 06-Apr-18    | 0           |
|             | <b>COMMISSIONING</b>       | 87                | 19-Feb-18   | 19-Jun-18    | 30          |
